

www.ifrc.org
Saving lives,
changing minds.

Emergency appeal operations update Democratic People's Republic of Korea (DPRK) / North Hamgyong Province: Floods

 International Federation
of Red Cross and Red Crescent Societies

Emergency Appeal n° MDRKP008	Glide n° FL-2016-000097-PRK
Operation update n° 4: Issued on: 15 July 2017	Reporting period: 13 March 2017 to 31 May 2017
Date of disaster: 31 August 2016	DREF allocation: CHF 506,810
Operation start date: 2 September 2016	Operation end date: 31 December 2017 (16 months)
Overall operation budget: CHF 7,421,586	Appeal Coverage (current): CHF 4,620,284 (62%)
Number of people affected:	600,000 people
Number of people to be assisted:	330,000 people (82,500 households)
Host National Society presence:	Democratic People's Republic of Korea Red Cross Society (DPRK RCS)
Red Cross Red Crescent Movement partners actively involved in the operation:	International Federation of Red Cross and Red Crescent Societies (IFRC) and International Committee of the Red Cross (ICRC)
Other partner organizations actively involved in the operation:	The State Committee for Emergency and Disaster Management (SCEDM), UN Organizations, European Union Programme Support Units

Extension of operation timeframe: This operation update details the progress of the operation up to 31 May 2017, and extends the operation timeframe by four months to allow completion of activities for water, sanitation and hygiene (WASH) and health due to delays in procurement processes. The operation will now be completed by 31 December 2017, with the final report to be issued by 31 March 2018.

SUMMARY

The Emergency Appeal seeks **7,421,586 Swiss francs** to enable the **International Federation of Red Cross and Red Crescent Societies (IFRC)** to support the **Democratic People's Republic of Korea Red Cross Society (DPRK RCS)** in delivering assistance and support to **330,000 people** (82,500 households) affected by the floods for **16 months**.

The requirement for additional international staff as surge support has also been established and in the revised appeal there is a provision for one operation manager for three months, one WASH delegate for 12 months as well as two national staff for logistics and DRM.

APPEAL HISTORY

- **13 September 2016** – Emergency Plan of Action for allocation from the IFRC Disaster Relief Emergency Fund ([DREF](#)) launched to support 20,000 people for 6 months with CHF 506,810 to ensure that the immediate needs of flood-affected population are met through provision and replenishment of essential household and shelter items.
- **20 September 2016** – [Emergency Appeal](#) was launched to support 28,000 people for 12 months with provision of health and care, WASH, Shelter, essential household items distribution and replenishment, winterization and DRR /Capacity building assistance. The IFRC initially sought CHF 15,199,723 to support the operation.

- **23 September 2016** – [Operation Update No. 1](#) was made on September 23 that outlined the support details for immediate humanitarian needs of 28,000 people (7,000 families) in North Hamgyong Province, highlighting the programmes and services under this operation to directly support the affected communities across the Province.
- **27 October 2016** – [Operation Update No. 2](#) was published to reflect the progress on relief activities conducted by DPRK RCS and highlighted the lack of funds leading to numerous activities that could not be executed.
- **5 January 2017** – [Emergency Appeal Revision](#) was made to prioritize the activities based on immediate needs. The IFRC sought CHF 7,421,586 to support the 330,000 people for 12 months with provision of health and care, WASH, Shelter, essential household items distribution and subsequent replenishment, winterization and DRR /capacity building assistance.
- **27 April 2017** - [Operation Update No. 3](#) (six months report) was published to reflect the progress on relief and rehabilitation activities conducted by DPRK RCS during the first six months of the emergency appeal operation.

APPEAL COVERAGE

As of today, 62 per cent of the total appeal has been covered (see [donor response](#)) through contributions received from partners and donors. On behalf of the DPRK Red Cross Society, IFRC would like to thank all partners and donors for the generous contribution towards the appeal.

Partners and donors are encouraged to pledge support towards the remaining 38 per cent of the appeal gap as there are still unmet needs existing in the affected community.

A. SITUATION ANALYSIS

Description of the disaster

In late August 2016, heavy rainfall occurred in North Hamgyong Province of DPRK, causing massive flooding in Tumen River and its offshoots around the Chinese-DPRK border and other areas across the province. The flooding in North Hamgyong was described as the largest natural disaster in northern DPRK since 1945 and was declared a national emergency of highest priority.

One pulse of water flowed down the Tumen flood plain, creating a violent torrent of water that washed away people, buildings, gardens and crops. This situation was further aggravated due to Typhoon Lionrock which simultaneously hit the coast of North Hamgyong Province. The winds and increased sea levels caused by the typhoon prevented the flood waters pouring down the Tumen River from discharging into the East Sea. The water was effectively locked in the riverbed, resulting in widespread flash-flooding and inundation of surrounding cities, and towns across the North Hamgyong Province.

Since natural disasters are not common in this region of DPRK, despite the activation of early warning system, people were not prepared against floods.

According to the government official figures, 138 deaths were reported with 400 people missing and at least 667,715 people affected across all six counties in the province of North Hamgyong. Over 30,000 houses were damaged, submerged or completely destroyed resulting nearly 70,000 people displaced. Statistics on flood damages from the government on 6 February 2017 reports that around 3,187 buildings were completely damaged.

Emergency shelter and non-food items were identified as immediate needs of flood affected communities of North Hamgyong Province. Construction or rehabilitation of houses was also at priority keeping in view the extreme cold (-37) in winter.

The Government of DPRK (GoDPRK) requested the international community for their immediate support to provide emergency shelter, non-food items, rehabilitation of water supply system and support to provide

CGI sheets for rehabilitation or reconstruction of new houses. As a result, a well-coordinated operation was initiated, mobilizing the available stock instantly.


B. OVERVIEW OF HOST NATIONAL SOCIETY

DPRK RCS is present throughout the country with its provincial and county branches. The map displays the presence of DPRK RCS in the country.

Up to 1,782 Red Cross volunteers were mobilized to support efforts in early warning and evacuation, search and rescue, first aid, hygiene promotion, psychological support and distribution of emergency relief items to the affected people in close cooperation and coordination with the local authorities and other public organizations.

DPRK RCS branches in the affected counties activated their early warning systems, alerting the population of the upcoming rains, based on data provided by the national early warning mechanism. Their volunteers communicated emergency information and early warning messages and supported the evacuation, especially targeting the most vulnerable people. Flood victims were provided with First Aid services including injury treatment, patient transportation, and hygiene promotion for epidemic disease control was a priority activity delivered by the volunteers.

DPRK RCS Headquarters activated the flood contingency plan and established a Task Force to coordinate its response activities, convening a coordination meeting with the GoDPRK, IFRC and ICRC. National Disaster Response Team (NDRT) and IFRC members travel regularly to the affected areas for monitoring and assessment of the different sectors.

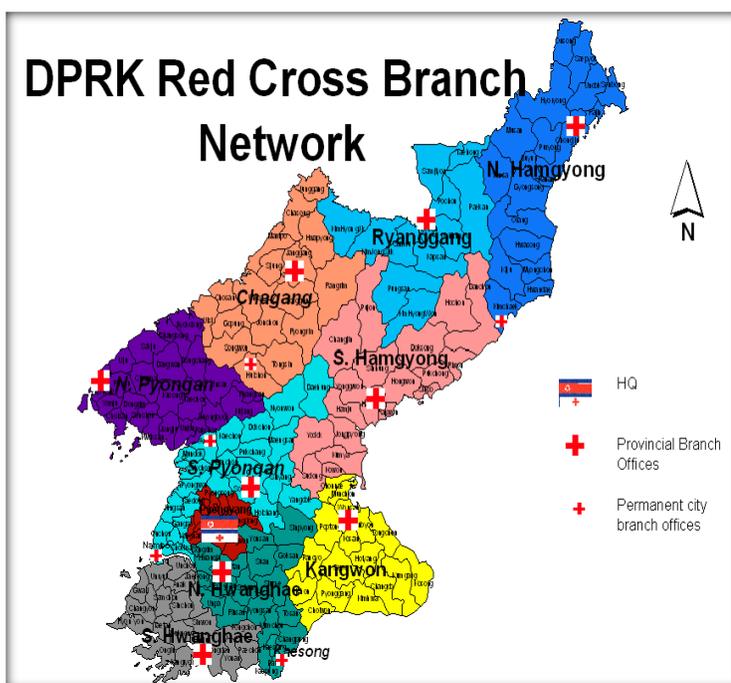

DPRK RCS presence in the country

As a leading humanitarian organization of the country, DPRK RCS launched an emergency response operation with support from the International Federation of Red Cross and Red Crescent Societies (IFRC) Country Office, and Partner National Societies (PNS) which supported multilaterally through the IFRC Emergency Appeal. In the early response phase, DPRK RCS reached over 7,000 households (28,000 people) with emergency shelter and essential non-food items (NFIs), which were mobilized from their warehouses in Hamhung City.

The distribution of NFIs for 7,000 families was coordinated by the local DPRK RCS branch in cooperation with GoDPRK authorities. The beneficiary selection focused on targeting support to the 7,000 most vulnerable including displaced and non-displaced families in Hoeryong City, Musan County, Onsong County, Kyongheun County, and Kyongwan County affected by the flood.

DPRK RCS has distributed additional NFIs along with 4.2 million additional water purification tablets to support 7,000 families with safe water for five months. Locally known “Winter Hygiene Kits¹” – 6,675 such kits have been procured and distributed.

C. OVERVIEW OF RED CROSS RED CRESCENT MOVEMENT IN COUNTRY

In DPRK, the Movement comprises DPRK RCS, IFRC and ICRC. While no PNS has a delegation in country, a number of PNS support the work of the DPRK RC technically and financially through a CAS-agreement.

Regular coordination meetings have been conducted between the DPRK RCS and the IFRC Country Office since the floods hit and have focused on the situation, guiding and coordinating the response. Technical meetings between the NDRT Coordination Team of DPRK RCS including Health, WASH, Disaster Management and OD Department and IFRC have been held regularly to discuss and coordinate operational issues and details.

The IFRC Secretary General visited DPRK from 29 August to 1 September 2016 and received firsthand information from DPRK RCS senior management about the floods as initial reports came to hand - he remains well informed of the evolving situation.

ICRC was quick to lend support to DPRK RCS in the health operation and is supporting the IFRC Emergency Appeal with a direct financial contribution of CHF 500,000 for shelter activities.

From 3 December until 13 December 2016, the President of the IFRC visited DPRK and spent three days travelling in Musan County and neighbouring Hoeryong City, both of which were badly affected by the floods. He witnessed ongoing reconstruction efforts and met with local people, DPRK Red Cross staff and volunteers and government officials. During his visit to DPRK, the IFRC President also met with senior officials of the DPRK RCS in Pyongyang and with government officials to discuss the wider humanitarian situation in the country.

A donor visit organized from 5 to 12 April to North Hamgyong province, which representatives from Netherlands RC, Canadian RC, Swedish RC and IFRC participated. The PNSs visited beneficiary households, health institutions, kindergartens and the DPRK RCS DP warehouses in Musan and Yonsa county, and Hoeryong City and Chongjin City.

D. OVERVIEW OF NON-RCRC ACTORS IN COUNTRY

The IFRC was invited to co-lead a joint GoDPRK and Humanitarian Country Team (HCT) assessment of flood-affected communities conducted from 6 to 9 September 2016. A total of 22 national and international staff from 13 organizations, including the DPRK RCS, participated in the mission. The assessment was coordinated by GoDPRK and the assessment report was released on 16 September.

Field teams from different organizations are visiting the affected areas regularly and sharing their experience and observations in the interagency meetings. Information about relief items distributed and other actions taken or planned were shared and coordinated amongst all HCT members. A series of Sector Working Groups (SWG) support the HCT activities, focusing on Food Security and Nutrition; Health; Shelter and NFIs; and WASH. IFRC chairs the Shelter and NFI SWG which was inaugurated only after the disaster was reported. In the Shelter working group meetings the procurement of CGI sheets as well as challenges/experiences in logistics are discussed and shared with all international stakeholders. The last meeting of the Shelter SWG took place in March 2017.

DPRK RCS maintains close coordination with national stakeholders, particularly the State Committee for Emergency and Disaster Management (SCEDM), enjoying a close and fruitful relationship with the SCEDM. In case of disasters, SCEDM is mandated as the GoDPRK lead agency.

¹ 25 Body Soap, 35 laundry Soap, 30 Sanitary pad, 20 toilet paper, 5 tooth paste

A HCT meeting was held on 13 March 2017 for the Emergency Response Plan for North Hamgyong Flood. Three suggested actions were discussed including a joint mission, a lesson learnt and a wrap up strategy. However, there is no progress information on these at the time of this update.

OPERATIONAL IMPLEMENTATION

Overview

The overall objective of the Emergency appeal is to ensure the humanitarian needs of up to 330,000 people in Hoeryong City, Musan County, Yonsa County, Onsong County, Kyonghung County and Kyongwon County in North Hamgyong Province affected by the floods are met in a timely, effective and efficient way.

The revised emergency appeal aims to strengthen DPRK RCS capacity in disaster management, particularly at the community, branch and provincial levels.

Summary of key achievements as of 31 May 2017

Sector	Achievements
Shelter and NFIs	<ul style="list-style-type: none"> 7,000 affected families (28,000 flood affected people) assisted with Non- Food Items to meet the immediate and medium term household, shelter and settlement needs. 1,688 people in Yonsa County provided with durable shelter solutions, with 422 housing units. 52,000 CGI sheets along with other roofing material procured for reconstruction of houses for affected communities.
WASH	<ul style="list-style-type: none"> 7,000 affected families assisted with water purification tablets for additional 5 months and 6,675 affected families assisted with winter hygiene kits to reduce the immediate risk of waterborne diseases in affected counties. 40 volunteers received specialized technical training to support their ongoing management and maintenance of water and sanitation facilities. 2,800 packages of IEC materials on hygiene promotion have been printed and distributed to health institutions and volunteers to deliver hygiene and other health promotions messages in the affected areas. 381 volunteers trained in hygiene promotion activities and have started delivering hygiene messages in the communities.
Health	<ul style="list-style-type: none"> 500 volunteers received two days First Aid Trainings that reduce the immediate and medium-term risks to health of affected populations. 300 volunteers trained in Health in Emergencies (HiE) 1,000 flipcharts and 1,000 manuals on first aid have been printed and distributed to trainers, volunteers and Red Cross youths.
Disaster Risk Reduction	<ul style="list-style-type: none"> 505 staff and volunteers received two days training on early warning and evacuation that enhanced the community's resilience towards disasters. 1,000 copies of community-based early warning and evacuation guidelines have been printed. 200 NDRT/PDRT members, branch staff and Red Cross volunteers equipped with emergency deployment kits. Eight (8) kits of early warning and evacuation materials procured and will be distributed to eight targeted flood affected communities in Hoeryong, Musan and Yonsa counties of North Hamgyong province. 40 trainers improved their knowledge and skills of the key components of disaster response with the focus on assessment, relief, distribution, monitoring and evaluation and reporting.

National Society Capacity Building	<ul style="list-style-type: none"> ▪ Disaster Preparedness Stock (NFI) for 7,000 families has been prepositioned to strengthen the National Society's level of preparedness for future disaster. ▪ 40 staff and volunteers received two days PMER training that enhance the National Society's level of HR preparedness to respond to future disaster. ▪ Red Cross Youth dissemination materials (musical instruments and visibility uniforms) were procured and distributed to 30 secondary schools in Hoeryong city, Musan county and Yonsa county of North Hamgyong province. ▪ Two Red Cross branches (North Hamgyong provincial and Musan county branches) were supported with office equipment and furniture to strengthen the organizational bases in the affected area. ▪ Volunteer management training was conducted for 60 branch staff and volunteer leaders from Hoeryong, Musan and Yonsa counties in North Hamgyong. ▪ Procurement of warehouse renovation material for Chongjin disaster preparedness (DP) warehouse is ongoing.
---	---

Currently DPRK RCS is focusing on rehabilitation of three water supply systems and utilization of remaining 42,000 CGI Sheets for reconstruction of new houses in North Hamgyong. In this regard, a team comprising the DM director and WASH officer of DPRK RCS is deployed regularly to North Hamgyong Province for coordination with Provincial government and monitoring of CGI sheets.

PROGRESS TOWARDS OUTCOME

The main objectives of the Emergency Appeal are organized under the following: health and care, water, sanitation and hygiene promotion, shelter and household, disaster risk reduction and national society's capacity building.

HEALTH & CARE

Outcome 1: The immediate and medium-term risks to the health of affected populations are reduced.			
Output			% of achievement:
Output 1.1: Target population is provided with rapid medical management of injuries and diseases.			70 %
Activities	Is implementation on time?		% progress (estimate)
	Yes (x)	No (x)	
Procure and distribute 500 first aid kits	X		40%
Procure and distribute 12,000 household first aid kits		X	45%
Conduct first aid and health in emergency (HiE) training for 500 trainers and volunteers	X		80%
Printing and distribution of 1,000 first aid manuals and 1,000 first aid flip charts to trainers, volunteers, Red Cross Youth and affected population		X	100%
Mobilize trained volunteers to provide community-based first aid, disease prevention and health promotion	X		90%

Progress towards outcomes:

There is limited funding allocated for Health in the Emergency Appeal so far, impacting on the progress in health activities being completed. Funding received for Health has enabled the implementation of the health activities which has commenced in January 2017, with procurement of health materials. The current progress in procurement of health resources is as follows:

Item Description	Quantity	Supplier	Status of requisition [Logistics requisition = LR] [Purchase order = PO]
FA kits for posts	200 units	GVA	LR sent to GVA
FA Backpack	200 units	GVA	LR sent to GVA
Printing of FA manual	500 copies	In country/ local	Finalized
Printing of FA flipchart	1000 copies	In country/ local	Finalized
Printing of Health message card for schools	500 copies	In country/ local	Finalized
Ri-hospital & Midwife kits	18 sets	GVA	LR sent to GVA
Solar heating systems	18 sets	In country	PO issued
Household FA kits	6,200 kits	In country	PO issued

As per IFRC standard procedures, procurement of First Aid (FA) Kits and FA Backpack will take six months and it will be completed in August 2017. Due to lengthy procurement procedures, implementation of health plan of action will not be completed in August 2017 as planned. **An extension of health programme to 31 December 2017 is required.** The long procurement process is a lesson learned for DPRK RCS and IFRC CO, that time required for procurement should be considered properly during the planning process.



Health in Emergency ToT in Chongjin city, North Hamgyong Province, May 2017. Photo: DPRK RCS

All together 500 volunteers from affected areas have been trained in First Aid that they can serve to their community in any emergency. These trained volunteers will be equipped with FA kit and FA backpack for delivering emergency services. A total of 200 FA Kits and 200 FA backpacks will be delivered in August 2017; in the meantime household local government doctors are supporting these trained volunteers by providing bandages and cotton to address FA emergencies in the affected community.

Health in emergency (HiE) training for both trainers and volunteers will be conducted in May and June, 2017 before the arrival of the rainy season. In all, 30 trainers and 470 volunteers from flood affected areas such as Hoeryong, Yonsa and Musan counties will participate in this training. The purpose of this training was to enhance the capacity of volunteers on health in disasters by equipping them with general knowledge about role of volunteers in emergency health and specific knowledge on epidemic control. The key topics of training covered types of disaster, health consequences caused by disaster, actions of volunteers before, during and after the disaster and principles and actions of epidemic prevention and control.



Volunteer conducting FA promotion in Yonsa county, North Hamgyong Province in May 2017.
Photo: DPRK RCS

Training of Trainers (ToT) was facilitated by health staff from the NHQ while Training of Volunteers (ToV) was facilitated by local trainers. A variety of training methods such as pre- and post-test, lecture, group discussion and presentation, role play and quiz, were applied in all the trainings to encourage interactive and participatory approach of participants for maximum impact of the training. Through the result of the pre- and post-test, the increase in knowledge levels of participants were recorded.

With the funding restraints, the initial plan of purchasing 12,000 household FA kits and 500 FA backpacks was revised in March. With the revised plan, the purchase of 6,200 household FA kits and 400 FA backpacks/FA kits are expected by the end of June and August respectively.

Output			% of achievement
Output 1.2: Health institutions are supported to continue providing appropriate health services in winter time.			8 %
Activities	Is implementation on time?		% progress (estimate)
	Yes (x)	No (x)	
Procure and distribute solar heating systems to 18 health institutions		x	50%
Procure and distribute ri hospital kits/midwife kits to 18 health institutions	x		50%

Progress towards outcome:

Eighteen (18) health institutions along with medical stocks were severely affected by the flood in North Hamgyong Province. DPRK RCS with the support of IFRC will equip the 18 health institution with midwife kits. The DPRK RCS will also install solar heating system in all 18 most affected health institutions.

Due to shortage of funds, procurement of Solar Heating Systems and their subsequent distribution were delayed. The Solar Heating Systems are under construction and expected to be completed by end of June.

The procurement process of **18 ri hospital kits/midwife kits** for 18 health institutions commenced mid-January 2017 through the international procurement processes. These 18 ri hospital kits/midwife kits will be delivered by end of August 2017 to DPRK and these kits will be distributed to selected 18 health institutions in September.

Output			% of achievement
Output 1.3: Community-based disease prevention and health promotion is provided to the target population.			100%
Activities	Is implementation on time?		% progress (estimate)
	Yes (x)	Yes (x)	
Mobilize RC youth to conduct health dissemination activities	X		100%

Progress towards outcome:

30 musical instrument kits² have been procured and distributed to 30 secondary schools in Musan, Hoeryong and Yonsa county; these musical instruments will be used for conducting the health dissemination activities by mobilizing the RC youth. By means of musical performance attention and interest of the community is ensured. Special songs, which require music instruments, with messages are performed around dissemination with use of flipcharts by trained RC youth members. The following key messages are disseminated through conducting the RC youth activities: -

- To prevent seasonal disease including diarrhoea and flu,
- First Aid for bleeding,
- First Aid for bone fracture
- Respiratory infection etc.

WATER, SANITATION, AND HYGIENE PROMOTION

Outcome 2: The immediate reduction in risk of waterborne and water related diseases in affected population			
Outputs			% of achievement
Output 2.1: Target population is provided with hygiene items which meet Sphere standards.			77 %
Activities	Is implementation on time?		% progress (estimate)
	Yes (x)	No (x)	
Distribution of hygiene kits and water purification tablets (WPT) to 7000 families.	X		100%
Procure and distribute winterized hygiene items ³ to 12,000 families for additional five (5) months.		X	53%

Progress towards outcome:

A final batch of 4,000 of winter hygiene kits is being procured. Delivery and distribution is expected to take place in June, this will bring the total number of winter hygiene kits distributed to 10,675. A little short of the planned 12,000, which is due to shortage of funds.

Output			% of achievement:
Output 2.2: Safe water and latrine solutions which meets Sphere and WHO standards are provided to target population as damaged systems are restored			67 %
Activities	Is implementation on time?		% progress (estimate)
	Yes (x)	No (x)	
Elaborate appropriate designs for water supply system and bill of quantities based on the detailed field survey		X	100%
Procure and deliver necessary construction materials (cement and reinforcement steel bar, pipes and fittings) to target communities		X	50 %

² 2 Guitars, 1 Drum set, 1 Audio & Hi-Fi Set, 5 microphones, 1 Accordion, 5 Korean Drum, 1 Trombone, 1 Trumpet, 20 T-Shirts, Uniform (Jacket & Trouser)

³ Consists of 25 body-soap, 35 laundry soap, 5 tooth paste, 30 sanitary pad, 20 toilet paper, 5 tooth brush

Conduct water and sanitation technical workshop for 30 volunteers on the construction, operation, and maintenance of water and sanitation facilities in the target communities	X		100%
Procure and distribute 5-month supply of WPTs to 7,000 families	X		100%
Install solar water heater in the kindergartens, children's nurseries and public bath for provision of warm water for hand washing and bath	X		10%
Monitor and evaluate the process of rehabilitation of water supply systems by DPRK Red Cross	X		10%
Procurement of spare parts for mobile water treatment units and replacement of one unit	X		100%

Progress towards outcome:

Rehabilitation of water supply

Cement, reinforcement steel bars and pumping equipment for the rehabilitation of the water source, pump station and reservoir tank have been procured locally. The materials were delivered to the communities in April, and construction is ongoing. The remaining materials, like pipes and fittings, are under procurement through international tender. Materials are expected to arrive by early July.

Seventeen (17) solar heaters will be installed at kindergartens, nurseries and public baths to provide the children and teachers warm water for personal hygiene, eight will be installed at Hoeryong City and nine at Musan County. The procurement is ongoing and it is expected that installation will be completed by end of August.

The DPRK RCS/IFRC WASH team is keeping close contact with the branches on the ground and arranges regular field monitoring during the implementation of activities. The field monitoring will not only focus on the progress of the activities but also on the wide collection of reflection and feedback from different groups of beneficiaries as well as from the branches in order to identify unmet or unexpected needs.

There will be a delay in implementation due to procurement process, and construction activities will continue till the end of October after harvest season.

One unit of EMWAT (emergency water) mobile water treatment unit and spare parts have been delivered to Pyongyang in May. The water treatment unit will be stored in the warehouse of DPRK RCS for future emergency operation.

Output			% progress (estimate)
Output 2.3: Hygiene promotion activities which meet Sphere standards provided to target population			84%
Activities	Is implementation on time?		% progress (estimate)
	Yes (x)	No (x)	
Conduct training on hygiene promotion for 500 volunteers		X	76%
Print and distribute 2,800 packages of IEC materials on hygiene promotion		X	100%
Mobilize volunteers for hygiene promotion activities	X		76%
Conduct surveys to determine the change in awareness and practices in communities reached		X	0%

Progress towards outcome:

Hygiene promotion training of trainers and volunteers have been arranged in May in Chongjin and Hoeryong city and Musan county. A total of 381 participants were trained on knowledge and skills for further arrangements of hygiene promotion activities in their respective communities. Further training of volunteers has been postponed to July due to onset of busy rice transplanting season in the communities.

Up to 2,800 packages of information, education and communication (IEC) materials for hygiene promotion have been printed and distributed to branches of Hoeryong , Musan, Yonsa, Kyongwon, Kyonghung and Onsong counties in May. These IEC materials will be utilized by Red Cross volunteers, health institutions, schools and kindergartens for hygiene promotion and education targeting community people and children.

Up to 28,000 people will be covered through hygiene promotion campaigns in Musan County, Yonsa County and Hoeryong City. DPRK RCS hygiene promotion trained volunteers will conduct the sessions. Hygiene promotion sessions cover causes, prevention and treatment of water borne diseases, proper hygiene practices including hand washing, personal and environmental hygiene etc.

SHELTER AND SETTLEMENTS**Outcome 3: The immediate and medium-term household, shelter and settlement needs of the target population are met.**

Outputs			% of achievement
Output 3.1: 7,000 families provided with essential household items.			100%
Activities	Is implementation on time?		% progress (estimate)
	Yes (x)	No (x)	
Distribution of emergency shelter ⁴ and household items ⁵ , including cooking set	X		100%

Progress towards outcome:

During the emergency phase DPRK RCS mobilized Non-Food Items (NFI) immediately from strategically located DP warehouses to respond to the situation efficiently.

After beneficiaries' selection and registration as per defined criteria, the distribution of 7,000 NFI has been completed in the affected areas in North Hamgyong Province. DPRK RCS trained staff and volunteers actively performed the registration and distribution process. The list of assisted beneficiaries has been compiled and filed for monitoring and audit requirements.

Output			% of achievement:
Output 3.2: Medium-term and durable shelter solutions that meet agreed standards are provided to target families.			60 %
Activities	Is implementation on time?		% progress (estimate)
	Yes (x)	No (x)	
Technical support from IFRC shelter expert	X		100%
Shelter activities	X		20%

⁴ tarpaulins (2 per family), shelter tool kits and tent (150 only)

⁵ Quilts (4 per family), jerry can, and hygiene kit and water purification tablets

Progress towards outcome:

The progress towards output 3.2 is the same as in operation update no.3 for this reporting period. To coordinate the second phase of reconstruction of houses/buildings, DPRK RCS / IFRC country office are coordinating with local authorities to monitor the use of CGI sheets . The second round of reconstruction is delaying as the focus of the governmental rehabilitation in North Hamgyong is on mitigation measures due to upcoming rainy season.

Output			% of achievement
Output 3.3: 7,000 families provided with shelter winterization materials			10%
Activities	Is implementation on time?		% progress (estimate)
	Yes (x)	No (x)	
Procure and distribute coal for cooking and heating		X	0%
Monitoring and logistics oversight		X	0%

Progress towards outcome:

Due to low funding response to the IFRC Emergency Appeal in the initial phase, it was not possible to allocate any un-earmarked funds to support these activities, with consideration to priorities on the ground and communication with the NS.

DISASTER RISK REDUCTION

Outcome 4: Communities are more resilient towards disasters			
Outputs			% of achievement
Output 4.1: Volunteers from the community are trained as first responders			58%
Activities	Is implementation on time?		% progress (estimate)
	Yes (x)	No (x)	
Conduct community based disaster response (Community Based Early Warning and Evacuation) training for 500 volunteers and community members	X		100%
Procure and distribute early warning materials	X		90%
Develop, prepare and train Provincial Disaster Response Team (PDRT), Branch Disaster Response Teams (BDRT) and Volunteers	X		8%
Conduct DRR mapping exercise and install identified disaster mitigation structures in the affected communities.		X	0%
Procure PDRT/NDRT/RC volunteer deployment kits	X		100%
Conduct DRR and disaster preparedness awareness raising activities	X		50%

Progress towards outcome:

A total of 505 participants (308 men and 197 women) including community Red Cross branch staff, volunteers, stakeholders and community people have been trained in two-days Community Based Early Warning and Evacuation trainings with simulation exercises in Hoeryong City, Musan and Yonsa County from March to May, 2017.

Eight sets of early warning and evacuation materials have been procured and will be distributed to targeted flood affected communities in Hoeryong, Musan and Yonsa county in the first week of June, 2017.



A two-days ToT, PDRT Relief skill training has been conducted in North Hamgyong province for 40 participants (35 men and 5 women). It provided an overview of the key components of disaster response with the focus on assessment, relief, distribution, reporting, monitoring and evaluation, and SPHERE⁶. After the flood operation midterm review conducted in February 2017 it was decided to increase the number of people trained in emergency response to improve the capacities in North Hamgyong to respond to future disasters. Therefore, additional emergency relief skill trainings targeting 460 branch staff, Red Cross volunteers and community people are planned in June and July, 2017. 200 NDRT/PDRT members, branch staff and Red Cross volunteers in the affected communities are fully equipped with emergency deployment kits to respond to future disasters. One deployment kit contains one sleeping bag, one sleeping mattress, one rechargeable flashlight, one rain suit, one Red Cross jacket and one backpack.



PDRT members and RC volunteers discussing damage and need assessment in emergency relief skill training in Chongjin city, North Hamgyong Province, 19 April 2017, DPRK. Photo: IFRC

Participatory Approach for Safe Shelter and Settlement Awareness (PASSA) training is planned in August 2017 targeting 500 community participants.

A thousand (1,000) copies of Community Based Early Warning and Evacuation (CBEWE) Guidelines have been printed and will be distributed to the affected communities to deliver lifesaving awareness messages in North Hamgyong Province. However, due to funding constraint, no funds have been allocated for mitigation measures.

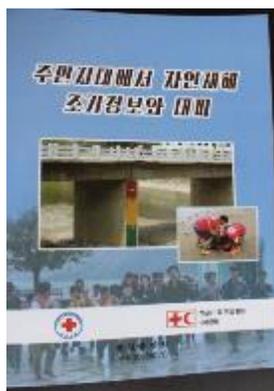

Community Based Early Warning and Evacuation Guidelines printed (front cover page on the left, back cover page in the middle and CBEWE CD on the right. Photo: IFRC DPRK

⁶ Humanitarian Charter and Minimum Standards in Humanitarian Response ([SPHERE](#))

NATIONAL SOCIETY CAPACITY BUILDING

Outcome 5: National Society level of preparedness for future disasters and capacity to deliver sustainable programming and services is strengthened.

Outputs			% of achievement
Output 5.1: Increased material and HR capacity is available for the National Society to respond to future disasters, deliver programs and services.			40%
Activities	Is implementation on time?		% progress (estimate)
	Yes (x)	No (x)	
Replenishment of family tents, jerry cans, tarpaulins, shelter tool kits, blue quilts and cooking hygiene kits and WPTs	X		80%
Final inspection on the replenished items	X		70%
Provide essential equipment and vehicles for North Hamgyong flood operation		X	30%
Recruit staff to support the North Hamgyong flood operation		X	0%

Progress towards outcome:

NFIs from DP warehouse were distributed to 7,000 flood affected families. Those distributed items are being replenished under this Emergency Appeal with the following status:

No	Item	Quantity to be replenished	Replenished to-date	In process	In kind donation	Comments
1	Quilts	28,000	19,500		8,500	8,500 will be delivered by Finnish RC by mid of June.
2	Cooking Sets	7,000	7,000	0	0	Completed
3	Tarpaulin Sheets	14,000	14,000	0	0	Completed
4	Hygiene Kits	7,000	7,000	0	0	Completed
5	Jerry Cans	7,000			7,000	Completed
6	Shelter Tool Kit	1,500	0	0	0	Completed
7	Tents	150			150	Tender process ongoing

Construction materials for the repair of one DP warehouse in Chongjin city, North Hamgyong has been delivered in June 2017.

Local branched were equipped with new materials and the procurement process for two land cruisers and one truck is ongoing.

No additional staff has been recruited to support the North Hamgyong flood operation activities.

Output			% of achievement
Output 5.2: Increased skill sets available for the National Society to respond to future disasters and deliver programmes and services			100 %
Activities	Is implementation on time?		% progress (estimate)
	Yes (X)	No (X)	
Provide training to branch staff and community leaders on planning, monitoring, evaluation and reporting	X		100%

Progress towards outcome:

Red Cross Youth dissemination materials (musical instruments and visibility uniforms) were procured and distributed to 30 secondary schools in Hoeryong city, Musan and Yonsa. These schools organized the Red Cross (RC) youth dissemination teams and promoted the RC messages on hygiene, first aid, health and disaster risk reduction through art performances. With the materials provided, the RC youth dissemination teams conducted various dissemination activities with the topics of first aid, hygiene, health care, safe water, tree planting and other RC messages reaching approximately 28,000 community people.

As additional support to the RC branches, North Hamgyong provincial and Musan county branches were supported with office equipment and furniture to strengthen the organizational basis in these areas.

The volunteer management training for North Hamgyong and three counties were conducted for 60 branches' staff and volunteer leaders in May 2017. The training contributed to the improvement of understanding on volunteer management cycle and the skills for recruiting, retention of volunteers, mobilizing, monitoring and reporting on volunteers' activities. To increase the number of registered volunteers in the North Hamgyong provincial branch additional training of 100 new volunteers is planned. Furthermore, additional volunteer visibility will be procured.

The organizational development (OD) intervention is limited to the three most affected counties and the provincial branch, due to limited resources. Traditional disaster risk reduction was not included in the RC training package for volunteer management, only FA, hygiene and other health related topics are covered. Considering the current trend of increased natural disasters in these areas, DPRK RCS HQ is planning to update the volunteer management manual with inserting the DRR concept in the package and disseminate it to all the branches and volunteers in North Hamgyong province.

Outcome 6: Continuous and detailed assessment and analysis is used to inform the design and implementation of the operation.

Outputs			% of achievement
Output 6.1: Management of the operation is informed by continuous assessments and a comprehensive monitoring and evaluation system			75%
Activities	Is implementation on time?		% progress (estimate)
	Yes (x)	No (x)	
Monitoring field visits by joint teams of DPRK RCS headquarters and IFRC	X		50%
Review workshops	X		50%

Progress towards outcome

Since the beginning of the operation, regular monitoring visits were conducted by different IFRC and DPRK RCS sector experts including WASH, shelter, health and DM analysing their respective activities. Those visits will continue until the end of the operation.

OPERATIONAL SUPPORT SERVICES

Human resources

One IFRC shelter advisor was deployed on 26 September 2016 for a short-term mission to give technical support for the shelter activities. Furthermore, the shelter advisor led the shelter working group in the international community and supports as well the winterization discussions.

One emergency operations manager was selected from regional disaster response team (RDRT) roster and was deployed on 30 January 2017 for three months to support the operation. One WASH delegate has also been appointed for one year from January 2017.

Two national staff positions have been provided to IFRC country office to ensure sufficient capacity to address increased activities in logistics and EA activity implementation.

Logistics and supply chain

Logistics activities aim to effectively manage the supply chain, including procurement, customs clearance, fleet, storage and transport to distribution sites in accordance with the operation's requirements and aligned to IFRC's logistics standards, processes and procedures.

The IFRC country office in DPRK, in coordination with the DPRK RCS, has conducted local procurement of 6,675 winter hygiene kits, 1,500 shelter tool kits and 7,000 kitchen sets taking in to account of context specific specification from DPRK RCS to ensure local and cultural contextual aspects. 7,000 hygiene kits, Health and WASH material is also being procured locally.

IFRC's Asia Pacific regional logistic unit (RLU) in Kuala Lumpur already dispatched the tarpaulins to replenish the in-country stocks distributed during the immediate relief phase. 52,200 CGI sheets and additional 5 million WPT had procured by RLU and delivered at DPRK in November 2017. Emergency WASH equipment including spares were procured by and delivered in May. The procurement of pipes and fittings for the rehabilitation of water supply is ongoing, and is expected to be completed by mid-July. Further Finnish Red Cross in close coordination with RLU is in process of procuring and dispatching remaining NFIs to replenish in-country stocks.

FA Kits, FA Backpack and ri / community hospital/midwife kits are under procurement process by the IFRC Geneva logistics management department.

Existing IFRC in-country Logistics staff, in coordination with IFRC DRM delegate, facilitates the in-country transportation and warehousing activities. KL RLU is maintaining close coordination with the IFRC country office and the DPRK RCS in regards to supply and technical support.

Information technologies (IT)

DPRK RCS and IFRC country office will be supported with four Laptops which are being procured. Communication cost of North Hamgyong branch for distribution of relief and NFI and associated logistics, monitoring and evaluation, reporting and communications activities have been covered under emergency appeal. A mobile internet device that allows delegates to have access to the internet outside Pyongyang has been procured that ensured good communication from the field.

Communications

Since the floods first struck, proactive media relations have resulted in extensive coverage for the IFRC / DPRK Red Cross response in the international media. Three press releases have been issued which have been picked up widely by newswires including AP, Reuters and AFP as well as mainstream media. The IFRC's head of delegation has given numerous interviews with international broadcasters including BBC, CNN and Al Jazeera. Coverage of the Red Cross operation was boosted considerably when IFRC was able to release video footage from a field mission to Musan County and Hoeryong City on 30 September 2016.

This was the first independent video material to be shared and it was broadcast by numerous media outlets. Over the course of September IFRC media relations efforts resulted in 2,806 mentions in traditional media and social media.

In October, the IFRC produced a variety of new communications materials aimed at positioning the response operation with key stakeholders and boosting fundraising efforts. These include a [reactive Q&A](#) , new [Key Messages and Talking Points](#). A range of new audio-visual materials are also available. New [video](#) material can be found in the IFRC's video newsroom and a short 40 second [video](#) has been produced that is available on the IFRC's YouTube page. New [photos](#) have been added to the IFRC's image library and a [photo-gallery](#) has been posted on ifrc.org. A Shorthand Social [multimedia](#) has also been produced on the Red Cross response to the floods.

Security

The IFRC delegation is security compliant, has standard security procedures in place and the international delegates and local staff are familiar with the security procedures. The DPRK RCS has easy access to the affected areas and enjoys excellent levels of cooperation with GoDPRK relevant authorities. Standard security measures such as fire extinguishers, fire management and evacuation plans are maintained in DPRK RCS warehouses

Planning, monitoring, evaluation and reporting (PMER)

Both DPRK RCS and the IFRC country office have well-functioning PMER to support the development of reports, updates and communication materials as necessary. Reporting on the operation is carried out in accordance with the IFRC Emergency Appeal minimum reporting standards. Three operation updates to cover the first seven months of the appeal launch have been issued. A final report will be issued within three months of the operation end date.

Administration and Finance

The IFRC delegation Finance and Administration (FAD) unit will oversee procurement, quality control of NFIs, and all financial matters and reports. The FAD unit, in coordination with IFRC Asia Pacific regional finance and logistics units, will extend support and guidance to the DPRK RCS logistics department in the replenishment of NFIs.

Reference documents



Click here for:
Previous [plans and reports](#)

[Revised emergency appeal](#)

[Financial report as at 31 May 2017](#)

Return to [title page](#)

Contact Information

For further information specifically related to this operation please contact:

Democratic People's Republic of Korea Red Cross Society (DPRK RCS)

- Kim Jong Ho, DM director, phone: +850 2 4350, email: dprk-rc@star-co.net.kp

IFRC DPRK country office, Pyongyang

- Chris Staines, head of country office; phone: +850 2 381 4350; +850 191 250 1149; email: chris.staines@ifrc.org
- Marlene Fiedler, DRM delegate, phone: +850 191 250 7921, email: marlene.fiedler@ifrc.org

IFRC regional office for Asia Pacific, Kuala Lumpur

- Martin Faller, deputy director; email: martin.faller@ifrc.org
- Alice Ho, operations coordinator; mobile: +60 13 360 0366; email: alice.ho@ifrc.org
- Pierre Kremer, partnerships and resource development coordinator; email: pierre.kremer@ifrc.org

For in-kind donations and mobilization table support:

- Riku Assamaki, regional logistics coordinator; mobile: +6012 298 9752; email: riku.assamaki@ifrc.org

For performance and accountability support (planning, monitoring, evaluation and reporting enquiries)

- Kit Roche, acting PMER manager; email: kit.roche@ifrc.org

IFRC Geneva

- Cristina Estrada, response and recovery lead; phone: +412 2730 4260; email: cristina.estrada@ifrc.org
- Susil Perera, senior officer, response and recovery; phone: +412 2730 4947; email: susil.perera@ifrc.org

How we work

All IFRC assistance seeks to adhere to the **Code of Conduct** for the International Red Cross and Red Crescent Movement and Non-Governmental Organizations (NGO's) in Disaster Relief and the **Humanitarian Charter and Minimum Standards in Humanitarian Response (Sphere)** in delivering assistance to the most vulnerable. The IFRC's vision is to inspire, **encourage, facilitate and promote at all times all forms of humanitarian activities** by National Societies, with a view to **preventing and alleviating human suffering**, and thereby contributing to the maintenance and promotion of human dignity and peace in the world.

The IFRC's work is guided by Strategy 2020 which puts forward three strategic aims:



Save lives.
protect livelihoods,
and strengthen recovery
from disaster and crises.



Enable **healthy**
and **safe** living.



Promote **social inclusion**
and a culture of
non-violence and **peace**.

Disaster Response Financial Report

MDRKP008 - DPR Korea - Floods

Timeframe: 12 Sep 16 to 31 Aug 17

Appeal Launch Date: 20 Sep 16

Interim Report

Selected Parameters

Reporting Timeframe	2016/9-2017/5	Programme	MDRKP008
Budget Timeframe	2016/9-2017/8	Budget	APPROVED
Split by funding source	Y	Project	*
Subsector:	*		

All figures are in Swiss Francs (CHF)

I. Funding

	Raise humanitarian standards	Grow RC/RC services for vulnerable people	Strengthen RC/RC contribution to development	Heighten influence and support for RC/RC work	Joint working and accountability	TOTAL	Deferred Income
A. Budget		4,819,471	2,602,115			7,421,586	
B. Opening Balance							
Income							
Cash contributions							
<i>Austrian Red Cross</i>			10,864			10,864	
<i>Austrian Red Cross (from Austrian Government*)</i>		52,417				52,417	
<i>British Red Cross</i>		120,344	122,501			242,846	
<i>Bulgarian Red Cross</i>		1,096				1,096	
<i>China Red Cross, Hong Kong branch</i>			25,405			25,405	
<i>China Red Cross, Macau Branch</i>			15,000			15,000	
<i>Czech Red Cross (from Czech private donors*)</i>		7,829				7,829	
<i>Danish Red Cross (from Danish Government*)</i>		100,000				100,000	
<i>Finnish Red Cross</i>		64,761				64,761	
<i>Finnish Red Cross (from European Commission - DG ECHO*)</i>		132,522				132,522	
<i>Finnish Red Cross (from Finnish Government*)</i>			275,817			275,817	
<i>German Red Cross</i>		107,248				107,248	
<i>ICRC</i>		500,000				500,000	
<i>Japanese Red Cross Society</i>		94,080	87,625			181,705	
<i>KNCKK:Korea NGO Council for Coop.with N.Korea</i>		184,227				184,227	
<i>Malaysian Government</i>		20,543				20,543	
<i>Movement of One Korea</i>		20,220	80,879			101,099	
<i>National YWCA of Korea</i>		9,932				9,932	
<i>New Zealand Red Cross</i>		13,704				13,704	
<i>Norwegian Red Cross</i>		179,048				179,048	
<i>Red Crescent Society of the Islamic Republic of Iran</i>		10,000				10,000	
<i>Red Cross of Monaco</i>		32,566				32,566	
<i>Spanish Red Cross</i>		21,432				21,432	
<i>Swedish Red Cross</i>		291,442	154,290			445,733	
<i>Swiss Red Cross</i>		14,000				14,000	
<i>Swiss Red Cross (from Swiss Government*)</i>		186,000				186,000	
<i>Thai Government</i>		29,119				29,119	
<i>The Canadian Red Cross Society</i>		73,953				73,953	
<i>The Netherlands Red Cross (from Netherlands Government*)</i>		321,061	749,143			1,070,204	
<i>The Republic of Korea National Red Cross</i>		100,000	188,385			288,385	
<i>VERF/WHO Voluntary Emergency Relief</i>		1,000				1,000	
C1. Cash contributions		2,688,543	1,709,910			4,398,453	
Inkind Personnel							
<i>The Netherlands Red Cross</i>			37,265			37,265	
C3. Inkind Personnel			37,265			37,265	
C. Total Income = SUM(C1..C4)		2,688,543	1,747,174			4,435,717	
D. Total Funding = B + C		2,688,543	1,747,174			4,435,717	

* Funding source data based on information provided by the donor

II. Movement of Funds

	Raise humanitarian standards	Grow RC/RC services for vulnerable people	Strengthen RC/RC contribution to development	Heighten influence and support for RC/RC work	Joint working and accountability	TOTAL	Deferred Income
B. Opening Balance							
C. Income		2,688,543	1,747,174			4,435,717	
E. Expenditure		-2,222,309	-716,186			-2,938,496	
F. Closing Balance = (B + C + E)		466,234	1,030,988			1,497,222	

Disaster Response Financial Report

MDRKP008 - DPR Korea - Floods

Timeframe: 12 Sep 16 to 31 Aug 17

Appeal Launch Date: 20 Sep 16

Interim Report

Selected Parameters

Reporting Timeframe	2016/9-2017/5	Programme	MDRKP008
Budget Timeframe	2016/9-2017/8	Budget	APPROVED
Split by funding source	Y	Project	*
Subsector:	*		

All figures are in Swiss Francs (CHF)

III. Expenditure

Account Groups	Budget	Expenditure					TOTAL	Variance
		Raise humanitarian standards	Grow RC/RC services for vulnerable people	Strengthen RC/RC contribution to development	Heighten influence and support for RC/RC work	Joint working and accountability		
A						B	A - B	
BUDGET (C)			4,819,471	2,602,115			7,421,586	
Relief items, Construction, Supplies								
Shelter - Relief	1,269,000		1,096,306	54,000			1,150,306	118,694
Construction Materials	174,000							174,000
Clothing & Textiles	406,000		271,731				271,731	134,269
Water, Sanitation & Hygiene	1,390,900		67,548	293,950			361,497	1,029,403
Medical & First Aid	629,000							629,000
Teaching Materials	121,000			107,199			107,199	13,802
Utensils & Tools	171,500		113,779				113,779	57,721
Other Supplies & Services	1,200,000							1,200,000
Total Relief items, Construction, Sup	5,361,400		1,549,363	455,148			2,004,511	3,356,889
Land, vehicles & equipment								
Vehicles	224,000							224,000
Computers & Telecom			827				827	-827
Total Land, vehicles & equipment	224,000		827				827	223,173
Logistics, Transport & Storage								
Storage			15,902	206			16,109	-16,109
Distribution & Monitoring	129,080		35,898	6,053			41,951	87,129
Transport & Vehicles Costs	50,000		27,101	1,813			28,913	21,087
Logistics Services	50,000		82,916	3,276			86,192	-36,192
Total Logistics, Transport & Storage	229,080		161,817	11,347			173,164	55,916
Personnel								
International Staff	95,000		40,754	55,454			96,208	-1,208
National Staff	12,000		14,564	1,309			15,874	-3,874
National Society Staff	202,105		16,342	8,633			24,975	177,130
Volunteers	152,000							152,000
Other Staff Benefits			47,829				47,829	-47,829
Total Personnel	461,105		119,489	65,396			184,885	276,220
Workshops & Training								
Workshops & Training	212,900		61,168	60,918			122,086	90,814
Total Workshops & Training	212,900		61,168	60,918			122,086	90,814
General Expenditure								
Travel	220,140		35,150	4,922			40,073	180,067
Information & Public Relations	210,000		41,762	53,000			94,763	115,237
Office Costs	10,000		5,264				5,264	4,736
Communications	20,000		4,825	554			5,379	14,621
Financial Charges			42,054	2,291			44,346	-44,346
Other General Expenses			0				0	0
Shared Office and Services Costs	20,000		50,586	14,430			65,016	-45,016
Total General Expenditure	480,140		179,642	75,198			254,841	225,299
Operational Provisions								
Operational Provisions				3,281			3,281	-3,281
Total Operational Provisions				3,281			3,281	-3,281
Indirect Costs								
Programme & Services Support Recover	452,961		134,700	41,212			175,912	277,049
Total Indirect Costs	452,961		134,700	41,212			175,912	277,049
Pledge Specific Costs								
Pledge Earmarking Fee			13,096	3,093			16,189	-16,189

Disaster Response Financial Report

MDRKP008 - DPR Korea - Floods

Timeframe: 12 Sep 16 to 31 Aug 17

Appeal Launch Date: 20 Sep 16

Interim Report

Selected Parameters

Reporting Timeframe	2016/9-2017/5	Programme	MDRKP008
Budget Timeframe	2016/9-2017/8	Budget	APPROVED
Split by funding source	Y	Project	*
Subsector:	*		

All figures are in Swiss Francs (CHF)

III. Expenditure

Account Groups	Budget	Expenditure					TOTAL	Variance
		Raise humanitarian standards	Grow RC/RC services for vulnerable people	Strengthen RC/RC contribution to development	Heighten influence and support for RC/RC work	Joint working and accountability		
	A					B	A - B	
BUDGET (C)			4,819,471	2,602,115		7,421,586		
Pledge Reporting Fees			2,208	592		2,800	-2,800	
Total Pledge Specific Costs			15,303	3,685		18,989	-18,989	
TOTAL EXPENDITURE (D)	7,421,586		2,222,309	716,186		2,938,496	4,483,090	
VARIANCE (C - D)			2,597,162	1,885,928		4,483,090		

Disaster Response Financial Report

MDRKP008 - DPR Korea - Floods

Timeframe: 12 Sep 16 to 31 Aug 17

Appeal Launch Date: 20 Sep 16

Interim Report

Selected Parameters

Reporting Timeframe	2016/9-2017/5	Programme	MDRKP008
Budget Timeframe	2016/9-2017/8	Budget	APPROVED
Split by funding source	Y	Project	*
Subsector:	*		

All figures are in Swiss Francs (CHF)

IV. Breakdown by subsector

Business Line / Sub-sector	Budget	Opening Balance	Income	Funding	Expenditure	Closing Balance	Deferred Income
BL2 - Grow RC/RC services for vulnerable people							
Disaster management	2,042,641		1,158,523	1,158,523	857,642	300,881	
Shelter	2,776,831		1,530,020	1,530,020	1,364,667	165,353	
Subtotal BL2	4,819,471		2,688,543	2,688,543	2,222,309	466,234	
BL3 - Strengthen RC/RC contribution to development							
Water and sanitation	2,602,115		1,747,174	1,747,174	716,186	1,030,988	
Subtotal BL3	2,602,115		1,747,174	1,747,174	716,186	1,030,988	
GRAND TOTAL	7,421,586		4,435,717	4,435,717	2,938,496	1,497,222	
