

www.ifrc.org
Saving lives,
changing minds.

Emergency Appeal Operations Update

Dominican Republic: Floods



Emergency Appeal 6-month operation update: MDRDO009	Glide no. FL-2016-000123-DOM
Date of issue: 03 October 2017	Date of disaster: 10 November 2016
Operation manager (responsible for this PoA): Priyadarshni Rai, IFRC community resilience delegate	Point of contact: Gustavo Lara – Executive Director Dominican Red Cross (DRC)
Operation start date: 24 November 2016	Expected timeframe: 12 months (the operation end date is 26 November 2017)
Overall operation budget: 2,459,751 Swiss Francs (CHF)	
Number of people affected: 1,792,000 people (based on population figures from the 2010 census)	Number of families to be assisted: 4,000 families (20,000 people)
Host National Society Presence (no. of volunteers, staff, branches): The Dominican Red Cross has 1 national headquarters, 175 branches and 20,000 volunteers	
Red Cross Red Crescent Movement partners actively involved in the operation: International Federation of Red Cross and Red Crescent Societies (IFRC), International Committee of the Red Cross (ICRC), Haiti Country Cluster Office, Pan American Disaster Response Unit (PADRU). The only Partner National Society present in the country is the Spanish Red Cross, who has offered their support if required. Support is also being provided through the Canadian Red Cross Society's Capacity Building for Emergency Response in the Americas (CERA) project, which is co-funded by the Canadian government.	
Other partner organisations actively involved in the operation: Ministry of Health, Ministry of Education, Ministry of Housing (INVI), National Emergency Operations Centre (NEOC) Ministry of Public Works, Ministry of Defence, United Nations Office for the Coordination of Humanitarian Affairs (UN-OCHA), National Emergency Commission, Presidency of the Republic, National Institute of Water and Sanitation (INAPA), Oxfam, World Vision.	
Summary of changes to the plan of action:	
<p>Change in the number of families to be assisted</p> <p>The emergency appeal's original objective was to provide humanitarian assistance to 5,000 families affected by the flooding in the provinces of Puerto Plata, Espaillat, Duarte, María Trinidad Sánchez, Montecristi, and Santiago. However, due to the appeal's low coverage, the number of families to be assisted was reduced to 2,500 families, who were subsequently selected and supported. In May 2017, additional flooding occurred in the southern part of the Dominican Republic, mainly in the provinces of San Cristobal, Barahona, and Santo Domingo. Consequently, an additional 1,500 families in the newly affected provinces were included in the total number of people to be assisted by this operation, bringing it to 4,000 targeted families. The 4,000 families will receive support through health, water, sanitation, and hygiene promotion, shelter, communications, and disaster risk reduction activities.</p>	
<p>Inclusion of a new activity</p> <p>The <i>Cleaning and disinfection of 64 wells activity</i> was added to the emergency plan of action.</p>	
*Please note that despite the increase in the number of families to be assisted and the inclusion of a new activity, the budget remained the same.	

< [Click here](#) for the interim appeal budget report. [Click here](#) for the contact information. >

Summary: After the passage of Hurricane Matthew over the island of Hispaniola, the Dominican Republic was affected by a series of hydro-meteorological events, which especially impacted the area of Central Cibao and the northern part of the country. The Dominican Red Cross Society began its relief operations to assist the population with its own resources (please see the [Annex 1](#) for links to articles on the operation).

A total of 3,723 families (18,615 persons) have been directly reached by the emergency humanitarian assistance actions of the Dominican Red Cross. Main actions in the 10 prioritized provinces include the distribution of the following relief items:



FA DRC volunteer delivers food to a beneficiary in Bajo Yuna. Source: DRC

General summary of assistance provided to 4,000 families in the past 6 months

DISTRIBUTION AND COVERAGE PER PROVINCE				
PROVINCE	FAMILIES REACHED	PEOPLE	ITEMS	DISTRIBUTION
PUERTO PLATA	74	370	Hygiene kits	Closed
ESPAILLAT	400	2,000	Hygiene kits, long-lasting insecticide treated [mosquito] nets (LLITNs) and repellent	Closed
DUARTE	691	3,455	Shelter kits, tarpaulins and buckets with spigots	Closed
MARIA TRINIDAD SANCHEZ	250	1,250	Hygiene kits, tool kits (kit includes two tarpaulins per family)	Closed
MONTECRISTI	487	2,435	Hygiene kits, mosquito nets, jerrycans and repellents	Closed
SANTIAGO DE LOS CABALLEROS	550	2,750	Hygiene kits, LLITNs, jerry cans, repellent, shelter kits (includes two tarpaulins per family)	Closed
SUBTOTAL	2,452	12,260	Based on 2,500 family goal, 98% reached	
SAN CRISTOBAL	350	1,750	Jerrycans	Closed
BARAHONA	921	4,605	Shelter kits, tarpaulins and buckets with spigots	Closed
SUBTOTAL	1,271	6,355	Based on 1,500 family goal, 85% reached	
TOTAL	3,723	18,615	Based on 4,000 family goal, 93% reached	

Moreover, the Dominican Red Cross (DRC) has distributed over 1,202,040 litres of water to Cambita and San Cristobal, and the DRC provided support to the distributions through the placement of water reservoirs (*tinacos*) in these cities, benefiting 801 families (4,005 people) over a 20-day period. Home disinfection and well cleaning actions also took place, mainly in the provinces of Sabaneta de Yasica, Puerto Plata Gaspar Hernández and Espaillat; this operational component was disrupted several times and could not be completed as planned due to incessant rainfall in the area.

Within the National Society Capacity Building sector, volunteers have received training in the following areas: Open Data Kit (ODK) and Mega V (16), Induction to Mega V (10), Hygiene Habits, Beneficiary Selection and Accountability (14 volunteers), and Community Based Health and First Aid (CBHFA) for Volunteers (92).

See [Annexes](#) for further information.

Coordination and partnerships

The Dominican Red Cross has maintained permanent communication with the Ministry of Health. In times of emergency, the National Society supports the actions of the Ministry through its branches.

A multidisciplinary team at the National Society headquarters coordinates and advises some 12,000 volunteers from branches located in affected areas who actively participating in response to floods, and work in coordination with water specialists, sanitation and hygiene promotion specialists, psychosocial support, first aid, damage and needs assessment, well cleaning, shelter management and logistics staff.

The provinces of Montecristi, Puerto Plata, Santiago de los Caballeros, Espaillat, María Trinidad Sánchez and Duarte, through Red Cross branches located in Palo Verde, Santiago, Sabaneta de Yasica, Gaspar Hernández, Moca, Nagua, Arenoso, Villa Riva, San Francisco de Macorís, among others, have been instrumental in the provision of assistance to the affected communities. Red Cross actions have expanded to the provinces of Barahona, San Cristóbal and Santo Domingo through branches in San Cristóbal, Cambita, Villa Altagracia, Polo, Enriquillo and Paraíso among others.

The IFRC deployed a Regional Intervention Team (RIT) member for reporting and Dashboard tasks and a RIT in information management for two months to support the implementation of activities, appeal coordination and the use of the Open Data Kit) and MEGA V tools during the operation through the following workshops:

<i>Date</i>	<i>Level</i>	<i>No. of volunteers</i>
<i>4 to 6 April 2017</i>	<i>National</i>	<i>16</i>
<i>27 January 2017</i>	<i>Santiago</i>	<i>10</i>
TOTAL		26

Finally, the IFRC's regional office for the Americas (ARO) has provided support to the National Society through specialists in water and sanitation, general coordination from its Panama office and the country cluster office in Haiti.

C. DETAILED PROGRESS ON OPERATIONAL PLAN

Health

Outcome 1: Reduce the risk of adverse effects on the mental health of at least 1,500 affected families in the districts affected by the floods.	Outputs		% reached	
			N° of families	Global ¹
	Output 1.1: The families and humanitarian aid personnel affected by the floods receive emotional support		345 families	23%
Activities	On time?		Amount	% progress
	Yes	No		
Coordination of meetings and workshops; presentation of actions and planning; DRC–Ministry of Health (MINSA)	Yes			60%
Community psychosocial support (PSS) training for volunteers	Yes		22 volunteers trained	100%
Purchase, design and printing of materials	Yes			50%
PSS workshops for the affected population (community leaders, focal points)		No		0%
Develop a referral system to ensure the provision of clinical care to people that require specialized support, in coordination with the health authorities	Yes			100%
Conduct briefings and debriefings with volunteers		No	4 briefings and debriefings (1 per province)	67%
Carry out group actions with volunteers to reduce the risk of adverse effects from this event on their mental health		No		0%
Achievements to date				

¹ The global percentage is based on the total number of families that the DRC expects to reach in each sector. For example, the global percentage for the health sector is based on 1,500 families.

During all relief and humanitarian assistance actions, National Society volunteers provided emotional assistance directly; however, the branches did not formally register these emotional support actions.

Coordination of meetings and workshops; presentation of actions and planning; DRC- MINSa

The Dominican Red Cross has maintained permanent communication with the Ministry of Health; during awareness raising and epidemiological control actions, the provincial health coordinators were in permanent contact with the provincial health directorates. Joint actions were carried out in vector control, epidemiological follow-up as well as emergency first aid care, and DRC branches received instructions and coordinated with the provincial offices.



A DRC PSS team works with children from the affected zones in Villa Rivas.
Source: DRC

Community PSS training for volunteers

The funds for the Hygiene Promotion for Volunteers and the Community PSS for Volunteers were combined to carry out the National CBHFA Workshop since its programme contained both components. The DRC achieved the goal of training 22 volunteers; at the onset of the rainfall, these trained volunteers were able to support 70 volunteers from the branches of Arenoso, Nagua, Villa Rivas, Cambita and San Cristóbal.

Purchase, design and printing of materials

Work has begun with materials that the National Society already had in stock (brochures and posters with the IFRC, National Society and the Ministry of Health logos); these materials will be replenished.

PSS workshops for the affected population (community leaders, focal points)

Community PSS activities for focal points and community leaders (aimed at achieving a multiplier effect at the community level and support network creation) were not carried out in the early phases of the operation since the National Society did not have any formally trained staff at that time; this activity still has not been carried out due to lack of sufficient resources, and it has been rescheduled for September/October 2017.

Develop a referral system to ensure the provision of clinical care to people that require specialized support, in coordination with the health authorities

The Ministry of Health has a referral system to ensure clinical care for people who require specialized support. The Dominican Red Cross works together with the Ministry through its branches and community networks to support this segment of the population. At the request of the Ministry of Health, the National Society developed a plan of action to prevent cases of leptospirosis, to promote awareness-raising, and the monitoring of campaigns for cases of fever, diarrhoea and cholera were carried out in the affected provinces; these campaigns included the transmission of key messages and the distribution of information and hygiene kits. Community health teams have been supporting provincial health directorates in vector control and community epidemiological monitoring for vector-borne diseases, particularly dengue and Zika.

Conduct briefings and debriefings with volunteers

Briefings were provided at the San Cristóbal (urban), Cambita, Moca and Nagua branches; however, these briefings have not yet taken place in Montecristi and Puerto Plata because the training in PSS, which is needed for the volunteers in the participating branches to have mastery of the subject, has also not been conducted. Furthermore, the plans for the second half of the year include strengthening of volunteering in emergencies processes.

Water, Sanitation and Hygiene Promotion

	Outputs		% reached	
			N° of families	Global
Outcome 2: Cover the needs of 4,000 families through access to safe drinking water and hygiene promotion.	Output 2.1: Safe drinking water and hygiene promotion are provided to the target population		3,543	88%
Activities	On time?		Amount	% progress
	Yes	No		
Disinfection (fogging) of affected areas	Yes		250 houses, collective centres and schools	70%
Acquisition of water purification materials		No	0	0%
(New Activity) Cleaning and disinfection of 64 wells	Yes		45 wells	70%
Purchase of 4,000 Hygiene kits	Yes		3,543 kits	89%
Distribution of 4,000 Hygiene kits	Yes		3,543 kits	89%
Purchase of 4,000 household cleaning kits		No		0%
Distribution of 4,000 household cleaning kits (1 per family)		No		0%
Accompaniment to the cleaning of 400 homes	Yes		300 homes	75%
Purchase of 4,000 buckets	Yes			35%
Distribution of 4,000 buckets (1 per family)	Yes			35%
Hygiene promotion workshop for volunteers	Yes		70 volunteers trained	100%
Hygiene promotion and water handling for the communities	Yes			70%
Distribution of 8,000 LLITNs (2 per family)	Yes		5,000 LLITNs	63%
Purchase of 10,000 jerry cans (2 per family)	Yes		2,000 jerry cans	20%
Distribution of 10,000 jerry cans	Yes		2,000 jerry cans	20%

Progress on expected results in Water, Sanitation and Hygiene Promotion

Out of the overall goal the objective of reaching 4,000 families in the 9 target provinces, 3,533 families have been reached, which amounts a completion rate of 88 per cent.

Disinfection of affected areas

A total of 250 houses, collective centres and schools were disinfected, covering 70 per cent of the target.

Acquisition of water purification material

This material could not be acquired due to the appeal's low coverage and the resulting lack of funding. Some pre-stocked material was used, which should be replenished for the National Society.

(New Activity) Cleaning and disinfection of 64 wells

The decision was made to include this activity to increase the number of beneficiaries in the drinking water budget line. Branch volunteers carried out this activity with the accompaniment of the community leaders. Because of the ongoing rains, programmed activities took a long time to be completed and even had to be reinitiated several times when wells became contaminated. Despite the challenges that have befallen this activity, 70 per cent of this activity has been completed.

Purchase / distribution of 4,000 hygiene kits

In total, 3,543 hygiene kits were purchased and delivered to 3,543 families for completion rate of 88 per cent.

Purchase / distribution of 4,000 household cleaning kits

The distribution of family cleaning kits activity was modified, and the DRC decided to include an activity related to the cleaning of affected homes and their surroundings, which was carried out by volunteers and affected community members; however, the non-stop rainfall's continuous impact on the target families caused delays in the implementation of this activity.

Accompaniment to the cleaning of homes

DRC volunteers cleaned 300 out of the target of 400 homes, which amounts to 75% progress.

Purchase of 10,000 jerrycans (affected communities)

In total, 2,000 jerrycans were purchased and distributed to the affected areas. Due to insufficient funding of the appeal, it was decided to reduce the target of 10,000 Jerrycans to 2,000. Based on the new figure, this activity has been 100 per cent completed.

Hygiene Promotion workshop for volunteers

The funding for the hygiene promotion workshop for volunteers and the Community PSS workshop for volunteers was combined into a National CBHFA Workshop, as its curriculum included both aspects. The goal to train 22 volunteers was achieved. At the start of the heavy rains, this group of trained volunteers provided support to 70 volunteers from the branches of Arenoso, Nagua, Villa Rivas, Gambita and San Cristóbal.

Hygiene promotion and water handling (community workshops)

The hygiene promotion and water handling component was included in every activity implemented in the affected areas, including awareness-raising talks prior to the distributions and later during the monitoring as well. The lack of funding limited the completion of this activity to 70 per cent.

Distribution of drinking water by tankers (San Cristóbal)

Due to the emergency caused by the rainfall, water and sanitation equipment was pre-positioned in the southern provinces of the country In March 2017. Based on the damages and needs assessment, the decision was made to place water reservoirs in the urban areas of San Cristóbal and to distribute drinking water via tanker trucks; this activity complemented the community awareness raising in safe water handling and hygiene promotion activity.

Distribution of 10,000 impregnated mosquito nets

The initial plan was to distribute 10,000 LLITNs for 5,000 families; however, due to the low coverage of the appeal, the number of nets was decreased from 8,000 to 4,000. The completion rate for the purchase and distribution of the LLITNs currently sits at 63 per cent. This activity was complemented with community awareness workshops on vector control.

Summary of trainings implemented in the last 6 months			
Workshop	Date	Location	Beneficiary Families
<i>Hygiene promotion for beneficiaries</i>	<i>4 February 2017</i>	<i>Montecristi, La Reforma</i>	<i>21</i>
<i>Hygiene promotion for beneficiaries</i>	<i>4 February 2017</i>	<i>Montecristi, Hato Viejo</i>	<i>33</i>
<i>Hygiene promotion for beneficiaries</i>	<i>4 February 2017</i>	<i>Montecristi, La Finca Mauro</i>	<i>8</i>
<i>Hygiene promotion for beneficiaries</i>	<i>5 February 2017</i>	<i>Montecristi, Los Solares</i>	<i>90</i>
<i>Hygiene promotion for beneficiaries</i>	<i>5 February 2017</i>	<i>Montecristi, Los Sapos</i>	<i>69</i>
<i>Hygiene promotion for beneficiaries</i>	<i>5 February 2017</i>	<i>Montecristi, Los Barrancones</i>	<i>30</i>
<i>Hygiene promotion for beneficiaries</i>	<i>5 February 2017</i>	<i>Montecristi, El Parque</i>	<i>60</i>
<i>Hygiene promotion for beneficiaries</i>	<i>5 February 2017</i>	<i>Montecristi, Barrio Chijo</i>	<i>30</i>
<i>Hygiene promotion for beneficiaries</i>	<i>5 February 2017</i>	<i>Montecristi, Los Chaleses</i>	<i>20</i>
<i>Hygiene promotion for beneficiaries</i>	<i>5 February 2017</i>	<i>Montecristi</i>	<i>112</i>
<i>Hygiene promotion for beneficiaries</i>	<i>25 April 2017</i>	<i>Nagua, Rio Mar</i>	<i>50</i>
<i>Hygiene promotion for beneficiaries</i>	<i>23 April 2017</i>	<i>Nagua, Arroyo Al Medio</i>	<i>28</i>
<i>Hygiene promotion for beneficiaries</i>	<i>23 April 2017</i>	<i>Nagua, Quebrada Amarilla</i>	<i>69</i>
<i>Hygiene promotion for beneficiaries</i>	<i>24 April 2017</i>	<i>Nagua, Buenos Aires</i>	<i>118</i>
<i>Hygiene promotion for beneficiaries</i>	<i>27 April 2017</i>	<i>Nagua, Rio Mar</i>	<i>69</i>
<i>Hygiene promotion for beneficiaries</i>	<i>28 January 2017</i>	<i>Santiago, Hoyo de Puchula</i>	<i>256</i>
<i>Hygiene promotion for beneficiaries</i>	<i>14 April 2017</i>	<i>Santiago, Hoyo de Puchula</i>	<i>41</i>

<i>Hygiene promotion for beneficiaries</i>	<i>28 January 2017</i>	<i>Santiago, Hoyo de Puchula</i>	<i>110</i>
<i>Hygiene promotion for beneficiaries</i>	<i>28 January 2017</i>	<i>Santiago, Barrio Los Santos</i>	<i>98</i>
<i>Hygiene promotion for beneficiaries</i>	<i>20 to 21 May 2017</i>	<i>Villa Riva: La Verde, La Langosta, Alto de Capora, Los Contreras, Los Peinados, Loma Colorá, Los Naranjos, Juana Rodríguez, Majagual, La Ceiba, Boca de Cebicos, Los Rieles arriba, Los Rieles Abajo, Polvorín.</i>	<i>537</i>
<i>Hygiene promotion for beneficiaries</i>	<i>20 May 2017</i>	<i>Cambita Garabito: San Francisco, La Torre, Las Nueces, Arroyo Higüero, La Lagunita, El Batey.</i>	<i>200</i>
<i>Hygiene promotion for beneficiaries</i>	<i>24 June 2017</i>	<i>Barahona: Polo, comunidades: Los Arroyos, La Cañá, Fondo Agustín, Las Auyamas, La Lanza, Los lirios, El charco, Los Barrancones de Los Arroyos.</i>	<i>300</i>
<i>Hygiene promotion for beneficiaries</i>	<i>29 June 2017</i>	<i>Barahona: Enriquillo and Paraíso; communities: Los Naranjos, Los Cocos (Enriquillo), Las Yaguas, Las Caobas and El Play de Paraíso.</i>	<i>175</i>
<i>Hygiene promotion for beneficiaries</i>	<i>30 June 2017</i>	<i>Barahona: La Cañada de Papoy</i>	<i>223</i>
TOTAL			2,747
Workshop	Date	Scope	No. of volunteers
<i>National CBHFA training for volunteers</i>	<i>27 to 31 March 2017</i>	<i>National</i>	<i>22</i>
<i>CBHFA training for volunteers</i>	<i>4 April 2017</i>	<i>Arenoso</i>	<i>19</i>

CBHFA training for volunteers	28 April 2017	Nagua Branch	12
Training for volunteers on hygiene habits, beneficiary selection and accountability	13 May 2017	Villa Riva Branch	14
CBHFA training for volunteers	13 May 2017	Cambita Garabitos	25
TOTAL			92

Livelihoods, nutrition and food security

Outcome 3 Contribute to the food security and the reestablishment of the livelihoods for 1,000 families affected by the floods in Montecristi, Puerto Plata and Duarte.	Outputs		% progress	
			N° of families	Global
	Output 3.1: 1,000 homes have sufficient food supplies, based on Sphere standards, to ensure food security		0	0%
	Output 3.2: 250 families have more resilient livelihoods through the support provided for the recovery of productive assets, technical capacities and protection activities for their livelihoods		0	0%
Activities	On time?		Amount	% progress
	Yes	No		
Beneficiary identification and selection		Cancelled		0%
Tender process to select providers		Cancelled		0%
Provider identification and selection		Cancelled		0%
Distribution and monitoring through the Mega V system.		Cancelled		0%
Promotional campaign for the reduction of food waste		Cancelled		0%
Distribution of food parcels to 1,000 families for 1 month		Cancelled		0%

Conduct a market study/identification and selection of programme suppliers for CTP		Cancelled		30%
Training for families on how to use the CTP		Cancelled		0%
Implementation of CTP for 250 families		Cancelled		0%
Training for families on better agricultural practices, marketing, business management and livelihoods protection actions		Cancelled		0%
Families implement livelihoods protection activities		Cancelled		0%
Accompaniment to families in livelihoods protection activities to be implemented		Cancelled		0%
Monitoring and evaluation		Cancelled		0%

Progress on expected results in Livelihoods, Nutrition and Food Security

The scheduled livelihood activities were not implemented due to the appeal's low coverage and the ongoing emergency in the country caused by the continuous rainfall; for these reasons, the GRC decided to prioritize the emergency care of affected communities in the southern provinces of the country following the floods in March 2017, and the recovery activities and selection of geographic areas are currently being assessed for this support.

Shelter

Outcome 4 Cover the needs of the families in the collective centres and settlements.	Outputs		% progress	
			N° of families	Global
	Output 4.1 4,000 families receive humanitarian aid (non-food household items)		3,732	93%
Output 4.2 100 families have temporary shelter		298	298%	
Activities	On time?		Amount	% progress
	Yes	No		
Distribution of 4,000 shelter tool kits to 4,000 families		No	964 kits	24%
Distribution of 10,000 tarpaulins	Yes		7,500 tarpaulins	75%

Training for volunteers in Participatory Approach to Safe Shelter Awareness (PASSA)		No	0	0%
Community development of PASSA		No	0	0%
Training for volunteers in safe shelters		No	0	0%
Cash Transfer Programme (CTP) for 500 families		No	0	0%
Monitoring of household repairs	Yes		0	0%


Progress on expected results in Shelter

Purchase and distribution of 4,000 shelter kits

While 2,500 shelter kits were purchased, only 964 were distributed, as there was no need for them; the remaining kits are in stock and will be used in future emergencies.

Purchase and distribution of 10,000 tarpaulins

A total of 7,500 tarpaulins were distributed in the provinces of Duarte, Barahona, María Trinidad Sánchez and Santiago de los Caballeros; the remaining 2,500 units were added to the stock of the National Society, and they will be used in future operations.

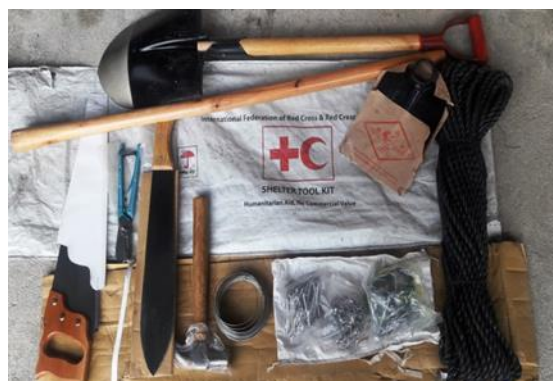

The contents of a shelter kit. Source: DRC

PASSA training for volunteers

This training was scheduled for August 2017; however, it did not take place due to the flooding in March 2017. Plans are being made to strengthen National Society's national shelter team (including focal points in Branches) in the last 3 months of 2017.

Implementation of PASSA in the community / Volunteer training on safe shelters / Cash transfer programme to 500 families and / or housing repair monitoring:

Low coverage of the appeal and the ongoing rainfall have made it impossible to implement PASSA and cash transfer programme activities in the communities; consequently, the DRC decided to prioritize the emergency care of affected communities in the southern provinces of the country following the floods in March 2017, and the recovery activities and selection of geographic areas are currently being assessed for this support. currently

Disaster risk reduction

Outcome 5: Disaster Preparedness and early warning actions are implemented for response at the community and institutional level for flooding and landslides.	Outcomes		% reached	
			N° of families	Global
	Output 5.1: At least 500 families in the affected areas know how to prepare and respond to hydro-meteorological hazards		0	0%
Activities	On time?		Amount	% progress
	Yes	No		
Initial baseline study for community activities		No	0	0%
End baseline study for community activities		No	0	0%
Trainer of trainers (ToT) on the Community Early Warning Systems (CEWS) Toolkit		No	0	0%
Training for volunteers and partners on CEWS toolkit		No	0	0%
Training volunteers and partners in Public Awareness Campaigns – hydro meteorological hazards		No	0	0%
Printing Materials for public awareness campaigns on hydro meteorological hazards		No	0	0 %
Workshop on establishing linkages between CEWS/early warning systems (EWS)		No	0	0%
Public Awareness and Public Education (PAPE) methodologies harmonization workshop		No	0	0%
National Strategic Targeting Methodology (STM) workshop		No	0	0%
Community disaster preparedness activities		No	0	0%
Progress on Risk Reduction expected results				
Please see the Shelter sector for this information.				
As originally planned, the National Society, in coordination with the IFRC, is preparing the risk reduction programme for affected communities, and a strengthening plan in disaster risk reduction is also being prepared for the National Society.				

National Society Capacity Building

Outcome 6: Strengthen the Dominican Red Cross's capacity in its headquarters and provincial branches.	Outputs		% reached	
			N° of families	Global
	Output 6.1: 100 volunteers trained to provide an effective response according to the National Society's contingency plans		23 volunteers	23%
Activities	On time?		Amount	% progress
	Yes	No		
Well-Prepared National Society (WPNS) assessment		No	0	0%
DANA training		No	0	50%
Strengthening of contingency planning		No	0	0%
National Intervention Team (NIT) training		No	0	0%
Strengthening of Emergency Operations Centre		No	0	0%
Leadership training on emergency response		No	0	0%
Update and revision of the contingency plan		No	0	0%
Equipment for the branches		No	0	0%
Progress on National Society Capacity Building expected results				
Please see the Shelter sector for this information.				
As originally planned, the emergency response capacity building programme is being prepared in coordination with the IFRC.				
Capacity building training is included in the National Society's plan pending the receipt of the required funds; the table below shows the scheduled training:				
Damage Assessment and Needs Analysis (DANA)	A training process on DANA has begun with the support of the CERA project. Two training sessions have been implemented and two others are planned: one with CERA funding and the second one with appeal funding. These were programmed for 11 to 13 August 2017; however, they had to be rescheduled due to the Hurricane Irma operation, and no date has been set yet for the completion of this activity.			
NIT training	Initially programmed for 11 to 17 September 2017			
Strengthening of EOC	Programmed for 16 to 22 October 2017			
Leadership training on emergency response	Programmed for last quarter of 2017; nonetheless, no specific dated has been set so far.			

Update and revision of the contingency plan	In process; it began the first week of September 2017, and it will finish at the end of October 2017
Equipment for the branches	This will depend on the availability of funding; if conducted, this activity would equip five branches.

Quality programming /Areas common to all sectors

Outcome 7: Continuous and detailed analysis and assessments are used to inform the operation's design and implementation.	Outputs		% reached	
	Output 7.1: Initial needs assessments are conducted in consultation with beneficiaries and authorities		N° of families	Global
Activities	On time?		Amount	% progress
	Yes	No		
Rapid emergency assessment	Yes			75%
Sectorial evaluation	Yes			85%
Coordination meetings with authorities and Civil Defence	Yes			90%
Monitoring and follow up by the IFRC	Yes			85%
Monitoring visits to the communities	Yes			95%
Deployment of general Regional Intervention Team (RIT) in ODK and Mega V for 3 months	Yes		2 months	100%
Workshop for volunteers in ODK and Mega V	Yes		1	100%
Beneficiary satisfaction survey		No		0%
Bi-national cooperation meeting		No		0%
Lessons learned workshop		No		0%

Progress on Quality Programming /Areas common to all sectors

Rapid emergency assessment	During the flooding in November 2016, rapid assessments were conducted in only 55 per cent of the affected areas. During the March 2017 floods, more than 75% of the affected areas were reached through a much more efficient rapid assessment process.
Sectorial evaluation	Sectorial evaluations also improved, as evidenced in community level workshops and interventions resulting from the sectorial evaluations that were carried out.

Coordination meetings with authorities and Civil Defence	Coordination meetings with the authorities are frequent, as the Dominican Red Cross is part of the National Risk Management System and the Emergency Operations Centre, which has remained active during the rainy periods and the interventions. Coordination has taken place with Municipal Mitigation and Response Prevention committees, and the National Society has received letters requesting support from the municipality of Cambita; additionally, the DRC has coordinated its work with the National Operations Centre, which in turn has recognized the DRC's work in their reports.
Monitoring and follow up by the IFRC	The National Society has been well supported by the IFRC, as evidenced by the mobilized RITs. The mobilization of the IFRC's Technical Coordinator was especially valuable, as he was able to participate in the National Society's assessments in the San Cristóbal province.
Monitoring visits to the communities	Red Cross Branches and the appeal team have provided continuous support to the affected communities.
Deployment of general Regional Intervention Team in ODK and Mega V for 3 months	The General RIT's mission has been very helpful for the implementation of ODK and Mega V
Workshop for volunteers in ODK and Mega V	Sixteen volunteers have been trained in ODK and Mega V; they have had the opportunity to put what they learned into practice during the distributions.
Beneficiary satisfaction survey	Pending; this will most likely be part of the Disaster Relief Emergency Fund (DREF).
Bi-national cooperation meeting	Underway; various meetings have been held between the DRC and the Haiti Red Cross Society to formalize mechanisms (Cooperation agenda in Haiti in March 2017 and numerous bilateral meetings between the Haiti Red Cross Society's president and the DRC's executive director)
Lessons learned workshop	Pending; it will be conducted by the end of the operation

Contact information

For further information, specifically related to this operation please contact:

Dominican Red Cross

- Gustavo Lara, executive director; phone +1 829-989-9730; email: gustavo.lara@cruzroja.org.do

IFRC Country Cluster Support Office for Cuba, Dominican Republic and Haiti

- Ines Brill, head of country cluster office; email: ines.brill@ifrc.org

In IFRC Regional Office of Americas:

- Inigo Barrena, disaster response and crisis and early recovery coordinator; phone: +507 317 3050; email: ci.barrena@ifrc.org.
- Mauricio Bustamante, Regional Logistics coordinator; phone: +507 317 3050; email: Mauricio.bustamante@ifrc.org

IFRC Geneva

- Cristina Estrada, response and recovery lead; phone: +41.22.730.4529, email: crisrina.estrada@ifrc.org

For Performance and Accountability (planning, monitoring, evaluation and reporting enquiries):

- Priscila Gonzalez, planning, monitoring and reporting coordinator; phone: +507 317 3050; email: priscila.gonzalez@ifrc.org

For Resource Mobilization and Pledges:

- Marion Andrivet, emergency appeals and marketing officer; phone: +507 317 3050; email: marion.andrivet@ifrc.org

Disaster Response Financial Report

MDRDO009 - Dominican Republic - Floods

Timeframe: 24 Nov 16 to 26 Nov 17

Appeal Launch Date: 26 Nov 16

Interim Report

Selected Parameters

Reporting Timeframe	2016/11-2017/8	Programme	MDRDO009
Budget Timeframe	2016/11-2017/11	Budget	APPROVED
Split by funding source	Y	Project	*
Subsector:	*		

All figures are in Swiss Francs (CHF)

I. Funding

	Raise humanitarian standards	Grow RC/RC services for vulnerable people	Strengthen RC/RC contribution to development	Heighten influence and support for RC/RC work	Joint working and accountability	TOTAL	Deferred Income
A. Budget		2,459,751				2,459,751	
B. Opening Balance							
Income							
Cash contributions							
<i>American Red Cross</i>		205,718				205,718	
<i>China Red Cross, Hong Kong branch</i>		26,409				26,409	
<i>Dominican American Coalition of Massachusetts</i>		9,762				9,762	
<i>Iraqi Red Crescent Society</i>		951				951	
<i>Japanese Red Cross Society</i>		81,200				81,200	
<i>Red Cross of Monaco</i>		16,042				16,042	
<i>Swedish Red Cross</i>		169,465				169,465	
<i>The Canadian Red Cross Society (from Canadian Government*)</i>		48,759				48,759	
<i>VERF/WHO Voluntary Emergency Relief</i>		800				800	
<i>Western Union Foundation</i>		7,410				7,410	
C1. Cash contributions		566,515				566,515	
Other Income							
<i>DREF Allocations</i>		240,000				240,000	
C4. Other Income		240,000				240,000	
C. Total Income = SUM(C1..C4)		806,515				806,515	
D. Total Funding = B + C		806,515				806,515	

* Funding source data based on information provided by the donor

II. Movement of Funds

	Raise humanitarian standards	Grow RC/RC services for vulnerable people	Strengthen RC/RC contribution to development	Heighten influence and support for RC/RC work	Joint working and accountability	TOTAL	Deferred Income
B. Opening Balance							
C. Income		806,515				806,515	
E. Expenditure		-458,774				-458,774	
F. Closing Balance = (B + C + E)		347,741				347,741	

Disaster Response Financial Report

MDRDO009 - Dominican Republic - Floods

Timeframe: 24 Nov 16 to 26 Nov 17

Appeal Launch Date: 26 Nov 16

Interim Report

Selected Parameters

Reporting Timeframe	2016/11-2017/8	Programme	MDRDO009
Budget Timeframe	2016/11-2017/11	Budget	APPROVED
Split by funding source	Y	Project	*
Subsector:	*		

All figures are in Swiss Francs (CHF)

III. Expenditure

Account Groups	Budget	Expenditure					TOTAL	Variance
		Raise humanitarian standards	Grow RC/RC services for vulnerable people	Strengthen RC/RC contribution to development	Heighten influence and support for RC/RC work	Joint working and accountability		
	A					B	A - B	
BUDGET (C)			2,459,751			2,459,751		
Relief items, Construction, Supplies								
Shelter - Relief	290,748		125,427			125,427	165,321	
Construction - Housing	50,129						50,129	
Clothing & Textiles	28,372		28,758			28,758	-386	
Food	75,192						75,192	
Water, Sanitation & Hygiene	326,121		61,067			61,067	265,054	
Teaching Materials	133,329						133,329	
Utensils & Tools	43,847		12,790			12,790	31,056	
Cash Disbursement	62,661						62,661	
Total Relief items, Construction, Sup	1,010,400		228,044			228,044	782,357	
Land, vehicles & equipment								
Computers & Telecom	23,059		1,420			1,420	21,639	
Total Land, vehicles & equipment	23,059		1,420			1,420	21,639	
Logistics, Transport & Storage								
Storage			7,907			7,907	-7,907	
Distribution & Monitoring	107,978		17,481			17,481	90,497	
Transport & Vehicles Costs	44,615		14,861			14,861	29,754	
Logistics Services	69,602		22,652			22,652	46,950	
Total Logistics, Transport & Storage	222,194		62,901			62,901	159,293	
Personnel								
International Staff	284,064		26,764			26,764	257,300	
National Staff	36,310						36,310	
National Society Staff	88,227		19,625			19,625	68,602	
Volunteers	94,847						94,847	
Other Staff Benefits	42,108		12,685			12,685	29,423	
Total Personnel	545,556		59,074			59,074	486,482	
Consultants & Professional Fees								
Consultants	22,057		17,486			17,486	4,571	
Professional Fees	20,052		42			42	20,009	
Total Consultants & Professional Fees	42,108		17,529			17,529	24,580	
Workshops & Training								
Workshops & Training	206,531		8,278			8,278	198,253	
Total Workshops & Training	206,531		8,278			8,278	198,253	
General Expenditure								
Travel	69,671		20,865			20,865	48,806	
Information & Public Relations	127,227		951			951	126,276	
Office Costs	17,846		6,306			6,306	11,540	
Communications	31,481		670			670	30,811	
Financial Charges	3,885		13,678			13,678	-9,793	
Other General Expenses			2			2	-2	
Shared Office and Services Costs	9,665						9,665	
Total General Expenditure	259,776		42,472			42,472	217,304	
Operational Provisions								
Operational Provisions			7,492			7,492	-7,492	
Total Operational Provisions			7,492			7,492	-7,492	
Indirect Costs								
Programme & Services Support Recover	150,126		27,769			27,769	122,357	

Disaster Response Financial Report

MDRDO009 - Dominican Republic - Floods

Timeframe: 24 Nov 16 to 26 Nov 17

Appeal Launch Date: 26 Nov 16

Interim Report

Selected Parameters

Reporting Timeframe	2016/11-2017/8	Programme	MDRDO009
Budget Timeframe	2016/11-2017/11	Budget	APPROVED
Split by funding source	Y	Project	*
Subsector:	*		

All figures are in Swiss Francs (CHF)

III. Expenditure

Account Groups	Budget	Expenditure					TOTAL	Variance
		Raise humanitarian standards	Grow RC/RC services for vulnerable people	Strengthen RC/RC contribution to development	Heighten influence and support for RC/RC work	Joint working and accountability		
	A					B	A - B	
BUDGET (C)			2,459,751			2,459,751		
Total Indirect Costs	150,126		27,769			27,769	122,357	
Pledge Specific Costs								
Pledge Earmarking Fee			3,096			3,096	-3,096	
Pledge Reporting Fees			700			700	-700	
Total Pledge Specific Costs			3,796			3,796	-3,796	
TOTAL EXPENDITURE (D)	2,459,751		458,774			458,774	2,000,977	
VARIANCE (C - D)			2,000,977			2,000,977		

Disaster Response Financial Report**MDRDO009 - Dominican Republic - Floods**

Timeframe: 24 Nov 16 to 26 Nov 17

Appeal Launch Date: 26 Nov 16

Interim Report

Selected Parameters

Reporting Timeframe	2016/11-2017/8	Programme	MDRDO009
Budget Timeframe	2016/11-2017/11	Budget	APPROVED
Split by funding source	Y	Project	*
Subsector:	*		

All figures are in Swiss Francs (CHF)

IV. Breakdown by subsector

Business Line / Sub-sector	Budget	Opening Balance	Income	Funding	Expenditure	Closing Balance	Deferred Income
BL2 - Grow RC/RC services for vulnerable people							
Disaster management	2,459,751		806,515	806,515	458,774	347,741	
Subtotal BL2	2,459,751		806,515	806,515	458,774	347,741	
GRAND TOTAL	2,459,751		806,515	806,515	458,774	347,741	

Annex 1

- Dominican Red Cross, situation report on floods: <http://reliefweb.int/report/dominican-republic/cruz-roja-dominicana-informe-de-situacion-por-inundaciones-10-noviembre-de>
- Red Cross Director says that the worst part comes after the floods: <http://noticiassin.com/2016/11/director-de-la-cruz-roja-dominicana%C2%A8despues-de-las-inundaciones-viene-lo-peor%C2%A8/>
- Distribution of Humanitarian Assistance in Santiago de los Caballeros: <http://www.cruzroja.org.do/2017/01/31/1683/>
- Dominican Red Cross responds to floods with the support of the International Federation of Red Cross and Red Crescent Societies: <http://www.ifrc.org/es/noticias/noticias/americas/dominican-republic/la-cruz-roja-dominicana-en-la-respuesta-a-las-inundaciones/>
- Support from the Robinson Cano Foundation and the Dominican Red Cross: <http://www.cruzroja.org.do/2017/02/08/cruz-roja-dominicana-junto-a-robinson-cano-entregan-asistencia-humanitaria/>
- Distribution of humanitarian assistance in Montecristi, Dominican Red Cross Twitter account: <https://pbs.twimg.com/media/C4WU7aXVUAAVfPc.jpg>
- Distribution of humanitarian assistance in Santiago de los Caballeros: <https://twitter.com/crdominicana/status/830151860237455360>
<https://twitter.com/crdominicana/status/829887620394004481>
- Red alert issued for rains and flooding, humanitarian network: http://www.redhum.org/alerta_detail/1116
- Dominican Red Cross provides details of its response to the floods: http://diario55.com/blog_details.cfm?post_id=24526
- Fatalities due to floods. Red Cross and Civil Defence work on evacuations: <https://www.metror.d.do/noticias/2016/11/28/menos-cinco-fallecidos-villa-isabela-inundaciones.html>
- 13 provinces in red alert; Red Cross and Civil Defence prepare response for possible evacuation: <http://eldia.com.do/el-coe-mantiene-13-provincias-en-alerta-por-inundaciones/>
- Hurricane Matthew will bring rainfall to the Dominican Republic: <http://acento.com.do/2016/ecologia/8387728-huracan-matthew-traera-lluvias-abundantes-republica-dominicana-alerta/>
- 5 people dead due to floods: <http://www.elnuevodia.com/noticias/internacionales/nota/mueren5personasporinundacionesenrepublicadominicana-2267038/>
- Livelihoods and crops largely damaged due to floods: <http://www.diariolibre.com/noticias/mas-de-100-mil-tareas-de-platanos-y-otros-productos-estan-inundadas-en-montecristi-KM5583084>
- Fatalities due to severe floods in the country: http://www.laconexionusa.com/noticias/20161128456605_lc45660528.asp

Annex 2

Sensibilización pública en salud comunitaria

Provincias	Municipios	Voluntarios capacitados en Spac y Aps	Comunidades intervenidas por voluntarios Capacitado en Spac	No. de Familias sensibilizadas, Leptospira, malaria, dengue, Colera.
Duarte	Nagua	29	Buenos Aires	118
			Rio mar	69
			Quebrada Amarilla	69
	Villa Rivas	14	La langosta	49
			Los contreras	57
San Cristobal	San Cristobal Urbana	27	Moscos	40
		15	Barrio La Cucaracha	61
		21	Villa Mercedes	67
		17		
	Cambita	25	La torres,	29
			Las nueces	21
			Arroyo Higuero	
		El batey (Comunidad Haitiana)	27	
		129		607

Primeros Auxilios Psicologicos en Albergues.

Comunidades Albergues	No. de familias	Embarazada	Paridas	0 a 5	5 de 18 en adelante	Discapacitados	Extranjero
Villas Mercedes (Iglesia Villa Progreso)		4	1	38	121	1 Ciego	2
Barrio Los Molinas Casa de Familias.	89	3	0	15	67		
BarrioMoscos. CentroComunal Manuel Montero	4	3	0	11	125		

Annex 3

OPERACIÓN LLUVIAS ABRIL-MAYO 2017				
Ficha Tinaco	Comunidad	Cantidad de Galones	Cantidad de litros	Cantidad de Familias Beneficiadas
1	villa mercedes	31800	117660	67
2	Barrio Nuevo	31800	117660	29
3	Madre Vieja Norte	31800	117660	40
4	La Cuchara	31800	117660	8
5	Cambita Barrio Lucinda	31800	117660	50
6	Cambita Barrio INVI	31800	117660	120
7	Cambiata el acueducto	31800	117660	80
	Total	222,600.00	823,620.00	394

nota: tinacos de 530 gl. Llenados minimo 2 veces por dia, $(530 \times 2 = 1,060 \text{ Gl} \times 30 \text{ dias} = 31800 \times 7 = 222,600)$ reportados es por la distribucion de agua masiva, donde se llevo agua a las cisternas de las

Tecnico EDAS
JOSE RAMON M.
GERMAN ROSARIO
GEMARO DOÑE
Felix Lora
Felix Lora
Felix Lora

|

|

22600 la diferencia con
escuelas y los albergues

Annex 4

LIMPIEZA DE CASAS SAN CRISTOBAL				
Comunidades intervenidas	Motivo de activacion	Situacion encontras	Recursos Movilizados	Cantidad de Beneficados
Lecheria	Desbordamiento de Cloaca, la cual penetro viviendas mediante el debordamiento cañada	Una cañada que le pasa por Frente a las viviendas .	5 -Voluntarios Un Jeep de Desinfeccion M-86	10 familias
Barrio las Flores	Seaneamiento de la viviendas, personas con casos leptopirosis	En este Barrio se encontraron dos casos de leptopirosis, un fallecido y uno interno en Reg.H-J-P	6 -Voluntarios Un Jeep de Desinfeccion M-86	25 familias
Centro educativo	Inapi-	Desbordamiento de Cloaca.	5-Voluntarios Un Jeep de Desinfeccion M-86	178- Niños Que asiten al centro, entre maña y tarde.

Annex 5

DETALLE DISTRIBUCION DE AYUDA HUMANITARIA ENTREGADA

FAMILIAS BENEFICIADAS	3287
-----------------------	------

3315	2643	4972	5320	5644	150	1092
------	------	------	------	------	-----	------

SANTIAGO	379
-----------------	------------

FILIAl	N° FAMILIAS	MUNICIPIO	COMUNIDAD	KIT HIGIENE	LONAS	JERRY CANS	MOSQUITEROS	REPELENTES	CUBETAS	SHELTER KIT	FECHA DISTRIBUCION	SALDO	OBSERVACIONES
SANTIAGO	344	Santiago	Hoyo de Puchula	127	0	0	127	254	0	0	28/01/2017	0	Entregado
			Hoyo de baitola	53	0	0	53	106	0	0	28/01/2017	0	Entregado
			Barrio Los Santo	91	0	0	91	182	0	0	28/01/2017	0	Entregado
			La Javilla	44	0	0	44	88			28/01/2017		Entregado
			Las Mercedes	29	0	0	29	38			28/01/2017		Entregado
	Hoyo de Puchula	35	81	46	70	70			41	09/03/2017	0	Entregado	
				379	81	46	414	738	0	41			

MONTECRISTI	481
--------------------	------------

FILIAl	N° FAMILIAS	MUNICIPIO	COMUNIDAD	KIT HIGIENE	LONAS	JERRY CANS	MOSQUITEROS	REPELENTES	CUBETAS	SHELTER KIT	FECHA DISTRIBUCION	SALDO	OBSERVACIONES
PALO VERDE	481	Palo Verde	Centro del Pueblo	110	0	700	700	700	0	0	05/02/2017		Entregado
			Los Mauri	8	0	22	22	22	0	0	05/02/2017		Entregado
			La Reforma	21	0	120	120	120	0	0	05/02/2017		Entregado
			Los Charleles	20	0	46	46	46	0	0	05/02/2017		Entregado
			Hato Viejo	33	0				0	0	05/02/2017		Entregado
			Los Solares	90	0				0	0	05/02/2017		Entregado
			Los Sapo	69	0				0	0	05/02/2017		Entregado
			Los Barrancones	30	0				0	0	05/02/2017		Entregado
			El Chijo	30					0	0	05/02/2017		Entregado
El Parque	70	0	86	86	86	0	0	05/02/2017		Entregado			
				481	0	974	974	974	0	0			

DUARTE	664
---------------	------------

FILIAl	N° FAMILIAS	MUNICIPIO	COMUNIDAD	KIT HIGIENE	LONAS	JERRY CANS	MOSQUITEROS	REPELENTES	CUBETAS	SHELTER KIT	FECHA DISTRIBUCION	SALDO	OBSERVACIONES
ARENOSO	150	Arenoso	EL GUAYABO	0	300	0	0	0	150	150	05/03/2017	0	Entregado
ARENOSO	150	Arenoso	EL GUAYABO	154		300	300	300			06/05/2017		Entregado
Villa Rivas	537	Villa Riva	Villa Riva	537	1074	1074	1074	1074		350	Sabado 20 de Mayo		Entregado
				691	1374	1374	1374	1374	150	500			

MARIA T SANCHEZ	250
------------------------	------------

FILIAl	N° FAMILIAS	MUNICIPIO	COMUNIDAD	KIT HIGIENE	LONAS	JERRY CANS	MOSQUITEROS	REPELENTES	CUBETAS	SHELTER KIT	FECHA DISTRIBUCION	SALDO	OBSERVACIONES
Nagua	250		Rio Mar	26	52	52	52	52	0	26	29 y 30 abril 2017	0	Entregado
			Arroyo al medio	45	20	90	90	90	0	10	29 y 30 abril 2017	0	Entregado
			Las Gordas Quebrada Amarilla	46	24	92	92	92	0	12	29 y 30 abril 2017	0	Entregado
			Buenos Aires	133	104	266	266	266	0	52	29 y 30 abril 2017	0	Entregado
							250	200	500	500	500	0	100

ESPAILLAT		350											
FILIAL	N° FAMILIAS	MUNICIPIO	COMUNIDAD	KIT HIGIENE	LONAS	JERRYCANS	MOSQUITEROS	REPELENTES	CUBETAS	SHELTER KIT	FECHA DISTRIBUCION	SALDO	OBSERVACIONES
Gaspar Hernandez	150	Espaillat	La Cuchara	100	210	210	200	200	0	44	25 marzo	0	Entregado
			Villa Progreso	50	110	110	100	100	0	23	25 de marzo	0	Entregado
Moca	200	Espaillat		200	0	0	0	0	0	0	Noviembre 2016	0	Entregado
				350	320	320	300	300	0	67			

PUERTO PLATA		74											
FILIAL	N° FAMILIAS	MUNICIPIO	COMUNIDAD	KIT HIGIENE	LONAS	JERRYCANS	MOSQUITEROS	REPELENTES	CUBETAS	SHELTER KIT	FECHA DISTRIBUCION	SALDO	OBSERVACIONES
Sabaneta de Yasica	75	Puerto Plata	Sabaneta de Yasica	75	0	0	0	0	0	0			
Montellano			Montellano										
Puerto Plata			Puerto Plata										
				75	0	0	0	0	0	0			

BARAHONA		889											
FILIAL	N° FAMILIAS	MUNICIPIO	COMUNIDAD	KIT HIGIENE	LONAS	JERRYCANS	MOSQUITEROS	REPELENTES	CUBETAS	SHELTER KIT	FECHA DISTRIBUCION	SALDO	OBSERVACIONES
Barahona	200	Vicente Noble	VICENTE NOBLE	200	0	0	0	0	0	0	OCTUBRE 2016	0	entregado
	214	Barahona	Cachada de Papoy	214		428	428	428					Entregado
	300	Polo	Los Arroyos	130		260	260	260			23/06/2017		Entregado
		Polo	Las Auyamas	16	20	32	32	32		10	23/06/2017		Entregado
		Polo	Fondo Agustín	72	30	144	144	144		15	23/06/2017		Entregado
		Polo	La Cañada	82	30	164	164	164		15	23/06/2017		Entregado
		Polo	La Lanza		120					60	23/06/2017		Entregado
		Polo	Los Lirios		40					20	23/06/2017		Entregado
		Polo	Los Arroyos		120					60	23/06/2017		Entregado
		Polo	El Charco		20					10	23/06/2017		Entregado
		Polo	Los Barrancones de Los Arroyos		20					10	23/06/2017		Entregado
		22	Paraiso	La Yagua	12		24	24	24			29/06/2017	
	Paraiso		Las Caoba	5		10	10	10			29/06/2017		Entregado
	Paraiso		El Play	5		10	10	10			29/06/2017		Entregado
	153	Enriquillo	El Naranjo	101		202	202	202			29/06/2017		Entregado
		Enriquillo	Los Coco Abajo	52		104	104	104			29/06/2017		Entregado
				889	400	1378	1378	1378	0	200			

SANCRISTOBAL		200											
FILIAL	N° FAMILIAS	MUNICIPIO	COMUNIDAD	KIT HIGIENE	LONAS	JERRYCANS	MOSQUITEROS	REPELENTES	CUBETAS	SHELTER KIT	FECHA DISTRIBUCION	SALDO	OBSERVACIONES
CAMBITA (SC)	200	Cambita	San Francisco	40	88	80	80	80		44	20/05/2017		Entregado
		Cambita	La Torres	33	36	66	66	66		28	20/05/2017		Entregado
		Cambita	Las Nueces	60	54	120	120	120		47	20/05/2017		Entregado
		Cambita	Arroyo Higuero	16	26	32	32	32		13	20/05/2017		Entregado
		Cambita	El Batey	24	28	48	48	48		24	20/05/2017		Entregado
		Cambita	La Lagunita	27	36	34	34	34		28	20/05/2017		Entregado
				200	268	380	380	380	0	184			

3,287

2,936

2,562

4,926

4,906

4,906

150

1,051

Annex 6

DISTRIBUCION POR FAMILIAS

Provincia	Comunidad	Mujeres	Niños	hombres	Ancianos	Discapitado	Embarazadas	Total de personas
Maria Trinidad Sanchez	Barranca Amarrilla	97	16	77	2	1	1	194
Maria Trinidad Sanchez	Buenos Aires	143	85	200	10	9	6	453
Maria Trinidad Sanchez	Arrollo Al medio	29	8	31	48	1	2	119
Maria Trinidad Sanchez	Rio Mar	15	53	42	51	4	7	172
								0
Gaspar Hernandez	Villa Progreso	79	4	43	2	4	1	133
Gaspar Hernandez	La cuchara	9	42	29	5	4	0	89
								0
Duarte	El Guayabo (Arenoso)	209	90	246	27	5	7	584
Duarte	Loma Coloras (Villa Riva)	71	15	12	4	1	0	103
Duarte	Los Rieles Arriba (villa Riva)	95	50	60	8	3	4	220
Duarte	Boca de Cevico (Villa Riva)	50	10	41	15	7	1	124
Duarte	Los Peinados (Villa Riva)	62	29	78	10	9	3	191
Duarte	Los Rieles Abajo (Villa Riva)	44	20	37	2	1	0	104
Duarte	Juan Rodriguez (Villa Riva)	43	27	77	5	5	2	159
Duarte	La Langosta (Villa Riva)	32	11	40	3	1	0	87
Duarte	los contreras (Villa Riva)	108	65	105	4	3	6	291
Duarte	Los Naranjos (Villa Riva)	80	20	130	42	10	2	284
Duarte	Majagual (Villa Riva)	27	23	57	9	2	3	121
Duarte	El Guayabo (Villa Riva)	209	87	246	27	7	1	577
Duarte	Polmorin (Villa Riva)	13	4	24	1	3	0	45
Duarte	La Verde (Villa Riva)	179	53	213	12	5	7	469
								0
Barahona	Los Cocos	86	78	74	2	2	3	245
Barahona	Cañada de Papoi	276	233	234	17	25	12	797
Barahona	paraiso	51	40	45	2	2	0	140
Barahona	La Lanza	66	212	71	0	0	0	349
Barahona	El Chalco	12	16	11	0	0	2	41
Barahona	Los Lirios	23	12	28	0	0	0	63
Barahona	La Auyama	49	16	43	2	1	0	111
Barahona	Fondo Agustin	82	24	62	10	5	3	186
Brahona	Los arroyos arriba	109	53	79	8	5	9	263
Barahona	los arroyos abajo	191	95	121	13	7	10	437
Barahona	la cañada	143	45	98	5	4	3	298
Barahona	EL Naranjal	140	92	136	22	9	6	405
								0
Santiago De Los caballeros	Hoyo de puchula	248	216	127	10	1	5	607
Santiago De Los caballeros	Hoyo de Bartola	103	90	53	4	1	2	253
Santiago De Los caballeros	Barrio los Santos	177	155	91	7	1	4	435
Santiago De Los caballeros	La Javilla	86	75	44	4	0	2	210
Santiago De Los caballeros	Las Mercedes	57	49	29	2	0	1	139
Santiago De Los caballeros	Hoyo de Puchula	68	60	35	3	0	1	167

								0
Monte Crististi	Centro del Pueblo	215	187	110	9	1	4	526
Monte Crististi	Los Mauri	16	14	8	1	0	0	38
Monte Crististi	La Reforma	41	36	21	2	0	1	100
Monte Crististi	Los Charlezes	39	34	20	2	0	1	96
Monte Crististi	Hato Viejo	64	56	33	3	0	1	158
Monte Crististi	Los Solares	176	153	90	7	1	4	430
Monte Crististi	Los Sapo	135	117	69	6	1	3	330
Monte Crististi	Los Barrancones	59	51	30	2	0	1	143
Monte Crististi	El Chijo	59	51	30	2	0	1	143
Monte Crististi	El Parque	137	119	70	6	1	3	335
								0
San Cristobal	La Lagunita	66	24	53	11	8	0	162
San Cristobal	Batey Haitiano	36	10	30	1	0	1	78
San Cristobal	San Francisco	75	22	53	0	1	1	152
San Cristobal	Arroyo Higuero	13	15	32	7	1	1	69
San Cristobal	Las Nueces	134	78	13	4	0	2	231
San Cristobal	La Torre	58	42	36	7	1	2	146
								0
								0
		Mujeres	Niños	hombres	Ancianos	Discapacitado	Embarazadas	Total de personas
		4881	3281	3867	467	165	142	12803
