


www.ifrc.org
Saving lives,
changing minds.

Emergency Plan of Action

Tanzania: Floods



International Federation
of Red Cross and Red Crescent Societies

DREF n° MDRTZ021	Glide n°: FL-2018-000043-TZA
Date of issue: 30 April 2018	Expected timeframe: 3 months
Operation start date: 30 April 2018	Operation end date: 31 July 2018
IFRC focal point and budget holder responsible for this operation (project manager): Lisa Zitman, Disaster management delegate, East Africa Cluster	National Society focal point responsible for this operation (project manager): Renatus Mkaruka, Director of Disaster management, Tanzania RC
Category allocated to the of the disaster or crisis: Yellow	
DREF allocated: CHF 196,499	
Total number of people affected: 15,862 or 3,172 HHs (1,146 in Zanzibar, 2,740 in Arusha and 11,976 in Dar es Salaam)	Number of people to be assisted: <ul style="list-style-type: none"> • 800 households or 4,000 people, representing 25% of affected population will be direct beneficiaries of this operation (500 in Zanzibar, 1,000 in Arusha and 2,500 in Dar es Salaam) • 3,172 households or 15,862 people, indirect beneficiaries
Host National Society presence (n° of volunteers, staff, branches): In Dar es Salaam branch 70 volunteers and 3 staff are supporting the operation, in Arusha 50 volunteers and 1 staff, in Zanzibar 30 volunteers and 3 staff and 7 staff from Tanzania Red Cross (TRCS) headquarters are supporting the flood operation.	
Red Cross Red Crescent Movement partners actively involved in the operation: International Federation of Red Cross and Red Crescent Societies (IFRC), Belgium Red Cross Flanders (BRC)	
Other partner organizations actively involved in the operation: Government of Tanzania including local governments & Dar es Salaam Multi-Agency Emergency Response Team (DARMAERT).	

Situation analysis

Description of the disaster



TRCS volunteer sending plastic sheltering material to flood victims in Longido, Arusha © TRCS

Heavy rainfall occurred in different parts of Tanzania mainland and Zanzibar from 12 to 18 April 2018, causing floods. The flood affected regions include Dar es Salaam (Kinondoni, Ilala, Temeke and Kigamboni Municipals); Arusha (Arusha District Council, Meru, Longido, Monduli districts); Zanzibar; Kilimanjaro (Same, Hai, Mwanga districts); Tanga (Handeni, Lushoto districts); Manyara (Simanjiro, Kiteto, Babati districts); Tabora (Nzega and Kaliua districts); Pwani (Mafia and Rufiji districts); Mwanza, Morogoro, Dodoma, Mbeya, Rukwa, Mtwara, Shinyanga, and Geita.

Immediately after the flooding occurred, TRCS deployed a National Disaster Response Team (NDRT), a Branch Disaster Response Team (BDRT) and volunteers from TRCS branches of Arusha, Dar es Salaam and Zanzibar to evacuate affected people, administer first aid to people in need and conduct a rapid initial assessment of the situation. The evacuations and first aid activities are ongoing in Arusha due to the continuous flooding.

Given the limited means available in country to respond fully to this emergency, Tanzania Red Cross Society (TRCS) is requesting CHF 196,499 from the International Federation of Red cross and Red Crescent Societies (IFRC) through the Disaster Relief Emergency Fund (DREF) to launch a relief operation.

This DREF operation will focus on the most affected regions, which are Arusha, Dar es Salaam and Zanzibar. Based on TRCS volunteer assessment and Dar es Salaam Multi-Agency Emergency Response Team (DARMAERT) reports, a total of 15,862 people are directly affected by floods in Zanzibar, Arusha and Dar es Salaam. The death toll as at now is 15 people in Dar es Salaam and one (01) person in Arusha. Additionally, 11 people were severely injured in Dar es Salaam.

In Arusha a total of 548 households have been displaced due to the floods and 203 houses are damaged. In Dar es Salaam, some 2,151 households are displaced, 42 houses and 21 latrines completely collapsed and 342 houses severely damaged (DARMAERT & TRCS assessment, 2018). In the island of Zanzibar, 191 households have been displaced and 225 houses damaged. As a result of this, the majority of flood victims sought refuge with relatives and neighbours while 19 households did not relocate and continue living in houses full of water which is a big health risk. It should be noted that the rescue and evacuation of families is carrying on in Arusha due to the continuous heavy downpour.



TRCS volunteers conducting flood rapid assessment in Magomeni, Dar es Salaam © TRCS

Summary of the current response

Overview of Host National Society.

As highlighted in the description of the disaster, TRCS deployed a National Disaster Response Team (NDRT), a Branch Disaster Response Team (BDRT) and volunteers from TRCS branches of Arusha, Dar es Salaam and Zanzibar to evacuate affected people and administer first aid to people in need, immediately after the flooding occurred. A total of 150 volunteers are involved in the emergency interventions in the three regions.

Tanzania Red Cross regional branches conducted a rapid impact and needs assessments from 14-16th April to assess the damage and needs on the ground. Based on the initial findings, TRCS did an initial distribution with prepositioned stock which only covered Dar es Salaam due to the limited stock available.

The below table highlights the initial distribution conducted by TRCS at initial stage of response

Items distributed	Quantity per HH	Total
Blankets	3 per HH	300
Buckets	2 per HH	200
Jerrycans	1 per HH	100
Mattresses	2 per HH	200
Kitchen sets	1 per HH	100
Tents		40
Total number of HH reached		100

In the Arusha and Zanzibar, the operation has been focused on evacuation, rescue and first aid services. In addition, TRCS is participating in DARMAERT stakeholder meetings for assessment, planning and joint response.

Overview of Red Cross Red Crescent Movement in country

IFRC provides technical support to the TRCS through the East Africa and Indian Ocean Islands Cluster office and Africa Region office based in Nairobi, Kenya. Additionally, there is one in country IFRC finance delegate supporting the National Society.

The Belgian Red Cross Flanders is supporting the initial phase of the floods response with funding for volunteer allowance and fuel. This has enabled the implementation of the rescue, evacuation and assessment activities.

Spanish Red Cross is available to give technical support to the response. In addition to this, TRCS is in constant contact with these in-country partners and IFRC and ICRC, with updates about the situation and response.

Overview of non-RCRC actors in country

The local government authorities in the affected areas are supporting the affected populations in rescue, evacuation and needs assessment. Prior to the floods and throughout the week of heavy rains, the Tanzania Meteorological Agency (TMA) has been issuing early warning and advisory messages to the public. The fire and rescue unit of the police force have equally been on the front line of the evacuation and rescue interventions. The Tanzania Asian Development Association and Shia Community were also engaged in the rescue and evacuation support.

Coordination mechanisms in each of the affected regions have been established and are chaired by regional Disaster Management (DM) commissioners, following the government DM structure. TRCS is a member of these coordination platforms at all levels and participates in the coordination meetings.

TRCS is in contact with UNICEF, a long-term partner in disaster response and relief. With financial support from UNICEF, the government has been distributing water purification tablets in the affected areas. No further financial support is expected from UNICEF to TRCS in this flood response.

Needs analysis, targeting, scenario planning and risk assessment

Needs analysis

According to the needs assessment conducted by TRCS branches, the immediate needs are food items¹ (FIs) and essential non-food items (NFIs) (kitchen sets, buckets and jerry-cans, mosquito nets, mattresses, blankets, rain coats and gum-boots for volunteers). Other items needed include emergency shelters (tents, tarpaulins), latrine slabs, oral rehydration salts, water purification tablets, hygiene promotion leaflets and support to repair surface water drainage systems.

The table below provides a summary of needs identified in Arusha, Dar salaam and Zanzibar.

Sector	Identified needs
Health	Heightened risk of malaria infection due to the loss of habitat and mosquito nets and ensuing exposure to mosquitoes. The local authorities have provided mosquito nets to all households in Tanzania as part of a Malaria prevention campaign between 2015 and 2017. TRCS will distribute mosquito nets to families affected by the floods, to replace the damaged nets. After the government initiative of mosquito net distribution, the need to conduct sensitization and enforce malaria prevention mechanisms has been identified. TRCS will sensitize targeted communities on malaria prevention during and after distribution of the mosquito nets. Due to the personal losses of property, psychosocial needs have also been identified. In addition, six (6) Health facilities have been affected in Dar es Salaam.

¹ In Tanzania Food Items and its logistic Management is handled by the Government

Water and sanitation	<p>The water systems have been affected by floods. This situation and the consequent use of unsafe water has increased the risk of water-borne diseases such as diarrhoea or Cholera. The loss of hygiene and household materials (such as bucket, jerry cans, soaps, etc.) worsens this situation. Furthermore, household latrines have been flooded and / or damaged, increasing the risk of poor hygiene and sanitation related diseases. In the assessment, the most urgent needs identified are water purification tablets, soap bars, buckets and hygiene awareness.</p> <p>The cholera outbreak in Longido which is a district within Arusha province that has not been affected by the floods, is a risk due to proximity and population movement of the nomadic community.</p>
Shelter	<p>People are currently sheltered by their neighbours and public facilities. However, this situation puts pressure on the host families whose houses are often overcrowded due to lack of living space. Therefore, the shelter need is urgent according to humanitarian standards. Beyond immediate shelter needs, the recovery phase needs to be considered by relevant actors to provide building materials to help families recover their houses. In the assessment, the most urgent needs identified are cooking utensils, mattresses and blankets.</p>

Targeting

This DREF operation targets 800 households of the most affected displaced households in Dar es Salaam, Arusha and Zanzibar. Targeted population is selected based on; displaced households, female-headed households, the chronically ill, elderly persons, pregnant and lactating women, and households with children under-five years old.

To note, hygiene promotion services will target the entire affected population, which is approximately 15,862 people or 3,172 households.

Scenario planning

Best case scenario	Most likely scenario	Worst case scenario
<p>The rains stop, no more people are affected, and no secondary effects are suffered e.g. outbreak of diseases in the current affected areas or other parts of the country.</p>	<p>The rains continue through April/May but no more than 50mm in 24 hours in any part of the current affected areas or other parts of the country.</p>	<p>The rains continue heavily through April/May, with episodes of more than 50mm in 24 hours in any part of the current affected areas or other parts of the country, resulting in massive displacement of people and destruction of infrastructure and assets.</p>
<p>TRCS Response: Limited to the current DREF operation and no more than 4 weeks response.</p>	<p>TRCS Response: Limited to the current DREF operation, with continued alert and on standby. Engaging with communities for early warning, preparedness and disaster risk reduction measures.</p>	<p>TRCS Response: Revision of the current DREF operation through an Operations update to widen the scope of intervention, with possible change of strategy, increased timeframe and possibly a request for a second allocation or proceed to a large-scale operation through an application for an Emergency Appeal.</p>

Operation Risk Assessment

The security situation is reasonably stable across the country. However, TRCS will ensure a continuous monitoring of security environment and implement security risk mitigation measures. Access can become challenging, depending on the continued rainfall, as damages to infrastructures like roads and bridges are common when floods hit Tanzania.

If the number of affected people rises further, it might become a challenge to provide sufficient protective gear for all the volunteers involved in the response operation. The limited amount of humanitarian actors in the country might become a risk if the rains continue heavily during April and May, and other parts of the countries might also become affected.

While implementing the operation, TRCS will continue to assess the situation and update the strategy to ensure the National Society is properly resourced and supported to provide the needed humanitarian assistance.

A cholera outbreak has been confirmed in the Longido District of Arusha Region. The flood affected districts in Arusha are Arumeru, Monduli and Arusha district council. Longido, the district where a cholera outbreak has been confirmed, is not affected by floods. However, due to the proximity and movement of people between the two districts, the spread of cholera is an identified risk. TRCS will carry out preventive measures in hygiene promotion and messaging in the floods affected areas to limit this risk.

B. Operational strategy²

Overall Operational objective

The overall objective of this DREF operation is to improve the living conditions of the most vulnerable 800 households affected by floods in Dar es Salaam, Arusha and Zanzibar. This will be done by carrying out the most urgent activities in Shelter, including NFI distribution, health and WASH.

Proposed strategy:

The operational intervention sectors will focus on **health** activities including provision of first aid services **and water, sanitation and hygiene** including hygiene promotion, vector control, NFI distributions and replenishment of utilized TRCS Disaster Preparedness (DP) stock. In the clean-up exercise in affected communities, TRCS volunteers will engage with the communities to provide sanitation and hygiene promotion. All data collected during the assessment and relief distribution will be shared with the government. Continuous needs assessment is a crucial part of the operation, thus will be carried out throughout the timeframe of the operation by staff and volunteers directly involved in the response operation. The below specific sectors will be addressed through this DREF operation.

Shelter

Through this DREF operation, TRCS will conduct an assessment of immediate shelter needs and procure NFIs including blankets (3 per family), kitchen sets (1 per family) and mattresses (2 per family) to support beneficiary families to regain their homes with a minimum of dignity. Some of the procured items will be used to replenish the stock used to serve 100 households during the initial response.

Health

During this operation, TCRS volunteers will continue to conduct search and rescue operations and provide first aid services to the affected and injured persons.

As a contribution to vector control and based on the needs identified, TRCS will procure mosquito nets for 800HH. Each family will receive two nets. During their distribution, the volunteers will train beneficiaries on their appropriate use and sensitize targeted communities on malaria prevention.

In addition, oral rehydration salt (ORS) will be purchased and distributed to households which have been identified with family members suffering from acute watery diarrhoea.

Water, Sanitation and Hygiene (WASH)

Through this DREF operation, TRCS will procure and distribute water treatments tablets (Aquatabs; 1 tablet for 20L, 20L per day per HH, 30 tablets per month to support 800HH) for home purification water for drinking and family hygiene kits (1 kit per household, kits include towels, soap bars, sanitary packs, toothbrushes and toothpaste). This DREF operation will address the water purification needs of 800HH for one month, i.e., 24,000 tablets of Aquatabs. Prior to distributing the Aquatabs, the target groups will be trained on the correct usage of water treatment products by volunteers. To support the WASH component, TRCS will procure NFIs including jerrycans and buckets to support

beneficiary families in collecting and storing clean and safe water. Some of the procured items will be used to replenish TRCS stock used during the initial response as indicated under shelter sector.

In addition, and key to the operation, hygiene promotion will be carried out with emphasis on hand washing with soap. This will include awareness raising to ensure people do not consume water from stagnant areas. Water sources such as hand-pumped wells will also be disinfected. In collaboration with the local government TRCS will carry out water quality monitoring.

Due to the high risk of cholera spreading from the nearby district of Longido in Arusha, TRCS will disseminate key messages on Cholera prevention during the hygiene promotion sessions in the communities. Additionally, TRCS will carry out a radio spot airing on hygiene promotion and cholera prevention.

TRCS will procure hoes, spades, wheelbarrows and rakes which will be used to drain the stagnant water during the environmental cleaning exercise.

The below table presents an overview of the NFIs to be procured for distribution and partial replenishment of utilized TRCS stock:

Items	To be distributed per HH (800 HHs)	To be replenished
Jerry cans (20L)	1 per HH	100 contributions to NS stock
Buckets (20L)	2 per HH	100 contributions to NS stock
Blankets for Arusha	Medium heavy blankets (3 per HH)	
Kitchen set	1 per HH	100 contributions to NS stock
Mattresses	2 per HH	100 contributions to NS stock)
Aquatabs	24,000 tabs (30 tabs/HH for 1 month)	
ORS	4,800 sachets (12 sachets / pers). Target here is 400 people (10% of 4,000 people or 800 HH)	
Family Hygiene Kits	1 per HH	
Items procured for Environmental Hygiene		
Hoes	20	
Spades	20	
Wheelbarrows	5	
Rakes	20	
ORS		

To implement the above-mentioned strategy, 150 volunteers will be trained and deployed to conduct beneficiary targeting and registration and hygiene promotion activities. Indeed, as they are already at the forefront of the rescue operations, they will also be in charge of training beneficiaries on the use of the water purification tablets, mosquito nets and will also be responsible of carrying out the distribution of procured NFIs to targeted beneficiaries.

Volunteers recruited and trained will be deployed in the various operational areas as follows to ensure that target number of people are reached:

Affected region	No. of people targeted	No. of volunteers deployed
Arusha	1,000	50
Dar es Salaam	2,500	70
Zanzibar	500	30
Total	4,000	150

To support volunteers in their mission, TRCS through this DREF operation will procure protection items for volunteers. Indeed, protection and visibility items will be procured for 150 volunteers which include: Red Cross jackets, raincoats and gumboots. In addition, TRCS will produce and issue IEC materials to promote hygiene awareness.

With funding from the long term IFRC Population Movement program, a logistics RDRT will be deployed for 2-3 months to support both the long-term program and the DREF operation. As such, the cost for this deployment will not be budgeted on this DREF operation. The logistics RDRT will assist TRCS with the procurement process to ensure that the procurement and distribution is in line with the IFRC/TRCS procurement policy, and quality of the to be procured NFIs. In addition and depending on the length of the RDRT stay on the field, he/she will provide the necessary support to TRCS on monitoring and reporting of this DREF operation. This same program will cover costs for the IFRC monitoring visit conducted during this DREF operation.

Monitoring and evaluation of this DREF operation, the TRCS Headquarter (HQ) team led by the Director of Disaster Management, will conduct two rounds of supportive field supervision in each of the three regions namely Dar es Salaam, Arusha and Zanzibar. The HQ team will consist of at least 7 staff (DM, Health, OD and PMERL) that will be allocated in each region. Daily and weekly supervision and reporting at field level will be conducted by TRCS field staff and volunteers led by the Regional Coordinators of Zanzibar and Dar es Salaam; and by Regional Secretary and Chairman in Arusha. Both the HQ and field monitoring will closely involve the local government officials responsible for the coordination of disaster management activities in accordance with the government structure. Further, field staff will keep on providing weekly updates/reports about the ongoing operation to the Disaster Response Manager based at the HQ. TRCS will be responsible for providing an operational and financial report (2 months after the end of the operation). This way, IFRC East Africa Cluster can consolidate and ensure publishing within 3 months from the end of operation.

At the end of the operation, an after-action review or lessons learned workshop will be organized by TRCS with IFRC and other stakeholders of this operation, to reflect on implementation. This workshop will allow for informed planning in future operations planned and implemented by TRCS.

C. Detailed Operational Plan



Shelter

People targeted: 4,000 people³ (800 HH)

Male: 1,600

Female: 2,400

Requirements (CHF)

Needs analysis:

According to the needs assessment by TRCS branches, the immediate needs are essential household non-food items (kitchen sets (1 per HH), blankets (3 per HH) and mattresses (2 per HH)).

Population to be assisted: Through this DREF operation, 800 most affected households (4,000 people; an average of 5 people per family) will be targeted based on the following criteria: displaced families (homes damaged or submerged) and essential household NFIs damaged/lost, the elderly, pregnant and lactating women, female headed households and households with under-fives and people with disabilities.

Programme standards/benchmarks: Activities implemented under this sector will seek to meet Sphere standards

&B Output Code	Shelter Outcome 1: Communities in disaster and crisis affected areas restore and strengthen their safety, well-being and longer-term recovery through shelter and settlement solutions	<ul style="list-style-type: none"> Number of households reached with distribution of blankets, mattresses and kitchen sets Number of assessments conducted for longer term shelter needs 																
	Shelter Output 1.1: Short-term shelter and settlement assistance is provided to affected households	800 households reached with distribution of blankets, mattresses and kitchen sets																
Activities planned-Week		1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	
AP005	Assessment of shelter needs, capacities and gaps and revision of operational strategy if necessary																	
AP005	Identification of caseloads and verification of beneficiaries in different target groups – inclusion factors integrate gender, diversity and disability in the response																	
AP005	Identification of community participation modalities in program design and implementation																	
AP005	Coordination with other relevant sectors for integrated programming																	
AP005	Coordination with government and other stakeholders																	

³ According to TRCS, the female to male ratio in Tanzania is 60% of women vs 40% of men.



Water, sanitation and hygiene

People targeted: 15,862 people or 3,172 HH

Male: 6,345

Female: 9,517

Requirements (CHF)

Needs analysis: The immediate needs under this sector include essential non-food items (buckets and jerry-cans) to be distributed to direct beneficiaries of this DREF operation, i.e. 4,000 people (800 HH). However, hygiene promotion (HP) will target the overall affected communities, i.e. 15,862 people or 3,172 HHs (1,146 in Zanzibar, 2,740 in Arusha and 11,976 in Dar es Salaam). As part of HP, other items will be procured and distributed including water purification tablets, hoes, wheelbarrows, spades and rakes to community disaster preparedness and response teams.

Population to be assisted: Through this DREF operation, 800 most affected families (4,000 people; an average of 5 people per family) will be targeted with distribution of WASH related NFIs based on the following criteria: displaced families (homes damaged or submerged) and essential household NFIs damaged/lost, the elderly, pregnant and lactating women, female headed households and households with under-fives and people with disabilities. Community disaster preparedness and response teams (CDRTs) will be supported with clean-up tools to assist the affected families.

Each household will receive 2 buckets, 1 jerrycan and water purification tablets for 800 HH for one month (24,000 tabs) which will serve to purify water for drinking. In addition, 20 hoes, 5 wheelbarrows, 20 spades and 20 rakes will be procured and handed to the local RC branches to support environmental (sanitation) activities.

Programme standards/benchmarks: Activities under this sector will seek to meet Sphere standards during implementation.

P&B Output Code	WASH Outcome1: Immediate reduction in risk of waterborne and water related diseases in targeted communities										Number of households reached with hygiene promotion activities							
	WASH Output 1.1: Continuous assessment of water, sanitation, and hygiene situation is carried out in targeted communities										<ul style="list-style-type: none"> Number of assessments conducted Number of volunteers trained on WASH assessments 							
	Activities planned	Week	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16
AP026	Conduct training for 20 RC volunteers on carrying out water, sanitation and hygiene assessments																	
AP026	Conduct initial assessment of the water, sanitation and hygiene situation in targeted communities																	
AP026	Continuously monitor the water, sanitation and hygiene situation in targeted communities																	
AP026	Coordinate with other WatSan actors on target group needs and appropriate response.																	
P&B Output Code	WASH Output 1.2: Daily access to safe water which meets Sphere and WHO standards in terms of quantity and quality is provided to target population										<ul style="list-style-type: none"> Number of water purification tablets distributed Number of households reached by distribution of water purification tablets Number of people trained on safe use of water purification tablets Number of households reached with hygiene kits 							

Budget

The overall budget for this operation is CHF 196,499 as detailed in attached budget.

TANZANIA FLOODS

MDRTZ021

Budget Group		Multilateral Response	Appeal Budget CHF
500	Shelter - Relief	0	0.00
501	Shelter - Transitional	0	0.00
502	Construction - Housing	0	0.00
503	Construction - Facilities	0	0.00
505	Construction - Materials	0	0.00
510	Clothing & Textiles	38,935	38,934.78
520	Food	0	0.00
523	Seeds & Plants	0	0.00
530	Water, Sanitation & Hygiene	44,626	44,626.09
540	Medical & First Aid	0	0.00
550	Teaching Materials	0	0.00
560	Utensils & Tools	34,565	34,565.22
570	Other Supplies & Services	0	0.00
571	Emergency Response Units	0	0.00
578	Cash Disbursements	0	0.00
Total RELIEF ITEMS, CONSTRUCTION AND SUPPLIES		118,126	118,126.09
580	Land & Buildings	0	0.00
581	Vehicles	0	0.00
582	Computer & Telecom Equipment	0	0.00
584	Office/Household Furniture & Equipment	0	0.00
587	Medical Equipment	0	0.00
589	Other Machinery & Equipment	0	0.00
Total LAND, VEHICLES AND EQUIPMENT		0	0.00
590	Storage, Warehousing	0	0.00
592	Distribution & Monitoring	5,217	5,217.39
593	Transport & Vehicle Costs	4,265	4,265.22
594	Logistics Services	0	0.00
Total LOGISTICS, TRANSPORT AND STORAGE		9,483	9,482.61
600	International Staff	0	0.00
661	National Staff	0	0.00
662	National Society Staff	1,904	1,904.35
667	Volunteers	36,196	36,195.65
669	Other Staff Benefits	0	0.00
Total PERSONNEL		38,100	38,100.00
670	Consultants	0	0.00
750	Professional Fees	0	0.00
Total CONSULTANTS & PROFESSIONAL FEES		0	0.00
680	Workshops & Training	7,563	7,563.04
Total WORKSHOP & TRAINING		7,563	7,563.04
700	Travel	0	0.00
710	Information & Public Relations	9,226	9,226.09

730	Office Costs	913	913.04
740	Communications	600	600.00
760	Financial Charges	496	495.65
790	Other General Expenses	0	0.00
799	Shared Office and Services Costs	0	0.00
Total GENERAL EXPENDITURES		11,235	11,234.78
830	Partner National Societies	0	0.00
831	Other Partners (NGOs, UN, other)	0	0.00
Total TRANSFER TO PARTNERS			0.00
599	Programme and Services Support Recovery	11,993	11,992.92
Total INDIRECT COSTS		11,993	11,992.92
TOTAL BUDGET		196,499	196,499.45
Available Resources			
	Multilateral Contributions		0.00
	Bilateral Contributions		0.00
TOTAL AVAILABLE RESOURCES		0	0.00
NET EMERGENCY APPEAL NEEDS		196,499	196,499

Contact information

Reference documents



Click here for:

- Previous Appeals and updates
- Emergency Plan of Action (EPoA)

For further information, specifically related to this operation please contact:

In the National Society

- **Tanzania Red Cross Society:** Julius Kejo, Secretary General; phone: +255 655 571 888; email: kejojulius@trcs.or.tz

In the IFRC Africa

- **IFRC Country Cluster Support Team office:** Andreas Sandin, Operations Coordinator, Nairobi, phone: +254 732508060, email: andreas.sandin@ifrc.org
- **IFRC Operational Manager for Tanzania:** Lisa Zitman, DM Delegate, Eastern Africa Cluster, email lisa.zitman@ifrc.org phone: +254 733 203 004
- **Head of DCPRR, IFRC Regional Office for Africa:** Adesh Tripathee, Head of DCPRR, email: adesh.tripathee@ifrc.org, phone: +254 731 067489
- **DREF Delegate, IFRC Regional Office for Africa:** Alina Atemnkeng, email: alina.atemnkeng@ifrc.org, phone: +254 731 067 277

In IFRC Geneva

- Eszter Matyeka, Senior officer, DREF; phone +41-2-2730-4566; email: eszter.matyeka@ifrc.org

For IFRC Resource Mobilization and Pledges support:

- **IFRC Regional Office for Africa** Kentaro Nagazumi, Coordinator Partnerships and Resource Development; Nairobi; phone: +254 731984117; email: kentaro.nagazumi@ifrc.org

For In-Kind donations and Mobilization table support:

- **Logistics Coordinator,** Rishi Ramrakha, Head of Africa Region Logistics Unit; phone: +254 733888022 / Fax +254 202712777; email: rishi.ramrakha@ifrc.org

For Performance and Accountability support (planning, monitoring, evaluation and reporting enquiries)

- **IFRC** Fiona Gatere, PMER Coordinator, phone: +254 20 283 5185; email: fiona.gatere@ifrc.org

How we work

All IFRC assistance seeks to adhere to the **Code of Conduct** for the International Red Cross and Red Crescent Movement and Non-Governmental Organizations (NGO's) in Disaster Relief and the **Humanitarian Charter and Minimum Standards in Humanitarian Response (Sphere)** in delivering assistance to the most vulnerable. The IFRC's vision is to inspire, **encourage, facilitate and promote at all times all forms of humanitarian activities** by National Societies, with a view to **preventing and alleviating human suffering**, and thereby contributing to the maintenance and promotion of human dignity and peace in the world.

www.ifrc.org

Saving lives, changing minds.




The IFRC's work is guided by Strategy 2020 which puts forward three strategic aims:

1. Save lives, protect livelihoods, and strengthen recovery from disaster and crises.
2. Enable healthy and safe living.
3. Promote social inclusion and a culture of non-violence and peace




International Federation of Red Cross and Red Crescent Societies
Fédération Internationale des Sociétés de la Croix-Rouge et du Croissant-Rouge
Federación Internacional de Sociedades de la Cruz Roja y de la Media Luna Roja
الاتحاد الدولي لجمعيات الصليب الأحمر والهلال الأحمر



Tanzania: Floods

28 april 2018 • FL-2018-000043-TZA

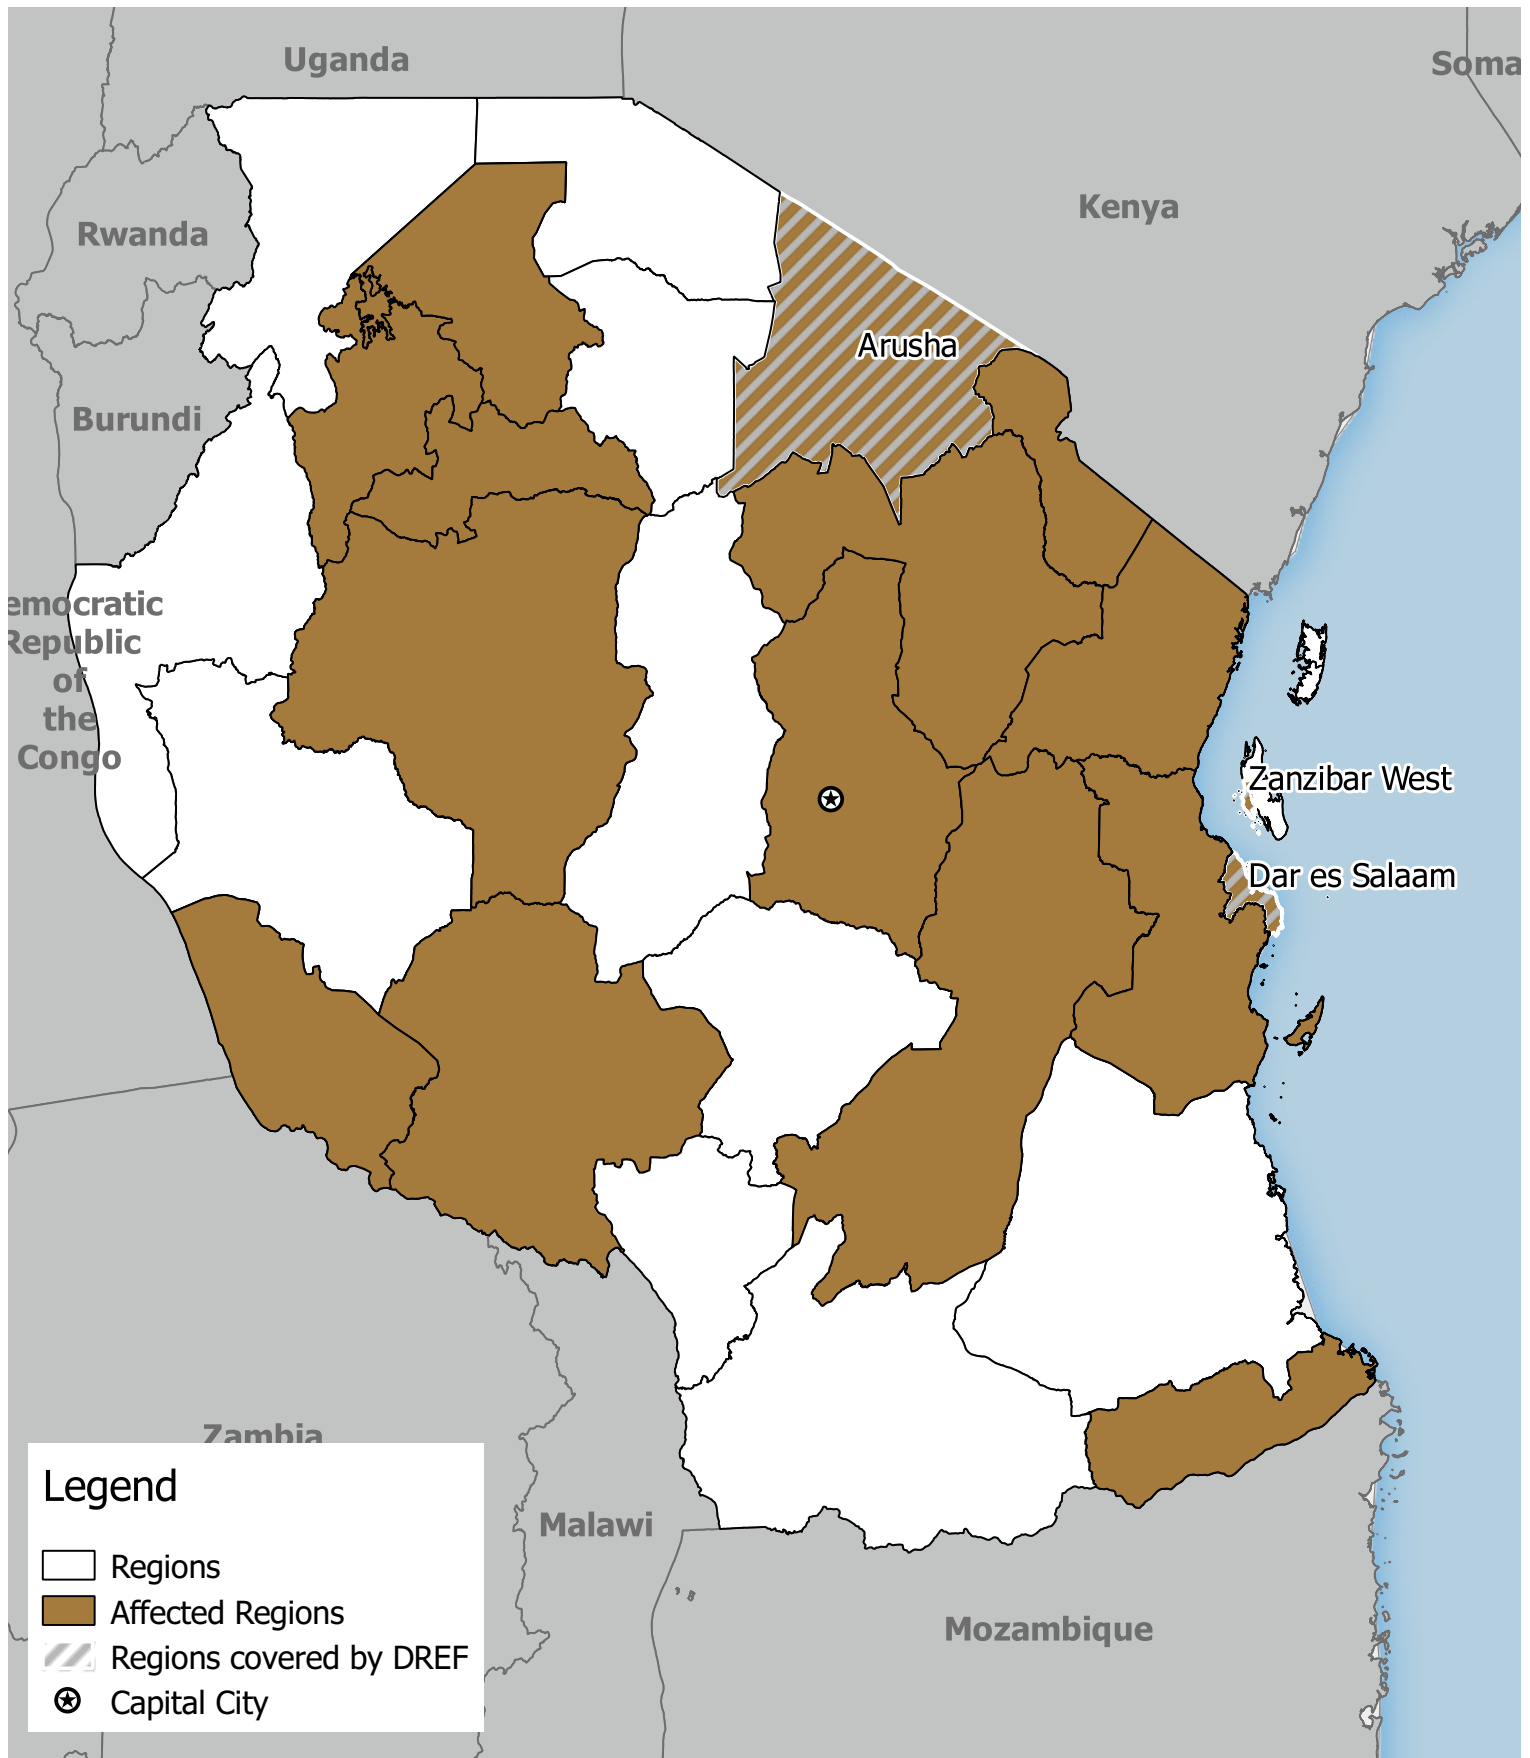

The maps used do not imply the expression of any opinion on the part of the International Federation of the Red Cross and Red Crescent Societies or National Societies concerning the legal status of a territory or of its authorities.

Map data sources: IFRC, GADM. Map produced by: IFRC Africa Regional Office, Nairobi.

0 100 200 300 400 km

