

www.ifrc.org  
Saving lives,  
changing minds.

## Emergency Plan of Action (EPoA) Nigeria: Floods

 International Federation  
of Red Cross and Red Crescent Societies

<b>DREF n° MDRNG024</b>	<b>Glide n°FL-2018-000120-NGA</b>
<b>Date of issue: 26 July, 2018</b>	<b>Operation start date: 25 July 2018</b> <b>Expected timeframe: 3 months</b> <b>Expected end date: 25 October 2018</b>
<b>Category allocated to the of the disaster or crisis: Yellow</b>	
<b>DREF allocated: CHF 253,671</b>	
<b>IFRC focal point:</b> Dr Michael Charles, Acting Head of Cluster Abuja, is Project Manager and responsible for this operation	<b>National Society Contact:</b> Alhaji Abubakar Kende: Secretary general Nigerian Red Cross Society (NRCS)
<b>Total number of people affected: 15,701</b> people affected (1,814 households)	<b>Number of people to be assisted: 5,549</b> individuals (878 households)
<b>Host National Society presence (n° of volunteers, staff, branches):</b> NRCS HQ – 10, Branches – 6 and Volunteers – 80/74.	
<b>Red Cross Red Crescent Movement partners actively involved in the operation:</b> International Federation of the Red Cross and red Crescent Societies.	
<b>Other partner organizations actively involved in the operation:</b> Ministry of Health, decentralized Government structures and Agencies.	

## A. Situation analysis

### Description of the disaster

As the rainy season is reaching its peak in Nigeria, different parts of the country have witnessed torrential rain falls in the last one month resulting in widespread flooding. On 13 July 2018, seven states of Katsina in the North West, Niger and Abuja FCT in the North Central, Yobe and Bauchi in the North East, Ogun and Ondo States in the South West have reported devastating floods affecting communities in their states.

The reports received from local Branches of Nigerian Red Cross Society (NRCS) indicate that communities in Kakurduma, Tududn Tukare Sabuwa, Mai Tambura, Tashan Buja and Gidan Tara in Katsina State were severely affected by the floods causing displacement of a total number of 3,765 people, injuries and death as well as damage to farms crops.

A total number of eight 8 people have been reported dead due to flooding in Niger State with couple others still missing. So far eight bodies have been recovered following a downpour in Rafi-Gora village and Gangare Saji in Kontagora Local Government Area of the state. The report suggests that 300 people were affected, 185 displaced, 50 casualties were recorded hospitalized.

In Bauchi the scourge left 4,984 people affected with flooding, whilst the total number displaced is at 280 households, and 7 deaths have been recorded. The flooding struck Bakin Ruwa, Rilway Kobi Street and Miri in Bauchi metropolis.

During the same period other locations of federal low cost, Yelwa, Kagadama, Yakubu Wanna Street and Fadama were affected as houses collapsed resulting in the deaths recorded.

In Ondo state about 3,200 people have been affected by the floods, a total number of 2,000 people have been displaced by the floods and 40 reported injured no deaths have been reported in the state. In flooding, approximately 15,701 people have been affected, out of which 5,549 people are reported to have displaced.

The table below indicate the numbers of affected individuals according to state:

State	Number of affected people	Number of injured people	Number of displaced people	Number of missing people	Death toll
Katsina	3,765	48	2,568	20	50
Ogun	452	13	351	0	15
Ondo	3,200	40	2,000	0	0
Bauchi	4,984	0	280	0	7
Niger	300	50	350	0	8
Abuja	3,000	20	0	0	1
<b>Total</b>	<b>15,701</b>	<b>171</b>	<b>5,549</b>	<b>20</b>	<b>81</b>

Affected families have relocated to host families or in transit sites such as schools. As the extreme weather condition continues, their current shelter solutions will not be able to meet basic requirements. The poor and fragile shelter condition is exposing children and the most vulnerable people including elderly and people with low mobility to the risks of respiratory and waterborne diseases beside congestions in the host family shelters. In Katsina, families have been moved to an already existing transit camp and this is causing a lot of pressure on existing facilities. There has been a record of few cholera cases in the transit camp as such with the increased population more there is potential of an outbreak especially if the rains persist. Seasonal forecast provided by the Nigerian Meteorological Agency (NiMet - the Government meteorological agency) predicted normal amount rainfall in 2018 in most parts of the country, even as some parts of the country may experience flood.

The NRCS is requesting for DREF support to assist the affected households to meet their basic health and hygiene, water and sanitation, as well as their food and Non-food needs. Through the DREF application, the NS is targeting to assist a total number of **5,549 individuals (878 households), 35% of total case load, who have been displaced** by the floods in the six targeted states.

## Summary of the current response

### Overview of Host National Society

The NRCS through its local branches has been working closely with the Emergency Response Agencies to conduct needs assessments in the affected communities. The volunteers have been providing support to the injured, through provision of first Aid services and psychosocial support.

As the peak of raining season is expected from July to August, quick actions must therefore be taken to reduce the potential impact of additional flood episodes and for those currently affected, to enable them to regain their dignity.

This operation will be limited to the following targets identified by a rapid assessment conducted by the Nigerian Red Cross Society (NRCS) from 16 to 19 July 2018. However, continuous assessments and monitoring of the situation will be used to adapt programming and review the plan of action of this operation.

### Overview of Red Cross Red Crescent Movement in country

The International Federation of Red Cross and Red Crescent Societies (IFRC), supports NRCS through its West Coast Country Cluster Support Team (CCST) Office in Abuja. As such, the Abuja CCST is providing necessary technical support in developing a plan of action and liaising with the Africa Region team to apply for a DREF allocation. This is to ensure that NRCS can carry out priority actions for the benefit of vulnerable people affected by the floods. IFRC has a liaison team in Nigeria, which continuously provide support to NRCS in disaster management, development programmes and support to organizational development. The NRCS is currently implementing a One International Appeal which is addressing the needs of the households affected by the conflict in the North-East Nigeria targeting the two states of Yobe and Adamawa.

International Committee of the Red Cross - ICRC is physically present in the country as a delegation office is domicile in Abuja and sub delegations in three states (Port Harcourt – South, Jos – North central, Yola – North Eastern) besides offices in Maiduguri, Kano and Biu) Implementing full fledged response around conflict interventions.

### Overview of non-RCRC actors in country

The State Emergency Management Agency (SEMA) in some states have supported in the search and rescue operations of the NRCS. The Police, Road Safety Corps have also supported in the search and rescue as well as casualty evacuations to the hospitals

Jama'atul Bidiawa Ikamatus Sunnah (JIBWIS - a faith base organization across the country) have supported the affected beneficiaries in Katsina with clothing materials.

The President His Excellency Muhammadu Buhari was in Azare - Bauchi on July 20, 2018 to console the affected people after the storm and flooding that occurred in the state. The Vice President of Nigeria also visited the affected families to appreciate the extent of the and promised to relocate victims to better place that is suitable location for the victims in Katsina. But no commitment was made on families with a deceased member as a result of this disaster.

The state government in Katsina and NEMA in Bauchi have made some effort in providing clothing materials, food and NFIs to the victims of flood which is never targeted properly due to poor assessment, coordination and targeting.

## Needs analysis, targeting, scenario planning and risk assessment

The rapid needs assessment conducted by the NRCS volunteers from 16 June to 17 July 2018, confirmed the following:

Some of the wounded individuals were immediately taken to the hospital after a First Aid intervention was carried out by the NRCS volunteers' immediate health centers in the neighborhood were also completely flooded. Similarly, some members of bereaved families affected by this situation were served with psychological First Aid. Support provided by NEMA and SEMA some local NGOs does not cover all the affected areas.

In some communities across the state there is serious disruption as the flooding water washed away properties, livestock, farm lands, access roads, water ways and flooded almost all houses and water is still seen to be stagnant.

Water distribution networks have been affected in urban centers and water points are completely flooded especially in rural communities in the states. Outbreaks of waterborne diseases such as cholera and an increase in cases of malaria are feared. Most of the affected populations have lost everything including food and non-food stocks.

Weather forecasts continue to be unpredictable with large fluctuations in every single day. The new weather forecasts announced by the authorities will be detrimental, adding uncertainty to an already precarious situation. Detailed assessments continue on the ground, in the affected local government authorities (LGAs) across the states in the country. The data collected by Red Cross volunteers will refine the content of the response.

Therefore, to initiate activities, this DREF will support in the following areas:

- ✓ Health priority actions;
- ✓ WASH activities;
- ✓ Provision of minimum means of subsistence to allow the affected families access to food and non-food items. As the affected population resides in both rural and urban areas, a socio-economic and market assessment will determine the minimum package to be supported for each selected household, so that cash is used to respond in this sector.
- ✓ Volunteers capacity will be strengthened through refresher trainings for cash distribution (to support families);
- ✓ Prevention of waterborne diseases and orientation training for community engagement.
- ✓ A continuous assessment of the needs of affected households will be conducted to adjust actions undertaken through this operation.

## Target Beneficiaries

This DREF allocation will target all the seven risk affected areas as NRCS has conducted assessments this far. Thus, and as per indications in Table 1 resulting from the ongoing assessment, a total of 778 households (5,449 individuals) will benefit from the operation as direct beneficiaries. Hence the focus is on the displaced individuals.

However indirect beneficiaries will also be reached through awareness raising and education which will be provided by the volunteers in the communities.

Analysis of ongoing assessment data and real-time monitoring of the situation will refine the priorities and adjustment of magnitude of the operation would be envisioned.

### Scenario planning (300 words)

The below table describes possible scenarios and how they will be addressed by NRCS:

<b>Best case scenario</b>	<b>Most likely scenario</b>	<b>Worst case scenario</b>
The rains stop, no more people are affected, and no secondary effects are suffered e.g. outbreak of diseases in the current affected areas or other parts of the country.	The rains continue through July/October but no more than 50mm in 24 hours in any part of the currently affected areas or other parts of the country.	The rains continue heavily through July/October, with episodes of more than 50mm in 24 hours in any part of the current affected areas or other parts of the country, resulting in massive displacement of people and destruction of infrastructure and assets. There is a possibility of having gastroenteritis among affected population
<b>NRCS Response:</b> Limited to the current DREF operation and no more than four weeks response.	<b>NRCS Response:</b> Limited to the current DREF operation, with continued alert and on standby. On the side-line, engaging with communities for early warning, preparedness and disaster risk reduction measures.	<b>NRCS Response:</b> Revision of the current DREF operation through an Operations update to widen the scope of intervention, with possible change of strategy, increased timeframe and possibly a request for a second allocation or proceed to a large-scale operation through an application for an emergency appeal.

### Operation Risk Assessment

The operation includes a provision of relief and basic support through cash distribution and transfer. There is a likelihood that targeted families may misuse the funds since the Cash Based Intervention (CBI) is unconditional. There is need to provide education to the communities on the CBI before the actual disbursement and also to ensure strong targeting so that the right people are supported through the operation. A risk assessment for CBI as well as a security assessment will be done before the CBI to inform the processes. In addition, the daily updates from the meteorological agency forecast increased rainfall across West Africa including Nigeria, compared to last year for the period -- July to October. This could worsen the situation for already affected persons or create new needs amongst the persons who were not severely affected by the current floods. The continued floods might make the targeted areas inaccessible and pose risk to the operation.

## B. Operational strategy

### Overall objective

The overall objective of the DREF operation was **to ensure that the immediate Food and basic needs, water, sanitation, and hygiene (WASH), and health needs of 5,549 flood-affected individuals were met through the provision of essential emergency relief assistance.**

Focus areas in Nigeria will be in North- West Nigeria focusing on the 6 states of Katsina, Bauchi, Ondo, Ogun, Niger and Abuja.

## Proposed strategy

To meet the above stated objective, NRCS intends to implement the below actions:

**1. Provision of Food and basic needs:** The provision of livelihoods and basic survival means (non-food, food, and water) will target **878 most vulnerable households (5,549 people)** with clear evidence that they have suffered the effects of the flood and have been displaced and in need of urgent support of basic needs. The targeting criterion will be confirmed in agreement with community members and main stakeholders. To help these vulnerable populations regain their dignity, **Cash Based Interventions (CBI)** will be the transfer modality that will be adopted to cover the essential means of subsistence, if feasible, allowing the affected families to get needed food and NFIs. A **rapid market assessment, price monitoring data collection, Financial Service Provider assessment / selection and risk assessment / analysis** will be carried out to ensure that all elements are well considered. A baseline survey will also be conducted after the selection of the beneficiaries before the actual first distribution is done. The definition of the minimum content to be considered per target household will be determined based on a socio-economic survey and the validated recommendations of stakeholders and beneficiaries. The CBI value per household is pegged at 30,000 NGN i.e. (CHF 83) which is in line with the minimum food basket on use in Nigeria. This will be unconditional CBI however education on how to use the funds will be provided to the families. After the actual distribution, a post monitoring distribution (PDM) will be conducted and a report produced and shared.

**2. Health:** To ensure that the immediate health needs of the affected people are met, NRCS, through this DREF operation intends to provide health and first aid services follow-up and care. Psychological care will equally be addressed as needed, under this component. A total of **60 first-aid kits (10 per state)** will be procured to ensure that volunteers have the necessary equipment to attend to the injured. The NS will also conduct a refresher training on First Aid and PSP training for the volunteers so that they are fully prepared to support the affected communities. The NS will procure a total number of **1,756 mosquito nets i.e. 2 per household** to help prevent the spread of malaria. IEC material for the affected communities will be printed to help educate the families of health and hygiene issues. A total **number of 6,000 pieces of IEC material** will be procured and distributed to the affected communities during the hygiene promotion.

**3. Water, Sanitation and Hygiene:** To prevent waterborne diseases, awareness (hygiene promotion) and sanitation (clean up) campaigns in affected locations need to be conducted, especially since it is still the rainy season. Activities under this sector will focus on waste management and the cleaning of gutters/public sanitation facilities. As the Government is planning to relocate some of the affected households to a temporary site in Katsina and other location, an assessment will be carried out in transit sites and health centers to analyze and respond to the needs in Household water treatment and safe storage activities will be considered only after a detailed assessment of needs, priorities and relevance in urban and rural areas affected by the floods. The NS will procure a total number of 878 bucket and 878 buckets to ensure proper and safe storage of water. NS will procure a total number of 10 boxes of aqua tablets to support the families so that they have access to clean and safe water. To avoid the spread of diarrheal disease and avoid open defecation in transit camps, the NS will procure materials and set up 10 latrines (5 for women and 5 for men) as well as install 10 hand washing facilities which will be set up in Katsina transit camp.

To ensure the safety of the staff and volunteers involved in the operation, they will all be identified and will wear bibs or T - shirts with the Red Cross emblem. Field movement and planning will be validated by the central level coordination mechanism before any execution. In addition, all volunteers involved in this operation will be covered by an individual IFRC insurance provided for through the operation.

## Lesson learnt Workshop

A lessons-learnt workshop will also be organized towards the end of the operation, to ensure that volunteer feedback is obtained, and any strength highlighted, or weaknesses identified, to address these and inform future planning. In addition, the lessons learnt workshop will serve to collect data for a case study on the CBI implementation. This too, will serve to inform future CBI planning by the NRCS. A report of this workshop will be produced and shared with all relevant actors.

## Operational support services

### Human resources

The operation is expected to involve 70 voluntary members of the NRCS 10 in each targeted state and up to 10 National Society staff members. The breakdown of the human resources is as follows:

- 10 NS staff (1 CBI, 1 DM/CEA, 1 Wash, 1 Health, 1 PMER, 1 logistician, 1 Finance, 1 HR, 1 IT, 1 communication staff).
- Seven (7) team leaders. In this specific case, NS expressed need to have an additional supervisor to cap the team of NS volunteers and supervisors.
- 70 trained volunteers

To support WASH and health and cash-based activities under the DREF, two RDRTs for WASH/Health and Cash based intervention profile will be deployed for a period of 2 months. The Abuja CCST will provide support to the NS through its various departments i.e. logistics, HR, finance, PMER and also a CBI delegate will work closely with the NS to ensure all relevant systems for a successful operation are in place.

### Logistics and Supply Chain

Local procurement will be done by the NRCS in accordance with the operation's requirements, and aligned to the IFRC's logistics standards, processes and procedures. The IFRC logistics Delegate based in Abuja will provide all the technical guidance and support to the NS to ensure compliance to IFRC standards whilst at the same time building the capacity of the NS logistics unit. The National Society Warehouses across the country are intact with some stocks within, if required warehouse space will be used to support the operation.

### Finance and Administration

Through its Finance Department, the IFRC will be tasked with the role of providing necessary support to the operation to review and validate budgets, bank transfers, technical assistance to the National Society regarding expense justification procedures and the review and validation of operational invoices.

### Security

Security management as part of this operation will be based on the RCRC Fundamental Principles and humanitarian values. In addition, the following actions related to security will be implemented:

- Regular security updates will be organized, and information disseminated;
- Real time monitoring of field activities through the NRCS information management system;
- The use of other IT means of contact system to ensure communications during follow-up missions;
- All staff and volunteers must have undergone the Stay Safe security course and abide by the Code of conduct before starting their mission.

**Community Engagement and Accountability**

NRCS has previous experience with community engagement approaches and activities as part of the emergency response of flood in the past, continuous support of immunization days beside other projects. Ebola Prevention Project (2015-2016).

The national society has two focal points who attended trainings on community engagement and accountability / communication with beneficiaries' approach. The National Society will integrate community engagement and accountability throughout the response, with the support of the IFRC, which will provide additional technical support through experienced resource available at CCST.

Community Engagement and Accountability activities and approaches will be integrated into the different areas of the response to ensure that:

- Communities are informed and know how to access Red Cross services, with information shared through reliable and preferred communication channels, such as face-to-face meetings, participatory sessions, working with community leaders and influential people who are trusted by communities,
- Communities are given opportunities to participate in the operation and influence decisions made, to contribute to greater community ownership over the operation and improve the quality of the response;
- Systems for collecting community feedback, complaints and perceptions are established;

**Planning, monitoring, evaluation, & reporting (PMER)**

The NRCS through its PMER department, will oversee all operational, implementation, monitoring and evaluation, and reporting aspects of the operation in the flood affected provinces through its country-wide network of branches and volunteers. The responsibility for day-to-day monitoring of the operation will be with NRCS provincial branches but supervised by the NRCS headquarters to ensure appropriate accountability, transparency and financial management of the operation. Operation updates will be issued to report progress of the implementation. A lesson learned workshop will be conducted towards the end of operation to draw lesson from the operation and a report of the workshop will be produced and shared widely. IFRC CCST office in Abuja through the PMER delegate will also will provide technical support in programme management to ensure that the operational goals are met. The IFRC CEA delegate will also provide support to ensure that complaints mechanisms are set up for the CBI so that feedback from the communities is received.





## Health

**People targeted: 5,449 people (878 Households)**

Male: 2,826

Female: 2,737

**Requirements (CHF): 52,975**

**Needs analysis:** With the destruction of homes in certain localities, the Red Cross will participate, alongside the authorities, in search/rescue and relief operations, as well as provide psychological support and epidemiological surveillance. Indeed, difficult access to health and care because of some flooded health centers, as well as the risk of proliferation of water-related diseases heightens the need for immediate health care for the affected people. In addition, most of the affected households suffered psychological stress due to loss of life of family members and property.

**Population to be assisted:** 5,449 people (878 households), including men, women, children and the elderly both in Katsina, Bauchi, Niger, Ogun, Ondo and Abuja.

**Programme standards/benchmarks:** This operation will seek to meet Sphere and WHO standards under this section.

P&B Output Code	Health Outcome 1: Vulnerable people's health and dignity are improved through increased access to appropriate health services.																
	Health Output 1.1: Communities are supported by NS to effectively detect and respond to infectious disease outbreaks	<i># of people reached with community-based disease prevention and health promotion programming</i> <i># of volunteers trained on communicable disease surveillance</i>															
	Activities planned Week / Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16
AP021	Train 35 volunteers and NS staff on communicable disease surveillance in coordination with MoH and District Health Offices																
P&B Output Code	Health Output 1.2: Communities are supported by NS to effectively respond to health and psychosocial needs during an emergency	<i># of people reached by First Aid services</i> <i># of mosquito nets distributed</i>															
	Activities planned Week / Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16
AP022	Mobile team members selection																
AP022	Procure 60 emergency first aid kits																
AP022	Refresher and orientation training for mobile team on first aid																
AP022	Support target population with first aid activities																
AP022	Procure and distribute 1,756 Mosquito nets																
AP022	Procure 6,000 IEC materials																
P&B Output	Health Output 1.5: Communities are supported by NS to effectively respond to health and psychosocial needs during an emergency	# people reached with PSS															

Code	Activities planned Week / Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16
AP023	Refresher and orientation training for mobile team on PSP																
AP023	Support target population with Psychosocial support																



## WASH

**People targeted: 5,449 (878 households)**

Male: 2,826

Female: 2,737

**Requirements CHF: 25,142**

**Needs analysis:** To prevent waterborne diseases, hygiene promotion and sanitation campaigns in affected locations need to be conducted, especially since it is still the rainy season. Software activities will be conducted as integral part of the community engagement and accountability techniques.

**Population to be assisted: 5,549 (878 households)** will directly benefit from this activity in Katsina, Bauchi, Ogun, Ondo, Niger and Abuja.

**Programme standards/benchmarks:** Sphere the activities will seek to meet.

P&B Output Code	WASH Outcome1: Vulnerable people have increased access to appropriate and sustainable water, sanitation and hygiene services																
	WASH Output 1.1: Communities are provided by NS with improved access to safe water.	<i># households reached with awareness raising activities on improved treatment and safe use of wastewater # of households supported with water buckets and water treatment tablets</i>															
	Activities planned Week / Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16
AP026	Conduct initial assessment of the water, sanitation and hygiene situation in targeted communities																
AP026	Continuously monitor the water, sanitation and hygiene situation in targeted communities																
AP026	Coordinate with other WatSan actors on target group needs and appropriate response.																
AP026	Procure water treatment tablets																
AP026	Procure and distribute water buckets																
AP026	Procurement and distribution of Jerry cans																
P&B Output Code	WASH Output 1.3: NS promote positive behavioral change in personal and community hygiene among targeted communities.																
	Activities planned Week / Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16





## Budget

The overall budget for this operation is CHF 253,671 as seen in attached budget.

	Budget Group	Multilateral Response	Appeal Budget CHF
500	Shelter - Relief	0	0
501	Shelter - Transitional	0	0
502	Construction - Housing	0	0
503	Construction - Facilities	0	0
505	Construction - Materials	0	0
510	Clothing & Textiles	10,536	10,536
520	Food	0	0
523	Seeds & Plants	0	0
530	Water, Sanitation & Hygiene	7,650	7,650
540	Medical & First Aid	11,900	11,900
550	Teaching Materials	6,280	6,280
560	Utensils & Tools	34,342	34,342
570	Other Supplies & Services	0	0
571	Emergency Response Units	0	0
578	Cash Disbursements	81,336	81,336
	<b>Total RELIEF ITEMS, CONSTRUCTION AND SUPPLIES</b>	<b>152,044</b>	<b>152,044</b>
580	Land & Buildings	0	0
581	Vehicles	0	0
582	Computer & Telecom Equipment	0	0
584	Office/Household Furniture & Equipment	0	0
587	Medical Equipment	0	0
589	Other Machinery & Equipment	0	0
	<b>Total LAND, VEHICLES AND EQUIPMENT</b>	<b>0</b>	<b>0</b>
590	Storage, Warehousing	0	0
592	Distribution & Monitoring	0	0
593	Transport & Vehicle Costs	13,783	13,783
594	Logistics Services	0	0
	<b>Total LOGISTICS, TRANSPORT AND STORAGE</b>	<b>13,783</b>	<b>13,783</b>
600	International Staff	32,000	32,000
661	National Staff	0	0
662	National Society Staff	10,334	10,334
667	Volunteers	3,080	3,080
669	Other Staff Benefits	0	0
	<b>Total PERSONNEL</b>	<b>45,414</b>	<b>45,414</b>
670	Consultants	0	0
750	Professional Fees	3,000	3,000
	<b>Total CONSULTANTS &amp; PROFESSIONAL FEES</b>	<b>3,000</b>	<b>3,000</b>
680	Workshops & Training	14,476	14,476
	<b>Total WORKSHOP &amp; TRAINING</b>	<b>14,476</b>	<b>14,476</b>
700	Travel	5,765	5,765
710	Information & Public Relations	1,000	1,000
730	Office Costs	990	990
740	Communications	1,617	1,617

760	Financial Charges	100	100
790	Other General Expenses	0	0
799	Shared Office and Services Costs	0	0
	<b>Total GENERAL EXPENDITURES</b>	<b>9,472</b>	<b>9,472</b>
		0	0
830	Partner National Societies	0	0
831	Other Partners (NGOs, UN, other)	0	0
	<b>Total TRANSFER TO PARTNERS</b>	<b>0</b>	<b>0</b>
599	Programme and Services Support Recovery	15,482	15,482
	<b>Total INDIRECT COSTS</b>	<b>15,482</b>	<b>15,482</b>
	<b>TOTAL BUDGET</b>	<b>253,671</b>	<b>253,671</b>
	<b>Available Resources</b>		
	Multilateral Contributions		0
	Bilateral Contributions		0
	<b>TOTAL AVAILABLE RESOURCES</b>	<b>0</b>	<b>0</b>
	<b>NET EMERGENCY APPEAL NEEDS</b>	<b>253,671</b>	<b>253,671</b>

## Contact information

For further information specifically related to this report, please contact:

### For Nigeria Red Cross Society (NRCS)

- Abubakar Kende, Secretary General NRCS; Tel: +234 8089595095; email: [abukende@yahoo.com](mailto:abukende@yahoo.com) / [abukende@gmail.com](mailto:abukende@gmail.com)

### IFRC Country Cluster Office, Abuja:

- Michael Charles, Acting Head of Cluster, IFRC West Coast Multi-Country Cluster Support Office for West Africa; email: [micheal.charles@ifrc.org](mailto:micheal.charles@ifrc.org)

### IFRC office for Africa Region:

- Adesh Tripathee, Head of Disaster Crisis Prevention, Response and Recovery Department, Nairobi, Kenya; phone +254 731067489; email: [adesh.tripathee@ifrc.org](mailto:adesh.tripathee@ifrc.org)
- Khaled Masud Ahmed, Regional Disaster Management Delegate, Tel: +254 (0) 731067286, email: [khaled.masud@ifrc.org](mailto:khaled.masud@ifrc.org)

### In IFRC Geneva

- Eszter Matyeka, Senior Officer, Disaster Relief Emergency Fund (DREF); email: [eszter.matyeka@ifrc.org](mailto:eszter.matyeka@ifrc.org)

### For IFRC Resource Mobilization and Pledges support

- IFRC Africa Regional Office for resource Mobilization and Pledge: Kentaro Nagazumi, Head of Partnership and Resource Development, Nairobi, email: [kentaro.nagazumi@ifrc.org](mailto:kentaro.nagazumi@ifrc.org); phone: +254 202 835 155

### For In-Kind donations and Mobilization table support:

- IFRC Africa Regional Office for Logistics Unit: Rishi Ramrakha, Head of Africa Regional Logistics Unit, email: [rishi.ramrakha@ifrc.org](mailto:rishi.ramrakha@ifrc.org); phone: +254 733 888 022

### For Performance and Accountability support (planning, monitoring, evaluation and reporting enquiries)

- IFRC Africa Regional Office: Fiona Gatere, PMER Coordinator, email: [fiona.gatere@ifrc.org](mailto:fiona.gatere@ifrc.org) , phone: +254 780 771 139




International Federation of Red Cross and Red Crescent Societies  
 Fédération internationale des Sociétés de la Croix-Rouge et du Croissant-Rouge  
 Federación Internacional de Sociedades de la Cruz Roja y de la Media Luna Roja  
 الاتحاد الدولي لجمعيات الصليب الأحمر والهلال الأحمر



## NIGERIA: Floods

26 July 2018 • FL-2018-000120-NGA

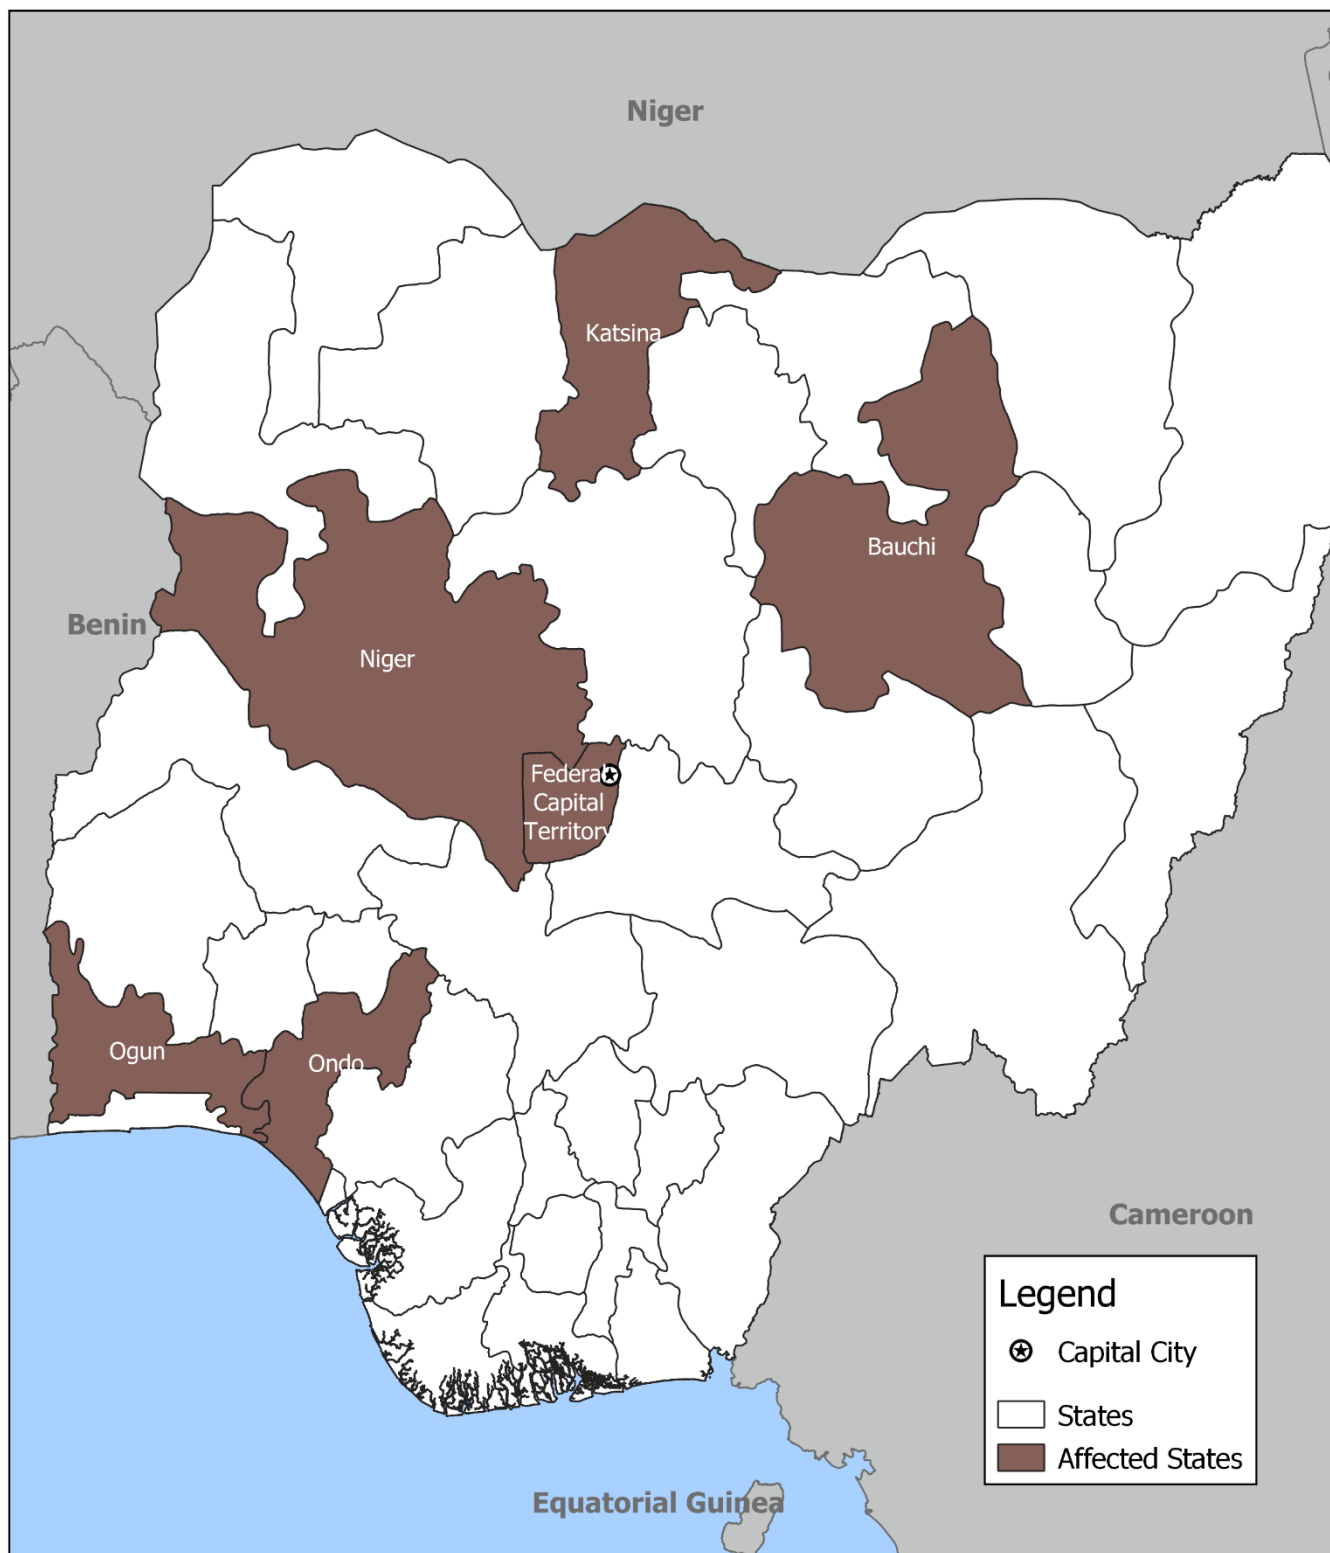

The maps used do not imply the expression of any opinion on the part of the International Federation of the Red Cross and Red Crescent Societies or National Societies concerning the legal status of a territory or of its authorities.  
 Map data sources: IFRC, GADM. Map produced by: IFRC Africa Regional Office, Nairobi.
