

www.ifrc.org
Saving lives,
changing minds.

Emergency appeal operations update

Philippines: Tropical Storm Tembin

 International Federation
of Red Cross and Red Crescent Societies

Emergency appeal n° MDRPH026	GLIDE n° TC-2017-000182-PHL
EPoA update n° 4: 15 February 2019	Timeframe covered by this update: 19 December 2017 to 21 January 2019
Operation start date: 19 December 2017	Operation timeframe: 15 months and ends on 31 March 2019
Overall operation budget: CHF ¹ 1,194,765	DREF amount allocated: CHF 313,498
N° of people being assisted: 28,006	
Red Cross Red Crescent Movement partners currently actively involved in the operation: PRC is working with the International Federation of Red Cross and Red Crescent Societies (IFRC) in this operation. PRC and IFRC are also coordinating with the International Committee of the Red Cross (ICRC) on this operation. German Red Cross, Turkish Red Crescent and Qatar Red Crescent are bilaterally supporting PRC in this operation. There are nine Partner National Societies with presence in the Philippines (more details below).	
Other partner organizations actively involved in the operation: A number of Government, United Nations (UN) and non-governmental actors are or were responding to this disaster. These include: <ul style="list-style-type: none"> • Government agencies: National Disaster Risk Reduction and Management Council (NDRRMC), Department of Social Welfare and Development (DSWD) and Local Government Units; • UN agencies: UN Office for the Coordination of Humanitarian Affairs (OCHA), United Nations International Children's Emergency Fund (UNICEF) and World Food Programme (WFP); • Other international organizations & NGOs: Action Against Hunger (ACF), International Organization for Migration (IOM), Médecins Sans Frontières (MSF), Oxfam, Plan International and Save the Children. 	

Appeal History

- **16 December 2017:** Tropical Storm Kai-Tak makes landfall over San Policarpio. Eastern Samar. PRC mounts a response to deliver immediate assistance to affected people.
- **16 to 20 December:** As PRC continues to deliver immediate assistance to people affected by Tropical Storm Kai-Tak, a new Low-Pressure Area (LPA) forms, gains strength and turns into a tropical depression (TD) and later becomes Tropical Storm Tembin.
- **21 December:** PRC enhances its preparedness measures for approaching Tropical Storm Tembin, and dispatches non-food items (NFIs) for 1,000 families from its Cebu regional warehouse to Mindanao. IFRC allocates CHF 31,764 from its Disaster Relief Emergency Fund (DREF) to support the National Society's readiness measures.
- **22 to 23 December:** Tropical Storm Tembin makes landfall in Cateel, Davao Oriental, then tracks west over the provinces of Lanao del Norte, Misamis Oriental, Misamis Occidental and Zamboanga del Norte.
- **25 December:** IFRC launches an Emergency Appeal for 2,836,944 Swiss francs, including a DREF start-up loan of CHF 313,498, to support the PRC in meeting the humanitarian needs of 20,000 people.
- **20 January 2018:** [Operations Update no.1](#) is published.

¹ CHF = Swiss francs.

- **24 April:** IFRC issues a [revised Emergency Appeal](#) for CHF 1,274,468 to assist 25,000 people over 12 months. Based on the validated financial report, the EA is currently seeking CHF 1,194,765 to assist 26,069 people over 12 months.
- **18 July:** [Operations Update no.2](#) is published.
- **25 October:** [Operations Update no.3](#) is published.

A. SITUATION ANALYSIS

Description of the disaster

On 22 December 2017, Tropical Storm Tembin (locally known as Vinta) hit Mindanao island in the Philippines, before making a second landfall on 23 December on Palawan island. The tropical storm exited the Philippine Area of Responsibility on 24 December. The storm brought heavy rainfall that caused widespread flooding as major rivers breached their banks. The heavy rain also caused flash floods and landslides in high lands and mountain sides across northern Mindanao and southern Palawan. Northern Mindanao is particularly prone to flash floods and landslides.

[DSWD](#) Disaster Response Operations Monitoring and Information Center reported that 871,757 people (184,278 families) were affected in 1,215 barangays across eight regions and 24 provinces, with 44 confirmed deaths (129 more pending validation) and 155 people missing. In addition to causing the loss of human lives, Tembin substantially impacted shelter, livelihoods, water, sanitation and hygiene (WASH) facilities and caused damage to critical infrastructure including roads, bridges and power transmission lines. Damages to agriculture and infrastructure were calculated at 2.1 billion Philippine pesos (PHP) or around CHF 38.9 million.

Summary of current response

Overview of Host National Society

Through the PRC Operation Centre, which functions 24/7, as part of its standard operating procedures, all PRC chapters in the forecasted storm-affected areas were alerted to prepare for preemptive evacuations and emergency response. The national headquarters of PRC and chapters closely coordinated with the national, regional, provincial, municipal, and city disaster risk reduction management offices (DRRMOs) and other counterparts. PRC also participated in the NDRRMC pre-disaster risk analysis and preparedness planning meetings.

Before TS Tembin made landfall, with support from the IFRC, PRC dispatched a standard set of non-food items to Mindanao for 1,000 families. Immediately after landfall, response teams (143 community-based Red Cross volunteers and chapter-based Red Cross action teams) were deployed for local response. National Disaster Response Team (NDRT) members including Water Search and Rescue (WASAR) teams were also deployed. PRC mobilized WASH hubs based in Mindanao with capacity for water treatment, storage and transporting. Coordination, assessment and response teams were deployed from the national headquarters to augment the chapter teams.



Beneficiaries from the indigenous group, the Matigsalug, use a makeshift raft from bamboo and banana trunks to transfer the corrugated iron sheets that will be used as roofing for households the PRC is supporting with shelter assistance. Access and transportation of shelter materials to the remote villages affected by Tembin is one of the challenges for the PRC recovery team and the families they are supporting, giving way to innovative but practical solutions to transfer the shelter materials from the supplier to the relocation sites. *(Photo: Maryjoy Evalarosa/IFRC)*

Details of response by PRC to the affected population

Area of focus	Service/support provided	Accomplishment	Unit
Shelter	Clothing	278	Families
	Kitchen Set (Assorted)	17	Families
	Sleeping Kit (Blanket)	4,217	Families
	Sleeping Kit (Mat)	4,249	Families
	Sleeping Kit (Mosquito Net)	4,027	Families
	Tarpaulin	4,077	Families

Livelihoods and basic needs	Bread	300	Individuals
	Cash for Relief (PHP3,000)	1,818	Families
	Food Packs	5,096 ²	Families
	Hot Meals	10,218	Individuals
Health	BP Taking	750	Individuals
	First Aid	31	Individuals
	PSP	2,339	Individuals
	Rescued/Assisted	764	Individuals
	Transported	1	Individual
	Welfare Desk	14	Desk
WASH	Bottled Water	244	Individuals
	Hygiene Kit	4,739	Families
	Hygiene Kit (Assorted)	17	Families
	Hygiene Promotion	28,006 ³	Individuals
	Jerry Can (10L)	4,249	Families
	Jerry Can (20L)	116	Families
	Water	26,069	Individuals
	Water Bladder 10K	1	Unit
	Water Bladder 5K	1	Unit
Protection, gender and inclusion	I am Alive Call	26	Individuals
	Tracing	38	Individuals
Assets deployed	Deployed teams for WASAR, assessment, welfare, health, WASH and relief		
	Two units of water tankers deployed in Cagayan de Oro and Lanao del Sur		
	Two units of water bladder (5,000 litres) installed in Cagayan de Oro		

For the map of PRC response, click [here](#)

Details of response by PRC to the affected population for the recovery phase to date

Area of focus	Service/support provided	Accomplishment	Unit
Shelter	Shelter assistance	370	Households
Livelihoods	Household livelihoods assistance	254	Households
	Community-managed livelihood programme	3	Associations
WASH	Latrine	254	Households
	Water sources/supply	3	Locations
DRR	CBDRRM	8	Communities

For the recovery phase, IFRC Appeal is supporting PRC on its implementation in Bukidnon and Zamboanga del Norte.

Overview of Red Cross Red Crescent Movement in country

PRC works with the IFRC, ICRC and nine Partner National Societies in the country, namely American Red Cross, Australian Red Cross, Canadian Red Cross, Finnish Red Cross, German Red Cross, The Netherlands Red Cross, Norwegian Red Cross, Spanish Red Cross, and Qatar Red Crescent Society. PRC ensures that all Movement partners are fully informed about the situation and plans.

The ICRC is also an active partner in the Philippines in line with its mandate to protect and assist people affected by armed conflict and other situations of violence. It cooperates closely with the PRC on various protection, assistance and prevention activities in the Mindanao region. Marawi City and surrounding areas affected by the conflict in 2017 have also been affected by the TS Tembin. Communications with ICRC on the operation are held at country level.

IFRC has a country office in the Philippines, which is supporting PRC in planning of this operation and in coordination with stakeholders. IFRC is closely monitoring the situation and has mobilized staff to provide technical support to PRC as well as coordination with other agencies via the Humanitarian Country Team (HCT).

For this operation, German Red Cross, Turkish and Qatar Red Crescent Societies bilaterally supported PRC during the relief phase in Lanao del Norte, Lanao del Sur and Palawan.

Movement Coordination

The IFRC country office is supporting PRC in disseminating updates to Movement partners with in-country presence and coordinating with the IFRC Asia Pacific Regional Office (APRO) in Kuala Lumpur in accordance with the IFRC Emergency Response Framework. The country office is also in close contact with ICRC on any security-related considerations. PRC convened a coordination meeting on 24 December, in which all Movement components were

² 3,947 families with (2-3 food ration) and 1,149 families with assorted food packs.

³ PRC WASH Services update as of 3 October 2018.

represented. In addition to coordinating with Movement partners, PRC has assigned dedicated personnel to represent the National Society in NDRRMC meetings.

Overview of non-RCRC actors in country

Coordinating with the authorities

As auxiliary to the public authorities, PRC maintains a strong relationship with government bodies through participation or collaboration with (i) the NDRRMC; (ii) the provincial, municipal and barangay disaster risk reduction and management councils; and (iii) the local government units defined in the Disaster Risk Reduction and Management Act from 2010.

PRC participates in NDRRMC meetings and coordinates with the Department of Social Welfare and Development (DSWD), Department of Health, and the NDRRMC at regional, provincial, municipal and barangay levels. PRC has assigned dedicated personnel who continue to represent the National Society in NDRRMC meetings. PRC is also participating in the NDRRMC Pre-Disaster Risk Analysis (PDRA) meetings and preparedness planning meetings.

Inter-agency coordination

At country level, PRC and IFRC consistently participate in meetings of the Humanitarian Country Team (HCT) held both during disasters and non-emergency times. PRC and IFRC are involved in relevant government-led cluster information sharing, planning, and analysis at all levels, while IFRC supports PRC coordination efforts through representation in other relevant clusters as required.

Needs analysis and scenario planning

Needs analysis

For this section, kindly refer to the [revised Emergency Plan of Action \(EPoA\)](#) and [Operations Update No.2](#).

Targeting

The targeting analysis is held in the [revised Emergency Plan of Action \(EPoA\)](#) and [Operations Update No.2](#).

Operation Risk Assessment

Some of the areas likely to be affected by the tropical storm are known to have presence of armed non-state actors (ANSAs) and as such is of significant security concern. Given the context, there will be a need to coordinate possible interventions with all Movement components – PRC, ICRC and IFRC – and to ensure compliance with security protocols. Constraints relating to access due to landslides, flash floods, flooded roads and debris such as fallen trees are likely to be faced in the response. PRC national headquarters will coordinate closely with its chapters in the affected provinces for ocular surveys before teams are deployed for assessments and immediate assistance.

Multiple areas in Mindanao are known to have presence of armed non-state actors (ANSAs) including the operational areas in Bukidnon and Zamboanga del Norte. Given the context, close coordination with the ICRC, local government units and local leaders is undertaken to ensure ease and safety for field movement.

B. OPERATIONAL STRATEGY

Proposed strategy

This operation aims to support the needs of 26,069 people (5,213 households) of the most vulnerable affected communities with appropriate immediate and medium-term assistance in a timely, effective, and efficient manner, as well as accompany them to recover from the impact of the typhoon and increase their resilience to future shocks for 15 months.

The Emergency Appeal will support components of the PRC relief and recovery plans of action in the following sectors:

1. **Immediate household needs** assistance, including distribution of essential household **non-food items** and **unrestricted cash grants**.
2. **Livelihoods** support for families to restart their **income earning** activities and **small enterprise** revival, through cash transfers.
3. **Shelter and settlements** assistance to support access to safer living conditions during the initial states of the emergency through the provision of tarpaulins, mosquito nets, blankets, followed by cash transfer and shelter solutions to prioritize self-recovery, and always accompanied by technical support and awareness sessions on build back safer techniques. For the early recovery shelter assistance, based on the evolving needs on the

ground, the support will be in the form of shelter assistance where beneficiaries will be provided with cash and in-kind corrugated iron sheets plus labour support and technical support.

4. **Health** interventions focusing on **psychosocial support, community-based disease prevention, epidemic control, and health promotion.**
5. **Water, sanitation and hygiene promotion** interventions focusing on improving access to safe water, access to improved sanitation, and the sustainable reduction of risk to diseases (water-borne, vector-borne and water-related) in affected communities.
6. **School and community preparedness and disaster risk reduction.**


Implementation of the TS Tembin recovery operation focuses in three provinces of Bukidnon and Zamboanga del Norte

Province	Municipality	Barangays
Lanao del Norte ⁴	Tubod	Dalama
Bukidnon	Kitaotao	Digongan, Kiolom, Panganan and Sinuda
Zamboanga del Norte	Gutalac	Canupong, Mamawan, Panganuran and Sibalik

As with all PRC-led operations, this Appeal supports of the overall PRC Plan of Action and follows key strategies:

- **A Movement-wide approach:** PRC is responsible for the overall coordination and implementation of the disaster response operation, supported by components of the Movement.
- **Cash transfers:** Cash transfers will contribute towards the empowerment of the affected population by giving them the flexibility to prioritize their own recovery needs.
- Establishment of mechanisms to facilitate two-way **communication** with, and ensure **transparency and accountability** to, disaster-affected people.
- **Integrated programming and resilience-building:** Early recovery interventions will aim to address a broad range of sectors, to provide for the needs of communities and contribute to their improved resilience.
- **Factoring lessons from previous operations:** PRC will draw on lessons from previous responses in Mindanao and the current response in Marawi City.
- The Emergency Appeal will also support **National Society capacity enhancement** at chapter and national levels.

C. DETAILED OPERATIONAL PLAN⁵

	<p>Shelter</p> <p>People reached: 10,995⁶</p> <p>Male: 5,498</p> <p>Female: 5,497</p>	
Outcome 1: Communities in disaster and crisis affected areas restore and strengthen their safety, well-being and longer-term recovery through shelter and settlement solutions		
Indicators:	Target	Actual
# of people targeted/reached with safe and adequate shelter and settlement	10,000	10,995 ⁷
Output 1.1: Short, medium and long-term shelter and settlement assistance is provided to affected households		
Indicators:	Target	Actual
# of households provided with emergency shelter and settlement assistance	2,000	1,793
# of households provided with shelter recovery assistance	370 ⁸	355
Progress towards outcomes		
Emergency shelter and household NFIs'		
Relief phase was completed where PRC reached a total of 4,249 households with non-food items. Through the appeal, IFRC supported PRC distribution to 1,793 households (8,965 people) in 14 municipalities. See Operations Update No. 3 for more details.		

⁴ This is the operational are of German red Cross where IFRC will also provide some support on their shelter intervention.

⁵ For targeting, PRC targets families with relief support while households for recovery support.

⁶ Total number of people reached is based on the average five person per household calculation by Philippine Statistics Office.

⁷ Total number of people is based on: 8,965 people provided with non-food items, 1,850 for shelter and 180 carpenters.

⁸ Target has been increased from 200 to 370 based on the actual needs on the ground.

Breakdown of households provided with non-food items by PRC⁹

	Blanket		Sleeping Mat		Mosquito Net		Tarpaulin	
	Total	IFRC supported stock	Total	IFRC supported stock	Total	IFRC supported stock	Total	IFRC supported stock
Total	4,217	1,759	4,249	1,793	4,027	1,571	4,077	1,621

The balance of NFI sets was released from the PRC disaster preparedness stocks that are supported by the Australian Government (DFAT) – these were mobilized and distributed through the support of the Appeal. IFRC also supported the mobilization of PRC staff and volunteers, and logistics and transportation for all the response activities.

Shelter Recovery

For the background of community and beneficiary profile, see [Operations Update No. 3](#) for more details.

As of reporting, 355 shelters have been completed out of the 370 targeted in the barangays of Kitaotao, Bukidnon: 25 in Digongan, 125 in Kiolom, 166 in Panganan and 54 in Sinuda. Beneficiaries received a combination of PHP 27,000 (CHF 540) cash for shelter materials, 10 corrugated iron sheets and labour support paid directly to the carpenters and masons.



IFRC and PRC technical staff continue to do monitoring in shelter relocation sites in Bukidnon. (Photo: Perzeus Jay Luna/IFRC)

Members of the Barangay Recovery Committee (BARECOM) continue to provide on-site monitoring in their respective barangays. PRC and IFRC technical staff also continue its monitoring for the ongoing shelter construction, for continuous technical support on the enforcement of build back better techniques. On-site, they would also receive feedbacks and concerns related to the construction.

In the first few weeks of shelter implementation, progress of shelter construction was in slow due to the limited number of carpenters. During coordination, the local government unit offered to outsource carpenters from neighbouring barangays. Another challenge was the transportation of shelter materials since the resettlement sites are very far from the main market making access difficult by road and river.

In coordination with PRC, German Red Cross and the local government unit, the Appeal will support the completion of 102 shelter in Barangay Dalama, Tubod, of Lanao Del Norte. Construction of these shelters are currently ongoing.

Output 1.2: Technical support, guidance and awareness raising in safe shelter design and settlement planning and improved building techniques are provided to affected households

Indicators:	Target	Actual
# of households provided with technical support and guidance, appropriate to the type of support they receive	2,000	2,171 ¹⁰

Progress towards outcomes

Alongside the distribution of tarpaulins to 4,077 families, was a basic orientation on their use and maintenance as emergency shelter materials. This is standard operating procedure for PRC.

⁹ Validation for the total number of non-food items distributed is ongoing. Final figure will be reflected in the next report.

¹⁰ Emergency shelter for 1,621 households and shelter recovery for 550 households.

For recovery phase of shelter assistance in Bukidnon, safe shelter awareness orientation was provided for the carpenters and masons, along with a representative from the household beneficiaries to ensure that the build back safer techniques are being incorporated in shelter construction and ensuring that knowledge is transferred to the beneficiaries which will further increase resilience of the whole community. This equates to 370 shelter families, carpenters and community members with a total of 550. This was implemented by 16 trained staff and volunteers.

In April 2018, a Participatory Approach for Safe Shelter Awareness (PASSA) workshop Training of Facilitators was conducted in Zamboanga del Norte for chapter staff and volunteers. There were 16 participants (six females and 10 males) attended the workshop. The workshop aimed to introduce the concept of disaster risk reduction by understanding about community hazards, risk, vulnerability and capacities. Communities in Zamboanga Province received shelter support by the Government and the training provided by PRC in safe shelter repair complimented this Government action.



Presentations of community base maps during the PASSA ToT in April 2018. (Photo: Zamboanga del Norte Chapter/PRC)



Livelihoods and basic needs

People reached: 10,720

Male: 5,360

Female: 5,360

Outcome 1: Communities, especially in disaster and crisis affected areas, restore and strengthen their livelihoods

Indicators:	Target	Actual
# of people who have enough food/cash/income to meet their survival threshold	10,000	10,720 ¹¹

Output 1.1: Basic needs assistance for livelihoods security including food is provided to the most affected communities

Indicators:	Target	Actual
# of 2,500 people reached with food assistance	2,500	25,480 ¹²

Progress towards outcomes

Food assistance

PRC distributed food packs to a total of 5,096 families – 3,947 families with 2 to 3-day food ration and 1,149 families with assorted food packs. Hot meals were provided to 10,218 individuals inside different evacuation sites. See [Operations Update No. 3](#) for more details.

PRC also received support from external donors and Movement Partners such as Turkish and Qatar Red Crescent Societies.

Output 1.2: Household livelihoods security is enhanced through food production and income generating activities

Indicators:	Target	Actual
# of households supported with in-kind assets or cash or vouchers for starting/strengthening economic activities	300	326

Progress towards outcomes

Household Livelihoods Assistance

A total of 254¹³ beneficiaries were provided with household livelihood assistance (HLA) in the four barangays in the municipality of Gutalac in Zamboanga del Norte. The total grant of PHP 10,000 (approximately CHF 200) was provided in two tranches: 60 per cent and 40 per cent respectively.


¹¹ 1,818 unconditional/multipurpose cash grants, plus 254 HLA and 72 CMLP.

¹² Overall accomplishment of PRC. This Appeal supported the mobilization cost.

¹³ Figure is based on the total number of households who were able to receive the full cash grant

Most of the beneficiaries opted for livestock raising which fits to their existing skills and capacities. Many of the beneficiaries opted for pig raising since they already have existing knowledge. Pigs are easy to sell in their local market.

Breakdown of livelihood options chosen by the household livelihood assistance's beneficiary.

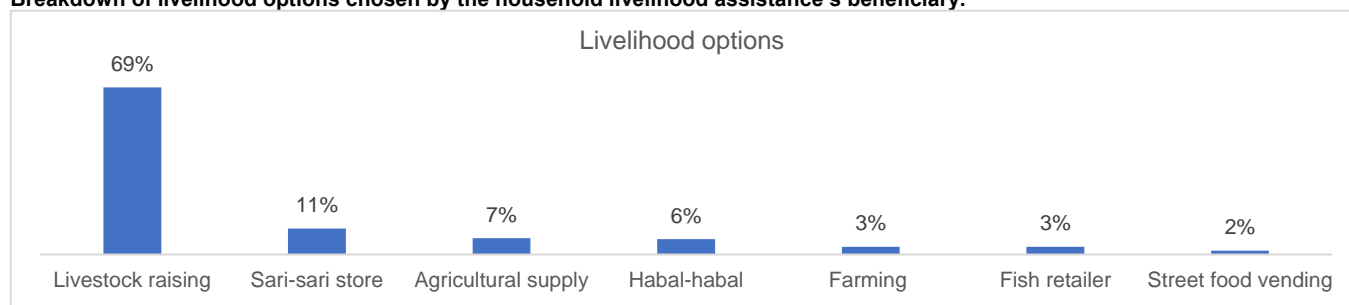

14 15

Seeds Assistance

Aside from the cash grant, the assistance was also complemented with the provision of vegetable seeds. A total of 750 households received these seeds in Bukidnon and Zamboanga del Norte. The seeds are aimed to support food security while they await the sale of their pigs and produce.



This beneficiary shows her vegetable produce from the seeds provided by PRC. Most of the beneficiaries set-up a backyard garden to plant the seeds. (Photo: Perzeus Jay Luna/IFRC)

Community-managed livelihoods projects (CMLP)

The livelihood support that is being implemented in the municipality of Kitaotao in Bukidnon province is based on the community managed livelihoods projects (CMLP) approach where an association is set up within the community to manage and implement their own livelihoods activities. Prior to intervention, the community needs to pass the criteria based on the capacity assessment conducted by PRC. Three associations were selected and registered in the Department of Labour and Employment and have a chairperson, secretary, treasurer and members. They were supported to open bank accounts to receive the cash grants.

Guided by PRC and IFRC technical staff, communities were linked and was coordinated with the local government units, such as the Municipal Agriculture's office, to select the best and most sustainable type of support to be provided. Association members were involved in project design and planning, implementation and monitoring on the type of livelihood option they will be implementing. PRC and IFRC technical staff on the ground supported the association in terms of, but not limited to, work plan, human resource plan, budget details and coordination with involved government offices.

Breakdown of associations to be supported and their livelihood ventures

Community	Name of association	No. of members	Type of livelihood
Digongan	Digongan Matigsalug Corn farmers' Association	25	Mobile corn sheller and drier
Kiulom	Kauswagan Alang sa Lumad Association	28	Corn/rice mill and solar drier
Sinuda	Sita-Matigsalug Abaca Growers Association	23	Abaca fiber production

Currently, all three project proposals are now with the PRC national headquarters for approval. Once approved, money will be transferred to the associations bank account to start the implementation.

Output 1.3: Community awareness activities on livelihoods strengthening and protection are carried out with target communities and public actors.

Indicators:	Target	Actual
# of households reached by public awareness and education on sustainable livelihoods	300	326

¹⁴ Sari-sari store is a small family run convenience store which is common in the Philippines.

¹⁵ Habal-habal is a two-wheeled single motorcycle used as public transportation especially in areas with narrow roads and in steeper and rougher terrains.

Progress towards outcomes

Community training for livelihoods

Part of the identified strategy of the household livelihood assistance and the community-managed livelihood activities is to link the communities to their respective LGUs for technical support. The linkage promotes the sustainability of the project through appropriate guidance and technical inputs, as well as an increased sense of ownership and responsibility for the enterprise. With partnership with the Municipal Agriculture Office, the selected 254 beneficiaries in Zamboanga del Norte were trained on different types of livelihoods activities such as pig and poultry raising.

For the CMLP capacity development will be provided to the association members. Trainings identified are for financial literacy, and leadership and management training. They will also be trained on agroforestry for increased land use management system know-how.

Output 1.4: Households are provided with unconditional/multipurpose cash grants to address their basic needs

Indicators:	Target	Actual
# of households reached with cash for basic needs (unconditional cash grants)	2,000	1,818

Progress towards outcomes

Multipurpose cash grants

Distribution of multipurpose cash grants was concluded in the relief phase. A total of 1,818 households (9,090 people) were provided with PHP 3,000 each (approximately CHF 60) in the provinces of Bukidnon, Lanao del Norte and Zamboanga del Norte. This value was based on the equivalent cost of a ten-day food basic for an average family and or ten days labour at the minimum rate. See [Operations Update No. 3](#) for more details.



Health

People reached: 11,739¹⁶

Male: 5,870

Female: 5,869

Outcome 1: The immediate risks to the health of affected populations are reduced

Indicators:	Target	Actual
# of targeted people reached have their immediate risks to health reduced	10,000	11,739

Output 1.1: Target population is provided with rapid medical management of injuries and diseases

Indicators:	Target	Actual
# of people reached by First Aid services	800	781

Progress towards outcomes

Through the welfare desks, PRC was able to provide medical services to 781 individuals – 750 people were checked for their blood pressure, referring some of them for medical treatment; and first aid to 31 people. See [Operations Update No. 3](#) for more details.

Output 1.4: Epidemic prevention and control measures carried out.

Indicators:	Target	Actual
# of households reached with community-based epidemic prevention and control activities	2,000	1,571

Progress towards outcomes

Mosquito nets were provided to the beneficiaries as part of the standard package of non-food items. In total, PRC provided 4,027 households with two pieces of treated mosquito nets, in which 1,571 was reached through the IFRC emergency appeal. PRC mobilized its trained volunteers during the distribution of treated mosquito nets. IFRC also supported the mobilization of PRC staff and volunteers, logistics and transportation for all the response. See [Operations Update No. 3](#) for more details.

¹⁶ 7,855 people with mosquito nets, 781 with first aid, 2,339 with psychosocial support and 764 with search and rescue

The balance of mosquito nets sets was released from the PRC disaster preparedness stocks supported by the Australian Government (DFAT) – these were mobilized and distributed through the support of the Appeal.

Output 1.5: Psychosocial support provided to the target population

Indicators:	Target	Actual
# of people reached by psychosocial support	3,500	2,339 ¹⁷

Progress towards outcomes

PRC, through its Welfare Services department, provided psychosocial support to 2,339 individuals in 20 affected barangays from the provinces of Davao del Norte, Lanao del Norte, Lanao del Sur, Misamis Oriental, Surigao del Norte and Zamboanga del Norte. Adults were provided with individual or group PSS, including psychological first aid, while children were supported to cope through recreational activities, including play and art. All activities related to setting up welfare desks has been completed. See [Operations Update No. 3](#) for more details.

Staff and volunteers mobilized for PSS activities were also trained. In Zamboanga del Norte Chapter, 25 volunteers (16 female and 9 male) were trained for PSS and Restoring Family Links on 26-28 March. In Lanao del Norte, a PSS crash course was conducted for four female volunteers. These activities are part of capacity building for chapters.

Output 1.4: Target population is reached with Search and Rescue activities

Indicators:	Target	Actual
# of people supported by search and rescue	650	764

Progress towards outcomes

There were 764 individuals assisted with rescue from the PRC water search and rescue (WASAR) teams during the emergency phase. See [Operations Update No. 3](#) for more details.



Water, sanitation and hygiene

People reached: 28,006
Male: 14,003
Female: 14,003

Outcome 1: Immediate reduction in risk of waterborne and water related diseases in targeted communities

Indicators:	Target	Actual
# of people reached in targeted communities have reduced their immediate risks of waterborne and water related diseases	25,000	28,006

Output 1.1: Continuous assessment of water, sanitation, and hygiene situation is carried out in targeted communities

Indicators:	Target	Actual
# of assessments and monitoring visits undertaken	3	3

Progress towards outcomes

Immediately after landfall, three teams from PRC National Headquarters were deployed to Lanao del Norte, Palawan and Zamboanga del Norte to conduct Rapid Disaster Assessment and Need Analysis (RDANA). All three teams had a WASH personnel to assess needs related to WASH.

Output 1.2: Daily access to safe water which meets Sphere and WHO standards in terms of quantity and quality is provided to target population

Indicators:	Target	Actual
# of people provided with safe water (according to WHO standards)	25,000	26,069
Litres safe water distributed (cumulative)	1,000,000	1,611,500

¹⁷ Figure reflected is based on the validated and recent 3W submitted by PRC DMS.

Progress towards outcomes		
<p>To address water needs in Zamboanga del Norte which was caused by Vinta, PRC distributed 1.6 million litres of water to 26,069 people through water tankering. PRC also identified and installed different water points in 18 communities with damaged water systems. See Operations Update No. 3 for more details.</p> <p>For proper water storage and handling, PRC distributed jerry cans to 4,365 households, of which 1,793 was reached through the IFRC support. The balance of jerry cans was released from the PRC disaster preparedness stocks support by the Australian Government (DFAT) – these were mobilized and distributed through the support of the Appeal.</p>		
Output 1.4 Hygiene promotion activities which meet Sphere standards in terms of the identification and use of hygiene items provided to target population		
Indicators:	Target	Actual
# of people reached by hygiene promotion activities	10,000	28,006
Progress towards outcomes		
<p>Activities related to hygiene promotion activities to increase public awareness and prevent diseases related to poor hygiene practices was concluded in emergency phase. A total of 165 volunteers were trained on hygiene promotion. Through the mobilized volunteers, PRC WASH Services reached 28,006 individuals for hygiene promotion.</p>		
Output 1.5: Hygiene-related goods (NFIs) which meet Sphere standards and training on how to use those goods is provided to the target population		
Indicators:	Target	Actual
# of households provided with a set of essential hygiene items	2,000	1,783
Progress towards outcomes		
<p>Overall, PRC was able to provide 4,739 households with hygiene kits¹⁸, in which 1,783 households were reached through the IFRC support. Alongside distribution was a short orientation on the content and use of the kit. Further, IFRC also supported the mobilization of PRC staff and volunteers, logistics and transportation for all the response. See Operations Update No. 3 for more details.</p> <p>The balance of hygiene kits was released from the PRC disaster preparedness stocks supported by the Australian Government (DFAT) – these were mobilized and distributed through the support of the Appeal.</p>		
Outcome 2: Sustainable reduction in risk of waterborne and water related diseases in targeted communities in the recovery phase		
Indicators:	Target	Actual
# of people reached have sustainable reduction in risk of waterborne and water related diseases	1,500	521
Output 2.1: Continuous monitoring and evaluation of water, sanitation, and hygiene situation is carried out in targeted communities		
Indicators:	Target	Actual
# of assessments and monitoring visits undertaken	3	3
Progress towards outcomes		
<p>Field operations people continue to monitor and assess the WASH situation in the operational areas. In Zamboanga del Norte, the WASH team conducted hygiene promotion activities. The intervention reminded communities about the importance of hygiene promotion. All hygiene promotion activities in Zamboanga del Norte has been completed by 32 trained RC 143 volunteers.</p> <p>In the second week of December, a detailed assessment on the appropriate WASH intervention to be implemented was conducted by NHQ WASH technical staff in Bukidnon, for the shelter relocation beneficiaries. Based on the assessment, relocated families need access to sanitation facilities and water supply.</p>		
Output 2.2: Community managed water sources giving access to safe water is provided to target population		
Indicators:	Target	Actual

¹⁸ A standard IFRC hygiene kit contains 12 pieces of body soap, 5 pieces laundry soap, 40 pieces sanitary pads, 5 pieces bath towels, 6 pieces toilet paper, 2 pieces toothpaste, 5 pieces toothbrush and 4 pieces of disposable razor

# households provided with safe water services that meet agreed standards according to specific operational and programmatic context	354	In progress
--	-----	-------------

Progress towards outcomes

In Bukidnon, 4 communities have been identified for rehabilitation of water sources as follows:

Location	Type of intervention
Digongan	Improvement of existing spring water source
Sitio Kilantap in Kiulom	Improvement of existing spring water source
Sitio Hanigon in Kiulom	Construction of spring box
Sinuda	Construction of hand pump

Currently, sending of quotation from different suppliers is ongoing. The construction of the project will be closely monitored by PRC and IFRC Project Engineers together with chapter staff and volunteers. The implementation will be through cash transfer approach.

Output 2.3: Improved access to and use of adequate sanitation by the target population

Indicators:	Target	Actual
# of households with access to an improved sanitation facility	100	In progress

Progress towards outcomes

The early recovery shelter programme in Bukidnon is an entry point for the support for water and sanitation facilities. The WASH Services has done the assessment and recommended latrine construction.

In Bukidnon, shelter beneficiaries will also be provided with latrine. The support will be in a form of conditional cash grant worth of PHP 5,600 and labor cost. The amount will be used to purchase latrine construction materials from the reputable suppliers previously identified by the BARECOM. A total of 355 beneficiaries were already identified for latrine construction support based on the following criteria:

- construction of shelter was finished
- stones for the chambers available on site
- materials for the superstructure available
- excavation for the digestive and leaching chamber completed



PRC technical staff are supervising the construction of pilot latrines and setting of septic tank at Sitio Kilantap, Barangay Kiulom, Kitaotao, Bukidnon. On the ground, they are also providing technical guidance related to the construction. *(Photo: Omar Amonoy/IFRC)*

Output 2.4: Hygiene promotion activities are provided to the entire affected population.

Indicators:	Target	Actual
# of people reached by hygiene promotion activities	500	521

Progress towards outcomes

The WASH Services trained 32 Red Cross 143 volunteers in Gutalac, Zamboanga del Norte. These volunteers were mobilized for the hygiene promotion activity with key messages on personal hygiene, water-borne diseases, safe drinking water and proper food handling, and vector-related diseases were the main topic during the hygiene promotion. IEC materials on hygiene promotion were printed and posted in communities where community volunteers conducted the activities. Summary on the number of people reached are as follows:

Barangay	Families Reached	Individuals Reached
Mamawan	27	121
Canupong	34	152
Panganuran	35	158
Sibalic	20	90
Total	116	521

The hardware intervention to be provided to the relocated families in Bukidnon will be complemented with PHAST activity. There will be a training to be provided to RC 143 who will be rolling out PHAST in their respective communities.



Protection, Gender and Inclusion

People reached: 28,006

Male: 14,003

Female: 14,003

Outcome 1: Communities identify the needs of the most vulnerable and particularly disadvantaged and marginalised groups, as a result of inequality, discrimination and other non-respect of their human rights and address their distinct needs

Indicators:	Target	Actual
# of people reached for inclusion and protection outcome	25,000	28,006

Output 1.1: NS programmes improve equitable access to basic services, considering different needs based on gender and other diversity factors.

Indicators:	Target	Actual
# of staff/volunteers available to provide equitable access to services	20	297

Progress towards outcomes

All staff and volunteers mobilized for this operation were capacitated based on the type of activities in which they were involved. Trainings were provided to staff and volunteers: 29 individuals in PSS and Restoring Family Links, 197¹⁹ in Hygiene promotion, 55 in first-aid, and 16 in PASSA.

Output 1.2: Emergency response operations prevent and respond to sexual- and gender-based violence and all forms of violence against children.

Indicators:	Target	Actual
# of children with access to equitable services preventing sexual and gender-based violence	5,000	5,392

Progress towards outcomes

IFRC has zero tolerance for any form of violence against children. Child protection policy is part in the mandatory orientation provided to volunteers mobilized in this operation where all staff and volunteers signed a document that they have read, understood and would abide the policy. Careful programming across all the sectors and operational areas of IFRC ensured that children is protected from exploitation and abuse regardless of their nationality, culture, ethnicity, gender, religious or political beliefs, socio-economic status, family or criminal background, physical or mental health or any other factor of discrimination.

For recovery operations, the 8 communities from Bukidnon and Zamboanga del Norte has a total population of 15,583. Approximately, there are 5,392²⁰ children (age from 0-14 years old) from these operational areas. IFRC and PRC staff and volunteers ensure that child protection is integrated all throughout its activities and programmes for the recovery operations. During the relief phase, PRC Welfare Service had taken into account child protection, as well as gender-based violence, through the establishment of welfare desks in different evacuation centres.



Disaster Risk Reduction

People reached: 15,583

Male: 7,792

Female: 7,791

Outcome 1: Communities in high risk areas are prepared for and able to respond to disaster

Indicators:	Target	Actual
# of people reached in targeted communities are prepared for and able to respond to disaster	15,583	15,583

Output 1.1: Communities take active steps to strengthen their preparedness for timely and effective response to disasters.

¹⁹ 165 trained volunteers during the emergency phase and 32 during recovery phase

²⁰ Based on Philippine Statistics Authority age structure breakdown, 0-14 years old constitute 34.6% of the total population in the Philippines.

Indicators:	Target	Actual
# of people reached with public awareness and education campaigns using harmonized messages to reduce, mitigate and respond to identified risks	15,583	15,583

Progress towards outcomes

To help build resilience in disaster affected communities, all eight operational communities are being supported with community-based disaster risk reduction programme.

Province	Barangay	No. of volunteers oriented about RC143	No. of RC 143 volunteers trained in first aid	No. of RC143 volunteers trained in CBDRRM
Bukidnon	Digongan	44	44	9
	Kiulom	44	44	10
	Panganan	44	44	8
	Sinuda	44	44	9
Zamboanga del Norte	Canupong	44	44	44
	Mamawan	44	44	44
	Panganuran	44	44	44
	Sibalic	44	44	44
Total		352	352	212

2 barangays were identified for vulnerability and capacity assessment (VCA) activity. Geographically, these 2 identified barangays are the farthest and mostly inaccessible for aid and information. VCA in Zamboanga del Norte was already conducted in Barangay Canupong. The output was presented to the barangay council. This will then move to the development of plan of action based on the vulnerabilities and capacities identified in the community. The VCA in Barangay Kiulom in Bukidnon province is ongoing.

At the completion of this programme, CBDRRM activities will help in the improvement of community resiliency through improved disaster response and mitigation of disaster risks for 15,583 people – the total population of the 8 barangays in Zamboanga and Bukidnon.

Outcome 2: Communities in disaster and crisis affected areas adopt climate risk informed and environmentally responsible values and practices

Indicators:	Target	Actual
# of people reached in targeted communities adopt climate risk informed and environmentally responsible values and practices	500	In progress

Output 2.1: Contributions to climate change mitigation are made by implementing green solutions

Indicators:	Target	Actual
# of people benefit from tree planting	500	In progress

Progress towards outcomes

Climate change mitigation activities is an integral component for the PRC DRR implementation. Tree planting activities will be initiated by the PRC, with the support of local government units. The Department of Agriculture will be donating the planting materials which will be planted in riverbanks to help prevent landslides, land degradation and erosion.

Strengthen National Society

Outcome 1: National Society capacity building and organizational development objectives are facilitated to ensure that National Societies have the necessary legal, ethical and financial foundations, systems and structures, competences and capacities to plan and perform

Indicators:	Target	Actual
# of PRC chapters that are well functioning for the emergency operation	4	4

Output 1.2: National Societies have effective and motivated volunteers who are protected

Indicators:	Target	Actual
-------------	--------	--------

# of volunteers insured		228
# of volunteers trained		228
# of volunteers provided with psychosocial support		In progress
# of volunteers involved in decision making processes		In progress
Progress towards outcomes		
<p>Prior to their mobilization, all volunteers were provided orientation on the history and seven fundamental principles of the Red Cross Red Crescent Movement.</p> <p>A total of 16 volunteers are being mobilized for the recovery operation, 7 in Bukidnon chapter and 9 in Zamboanga del Norte chapter. All their feedbacks and inputs based on the progress of the project implementation are factored in the programme design and strategy. All volunteers mobilized for the recovery operation are insured under the Membership and Accident Assistance Benefit (MAAB) of PRC. From the start of the operation, from relief to recovery, a total 228 volunteers were trained in different types of trainings.</p>		
Output S1.1.6: National Societies have the necessary corporate infrastructure and systems in place		
Indicators:	Target	Actual
# of deployment of RCAT	1	1
# of training provided to staff and volunteers	3	3
PRC disaster preparedness strategy developed	Yes	Ongoing
Progress towards outcomes		
<p>For the recovery operation, Bukidnon and Zamboanga del Norte chapters were provided with necessary office supplies for a conducive working environment. Aside from basic equipping, volunteers mobilized in this operation were also trained and oriented prior to deployment. There were 29 staff trained for PSS and Restoring Family Links, 197 for hygiene promotion and 55 for first-aid. RCAT 143 volunteers were also deployed and mobilized for this operation during the emergency phase.</p> <p>For disaster preparedness strategy, IFRC has been supporting PRC on their annual pre-disaster meeting where standards operating procedures is continued to be updated based on the current trends and situation in the country. Part of the PRC strategy is to strengthen the capacity of all its chapters to have well-trained volunteers that can be mobilized and deployed in times of disaster. Under the developmental programming, IFRC is supporting PRC in strengthening the Red Cross Action Team (RCAT) 143 programme.</p> <p>The Appeal will support the Bukidnon and Zambaonga del Norte Chapters with capacity and infrastructure development.</p>		

International Disaster Response		
Outcome S2 1: Effective and coordinated international disaster response is ensured		
Indicators:	Target	Actual
% of targeted population satisfied that they have access to information, feedback mechanisms and can influence the tropical storm operation	80% (of most vulnerable affected)	98%
Output S2 1.1: Effective response preparedness and NS surge capacity mechanism is maintained		
Indicators:	Target	Actual
# of CEA RDRT deployed	1	1
Progress towards outcomes		
<p>Staff and volunteers, working on the ground, who were oriented on CEA conducted a community validation where the selection criteria were explained. This was to let the beneficiaries and wider communities understood the rationale behind the selection criteria, considering that only fraction of the affected populations were supported with recovery assistance. IEC materials about the programme are being posted in strategic locations in the operational areas. These are being translated in local dialect to ensure understanding and clarity.</p>		

CEA RDRT was also deployed in Tembin operational areas to support community engagement and accountability activities. The RDRT supported the chapter to establish a process of documenting CEA activities.

BARECOMs continue to do on-site monitoring and receive direct feedback which are essential for the programme implementation and resolving challenges at their level. They continue to be an important platform to promote community participation and accountability.

A completion survey to be done for the livelihood and shelter assistance will also have a CEA component. This would include a satisfaction question where the community people can gauge their access to information and feedback mechanism.

In the completed PDM for the non-food and cash assistance, out of the 674 respondents, 42 per cent said that they have access to the local PRC chapter while 46 per cent mentioned that they have other means of reaching PRC. Only 28 per cent used the feedback mechanism of PRC wherein 75 per cent of them received a response. Overall, 98 per cent of the total respondents were happy in the process of selection, distribution and feedback mechanism.

Output S2 1.2: NS compliance with Principles and Rules for Humanitarian Assistance is improved

Indicators:	Target	Actual
% compliance with Principles and Rules for Humanitarian Assistance	100%	100%

Output S2 1.3: Supply chain and fleet services meet recognized quality and accountability standards

Indicators:	Target	Actual
% of international procurement respecting the IFRC procurement procedures	100%	100%

Progress towards outcomes

Logistics team had been engaged in procuring, storing and transporting emergency relief items and supported personnel movement. Non-food items from IFRC disaster preparedness stock for 2,000 households were mobilized to three provinces: 800 in Lanao del Norte, 700 in Lanao del Sur and 500 in Zamboanga del Norte. For recovery support, 3,824 pieces of CGI sheets, donated by American Red Cross, were sent to Bukidnon for the shelter assistance. All in-country transportation and distribution were carried out in close coordination with PRC Logistics Department and Disaster Management Services Department. Two 10-wheeler trucks were hired to support transportation of items.

All replenishment of stocks was completed. Blankets and plastic mats were procured locally, while the replenishment for hygiene kits, jerry cans and tarpaulins were procured internationally through the IFRC Operational Logistics, Procurement and Supply Chain Management Department in Kuala Lumpur. To date, logistics continue to provide support for shelter, wash and livelihood in the operational areas of Bukidnon. Furthermore, one IFRC vehicle has been deployed for the staff and volunteers.

Output S2 1.4: Coordinating role of the IFRC within the international humanitarian system is enhanced

Indicators:	Target	Actual
# of coordination meetings with other stakeholders	3	3

Progress towards outcomes

PRC participates in NDRRMC meetings and coordinates with the Department of Social Welfare and Development (DSWD), and Department of Health, and the NDRRMC at regional, provincial, municipal and barangay levels. PRC has assigned dedicated personnel who continue to represent the National Society in NDRRMC meetings. PRC is also participating in the NDRRMC Pre-Disaster Risk Analysis (PDRA) meetings and preparedness planning meetings.

At country level, PRC and IFRC consistently participate in meetings of the Humanitarian Country Team (HCT) held both during disasters and non-emergency times. PRC and IFRC are involved in relevant government-led cluster information sharing, planning, and analysis at all levels, while IFRC supports PRC coordination efforts through representation in other relevant clusters as required.

Outcome S2. 2: The complementarity and strengths of the Movement are enhanced

Indicators:	Target	Actual
MCA in place	100%	100%

Output S2 2.1: In the context of large-scale emergencies the IFRC, ICRC and NS enhance their operational reach and effectiveness through new means of coordination.		
Indicators:	Target	Actual
Involvement in regular coordination meetings	Yes	Ongoing
Progress towards outcomes		
<p>PRC works with the IFRC, ICRC and 10 Partner National Societies in the country. Aside from PNS with in-country presence, PRC also works bilaterally with other Movement Partners such as Turkish and Qatar Red Crescent Societies. Since the 2014 Movement Wide Operational Framework was established, PRC has been leading all in-country emergency operations. On 7 June 2018, ICRC, IFRC and PRC formally signed the Movement Coordination Agreement, making PRC the lead for all emergency operations in the country with support from ICRC and IFRC.</p> <p>Furthermore, PRC organizes a monthly in-country Movement-wide meeting to update partners on current plans and activities. Partners also share relevant information related to in-country plans and activities. In case of large-scale disasters, IFRC, ICRC and the NS will follow the Movement Coordination Agreement in place and will further seek ways to improving coordination mechanism.</p>		

Influence others as leading strategic partner		
Outcome S3 1: The IFRC secretariat, together with National Societies uses their unique position to influence decisions at local, national and international levels that affect the most vulnerable.		
Indicators:	Target	Actual
IFRC and NS are visible, trusted and effective advocates on humanitarian issues.	100%	In progress
Output S3 1.1: IFRC and NS are visible, trusted and effective advocates on humanitarian issues		
Indicators:	Target	Actual
# of communications materials produced (social media, media articles, interviews, etc.)	6	7
Progress towards outcomes		
<p>The communications team ensured that the Red Cross response efforts are effectively communicated amongst its key public audiences at the onset of the emergency up to the recovery highlights and milestones. The team generated high quality photos, video clips, and news stories which were used across IFRC and PRC multimedia platforms. These materials were also widely circulated/utilized by PRC, PNS, and IFRC, and sent to national and international media. Both PRC and IFRC communications team were also active in posting relevant information regarding the operation on several social networking sites.</p> <p>PRC published news articles on their public website and on their official social media accounts:</p> <ul style="list-style-type: none"> - PRC Facebook Live of ceremonial turnover ceremony for Tembin/Vinta affected families (click here, here, here) - PRC appeals for aid for 500,000 people affected by Vinta (click here) - Red Cross launches emergency appeal for #VintaPH (click here) - PRC gives cash grants to Vinta-displaced families in Mindanao (click here) - PRC receives 3.3 million Philippine peso assistance from Turkish Red Crescent for Vinta Relief Operation (click here) <p>The IFRC Communications team also produced several communications materials:</p> <ul style="list-style-type: none"> - AV materials on Tembin (click here) - Six months on recovery milestones, highlights on Twitter (click here, here, here, here, here, here) - Community voices news article (click here) - A news article which is up to the IFRC public website (click here) - Two press releases: 1 for DREF which was released on 23 December 2017 and 1 for the emergency appeal which was released on 26 December 2017. 		
Output S3 1.2: IFRC produces high-quality research and evaluation that informs advocacy, resource mobilization and programming.		
Indicators:	Target	Actual
# of rapid and detailed assessment teams deployed – chapter level and augmented by NHQ.	6	6

Progress towards outcomes		
Right after the landfall, six teams from the National Headquarters were deployed to Lanao del Norte, Palawan and Zamboanga del Norte. The first three teams were deployed for rapid assessment then two weeks later, three teams were deployed for detailed assessment in the same areas.		
Outcome S3 2: The programmatic reach of the National Societies and the IFRC is expanded.		
Indicators:	Target	Actual
Work in planning and reporting to ensure effective accountability internally and externally.	100%	100%
Output S3 2.1: Resource generation and related accountability models are developed and improved		
Indicators:	Target	Actual
# of post-distribution visits to affected communities	5	2
Progress towards outcomes		
<p>The BARECOM comprises five to ten community members in each barangay who contribute directly to the local recovery planning, beneficiary selection process, and prioritization of activities as well as implementation and monitoring of the interventions. These committees act as advisory groups for all programmes under PRC/IFRC recovery interventions such as shelter, livelihoods, water and sanitation, and disaster risk reduction. They provide valuable insight into individual community recovery needs for each sector and assist in identifying beneficiaries who can then be validated through collective community processes. They also received community feedback and relay it to PRC staff and volunteers for action. As such, the barangay recovery committees help to ensure an integrated approach of multiple programme sectors.</p> <p>Since the start of the recovery operation, staff and volunteers conduct daily monitoring in different operational areas. All these visits provide a good avenue for the community to talk to PRC. In January, two post-distribution visits were conducted for the PDM survey on unconditional/multipurpose cash grant and non-food items.</p>		
Output S3 2.2: National Societies are supported in resource and partnership development (from both domestic markets and foreign sources).		
Indicators:	Target	Actual
IFRC leadership in resource development for emergencies is maintained.	100%	100%
% of appeal supported	80%	100%
Progress towards outcomes		
The appeal is 100% covered in terms of the funding sought which is at CHF 1,194,765.		

Effective, credible and accountable IFRC		
Outcome S4 1: The IFRC enhances its effectiveness, credibility and accountability		
Indicators:	Target	Actual
Effective performance of staff supported by HR procedures	100%	100%
Output S4 1.1: IFRC staff shows good level of engagement and performance		
Indicators:	Target	Actual
% of compliance with PRC HR procedures	100%	100%
Progress towards outcomes		
The operation recruited a field officer who supports the programme implementation. Recruitment process was based on PRC HR procedures. Mobilization and provision of allowance to volunteers is also based on standard HR procedure.		
Output S4 1.2: Financial resources are safeguarded; quality financial and administrative support is provided contributing to efficient operations and ensuring effective use of assets; timely quality financial reporting to stakeholders		

Indicators:	Target	Actual
% of financial reporting respecting the IFRC procedures	100	100
Output S4 1.3: Staff security is prioritised in all IFRC activities		
Indicators:	Target	Actual
# of security updates provided to PRC and stakeholders		Ongoing
Progress towards outcomes		
<p>The IFRC, through the finance department, provides the necessary operational support for review, validation of budgets, bank transfers, and technical assistance to the National Societies on procedures for justification of expenditures, including the review and validation of invoices. PRC – which is on the working advance system – has been supported for many years by the IFRC and is accustomed to these financial procedures. All financial transactions in this operation adhere to the standard IFRC financial procedures. The IFRC finance and administration team in Manila provides both administration and transport support at headquarters and in the field.</p> <p>Parts of Mindanao are security-sensitive due to the presence and operations of non-state armed groups. Overall, the area is at orange security level. Given the context, regular coordination is maintained with the ICRC and other Movement partners, as per existing security framework and Movement coordination agreement. Regular information-sharing has been maintained and specific security protocols for each security level. All staff and volunteers are required to complete the IFRC Stay Safe e-learning courses: Stay Safe Personal Security, Stay Safe Security Management and Stay Safe Volunteer Security.</p>		

D. BUDGET

Financial report is attached at the end of the operations update.

Reference documents



Click for:

- [Previous Appeals and updates](#)
- [Revised Emergency Appeal](#)
- [Revised Emergency Plan of Action](#)

For further information, specifically related to this operation please contact:

In the Philippines Red Cross

- Elizabeth Zavalla, Secretary General; phone: +63 2 790 2300; email: secgen@redcross.org.ph
- Leonardo Ebajo, director for disaster management services; email: leonardo.ebajo@redcross.org.ph

In IFRC Philippines Country Office

- Patrick Elliott, Operations Manager; phone: +63 998 961 2140; email: patrick.elliott@ifrc.org

In IFRC Asia Pacific Regional Office, Kuala Lumpur

- Alka Kapoorsharma, acting Deputy Regional Director; email: alka.kapoorsharma@ifrc.org
- Necephor Mghendi, head of Disaster and Crisis Unit (DCPRR); email: necephor.mghendi@ifrc.org
- Johanna Arvo, Operations Coordinator; email: johanna.arvo@ifrc.org
- Riku Assamaki, Logistics Coordinator; email: riku.assamaki@ifrc.org
- Rosemarie North, Communications Manager; email: rosemarie.north@ifrc.org
- Sophia Keri, Resource Mobilization in Emergencies Coordinator; email: sophia.keri@ifrc.org
- Siew Hui Liew, PMER Manager; email: siewhui.liew@ifrc.org

In IFRC Geneva

- Nelson Castano, Operation Coordination Manager; email: nelson.castano@ifrc.org

How we work

All IFRC assistance seeks to adhere to the [Code of Conduct](#) for the International Red Cross and Red Crescent Movement and Non-Governmental Organizations (NGOs) in Disaster Relief and the [Humanitarian Charter and Minimum Standards in Humanitarian Response \(Sphere\)](#) in delivering assistance to the most vulnerable. The IFRC's vision is to inspire, **encourage, facilitate and promote at all times all forms of humanitarian activities** by National Societies, with a view to **preventing and alleviating human suffering**, and thereby contributing to the maintenance and promotion of human dignity and peace in the world.

The IFRC's work is guided by Strategy 2020 which puts forward three strategic aims:



Save lives,
protect livelihoods,
and strengthen recovery
from disaster and crises.



Enable **healthy**
and **safe** living.



Promote **social inclusion**
and a culture of
non-violence and **peace**.

Disaster Response Financial Report

MDRPH026 - Philippines - Tropical Storm Tembin

Selected Parameters

Reporting Timeframe	2017/12-2019/1	Programme	MDRPH026
Budget Timeframe	2017/12-2019/3	Budget	APPROVED

All figures are in Swiss Francs (CHF)

I. Funding

	TOTAL	Deferred Income
A. Budget	1,194,697	
B. Opening Balance		
Income		
Cash contributions		
<i>American Red Cross</i>	150,713	
<i>China Red Cross, Hong Kong branch</i>	23,828	
<i>Japanese Red Cross Society</i>	269,471	
<i>Red Cross of Monaco</i>	23,574	
<i>Swedish Red Cross</i>	325,104	
<i>The Canadian Red Cross Society (from Canadian Government*)</i>	87,783	
<i>The Netherlands Red Cross (from Netherlands Government*)</i>	276,976	
C1. Cash contributions	1,157,449	
Inkind Goods & Transport		
<i>American Red Cross</i>	37,317	
C2. Inkind Goods & Transport	37,317	
C. Total Income = SUM(C1..C4)	1,194,765	
D. Total Funding = B + C	1,194,765	

* Funding source data based on information provided by the donor

Disaster Response Financial Report

MDRPH026 - Philippines - Tropical Storm Tembin

Selected Parameters

Reporting Timeframe 2017/12-2019/1 Programme MDRPH026

Budget Timeframe 2017/12-2019/3 Budget APPROVED

All figures are in Swiss Francs (CHF)

III.Expenditure

Account Groups	Expenditure											Total	Variance	
	Budget	Strategy for implementation				Area of focus								
		SFI1 - Strengthen National Society capacities	SFI2 - Ensure effective international disaster management	SFI3 - Influence others as leading strategic partners	SFI4 - Ensure a strong IFRC	AOF1 - Disaster risk reduction	AOF2 - Shelter	AOF3 - Livelihood s and basic needs	AOF4 - Health	AOF5 - Water, sanitation and hygiene	AOF6 - Inclusion, gender and protection			AOF7 - Migration
A												B	A - B	
Budget (C)						1,194,697							1,194,697	
Relief items, Construction, Supplies														
Shelter - Relief	44,418					44,418							44,418	0
Shelter - Transitional	25,697					25,697							25,697	0
Construction - Facilities	19,929					2,948							2,948	16,981
Construction Materials	102,210					37,811							37,811	64,399
Clothing & Textiles	34,762					34,762							34,762	0
Food	343					343							343	0
Seeds & Plants	3,000					3,000							3,000	0
Water, Sanitation & Hygiene	28,380					28,380							28,380	0
Medical & First Aid	1,267					1,267							1,267	0
Utensils & Tools	4,640					4,640							4,640	0
Other Supplies & Services	1,300													1,300
Cash Disbursement	339,913					302,481							302,481	37,432
Total Relief items, Construction, Supplies	605,859					485,747							485,747	120,112
Land, vehicles & equipment														
Computers & Telecom	7,051					7,112							7,112	-61
Office & Household Equipment	1,779					1,779							1,779	0
Total Land, vehicles & equipment	8,830					8,890							8,890	-61
Logistics, Transport & Storage														
Storage	6,805					6,805							6,805	0
Distribution & Monitoring	5,086					5,086							5,086	0
Transport & Vehicles Costs	76,020					71,980							71,980	4,040
Logistics Services	9,400					9,400							9,400	0
Total Logistics, Transport & Storage	97,311					93,271							93,271	4,040
Personnel														
International Staff	58,420					68,207							68,207	-9,787

Disaster Response Financial Report

MDRPH026 - Philippines - Tropical Storm Tembin

Selected Parameters

Reporting Timeframe	2017/12-2019/1	Programme	MDRPH026
Budget Timeframe	2017/12-2019/3	Budget	APPROVED

All figures are in Swiss Francs (CHF)

III. Expenditure

	Budget	Expenditure	Variance
AOF1 - Disaster risk reduction			0
AOF2 - Shelter	1,194,697	1,045,313	149,383
AOF3 - Livelihoods and basic needs			0
AOF4 - Health			0
AOF5 - Water, sanitation and hygiene			0
AOF6 - Inclusion, gender and protection			0
AOF7 - Migration			0
Area of focus Total	1,194,697	1,045,313	149,383
SFI1 - Strengthen National Society capacities			0
SFI2 - Ensure effective international disaster management			0
SFI3 - Influence others as leading strategic partners			0
SFI4 - Ensure a strong IFRC			0
Strategy for implementation Total			0
Grand Total	1,194,697	1,045,313	149,383

Disaster Response Financial Report

MDRPH026 - Philippines - Tropical Storm Tembin

Selected Parameters

Reporting Timeframe	2017/12-2019/1	Programme	MDRPH026
Budget Timeframe	2017/12-2019/3	Budget	APPROVED

All figures are in Swiss Francs (CHF)

III. Expenditure

Account Groups	Budget	Expenditure					TOTAL	Variance
		Raise humanitarian standards	Grow RC/RC services for vulnerable people	Strengthen RC/RC contribution to development	Heighten influence and support for RC/RC work	Joint working and accountability		
	A					B	A - B	
BUDGET (C)			1,194,697			1,194,697		
Relief items, Construction, Supplies								
Shelter - Relief	44,418		44,418			44,418	0	
Shelter - Transitional	25,697		25,697			25,697	0	
Construction - Facilities	19,929		2,948			2,948	16,981	
Construction Materials	102,210		37,811			37,811	64,399	
Clothing & Textiles	34,762		34,762			34,762	0	
Food	343		343			343	0	
Seeds & Plants	3,000		3,000			3,000	0	
Water, Sanitation & Hygiene	28,380		28,380			28,380	0	
Medical & First Aid	1,267		1,267			1,267	0	
Utensils & Tools	4,640		4,640			4,640	0	
Other Supplies & Services	1,300						1,300	
Cash Disbursement	339,913		302,481			302,481	37,432	
Total Relief items, Construction, Sup	605,859		485,747			485,747	120,112	
Land, vehicles & equipment								
Computers & Telecom	7,051		7,112			7,112	-61	
Office & Household Equipment	1,779		1,779			1,779	0	
Total Land, vehicles & equipment	8,830		8,890			8,890	-61	
Logistics, Transport & Storage								
Storage	6,805		6,805			6,805	0	
Distribution & Monitoring	5,086		5,086			5,086	0	
Transport & Vehicles Costs	76,020		71,980			71,980	4,040	
Logistics Services	9,400		9,400			9,400	0	
Total Logistics, Transport & Storage	97,311		93,271			93,271	4,040	
Personnel								
International Staff	58,420		68,207			68,207	-9,787	
National Staff	37,821		37,846			37,846	-25	
National Society Staff	36,698		28,732			28,732	7,966	
Volunteers	17,278		15,442			15,442	1,836	
Total Personnel	150,217		150,227			150,227	-10	
Consultants & Professional Fees								
Professional Fees	1,322		1,324			1,324	-3	
Total Consultants & Professional Fes	1,322		1,324			1,324	-3	
Workshops & Training								
Workshops & Training	32,821		21,571			21,571	11,250	
Total Workshops & Training	32,821		21,571			21,571	11,250	
General Expenditure								
Travel	50,221		45,591			45,591	4,630	
Information & Public Relations	4,870		4,870			4,870	0	
Office Costs	12,615		12,315			12,315	300	
Communications	2,789		2,372			2,372	417	
Financial Charges	-745		-745			-745	0	
Other General Expenses	65		65			65	0	
Shared Office and Services Costs	32,436		34,391			34,391	-1,955	
Total General Expenditure	102,252		98,859			98,859	3,392	
Operational Provisions								
Operational Provisions	118,018		116,656			116,656	1,362	
Total Operational Provisions	118,018		116,656			116,656	1,362	

Disaster Response Financial Report

MDRPH026 - Philippines - Tropical Storm Tembin

Selected Parameters

Reporting Timeframe	2017/12-2019/1	Programme	MDRPH026
Budget Timeframe	2017/12-2019/3	Budget	APPROVED

All figures are in Swiss Francs (CHF)

III. Expenditure

Account Groups	Budget	Expenditure					TOTAL	Variance
		Raise humanitarian standards	Grow RC/RC services for vulnerable people	Strengthen RC/RC contribution to development	Heighten influence and support for RC/RC work	Joint working and accountability		
	A					B	A - B	
BUDGET (C)			1,194,697			1,194,697		
Indirect Costs								
Programme & Services Support Recov	72,581		63,475			63,475	9,105	
Total Indirect Costs	72,581		63,475			63,475	9,105	
Pledge Specific Costs								
Pledge Earmarking Fee	4,358		4,393			4,393	-35	
Pledge Reporting Fees	1,130		900			900	230	
Total Pledge Specific Costs	5,487		5,293			5,293	194	
TOTAL EXPENDITURE (D)	1,194,697		1,045,313			1,045,313	149,383	
VARIANCE (C - D)			149,383			149,383		
