


www.ifrc.org  
Saving lives,  
changing minds.

## Emergency Plan of Action (EPoA) Tanzania: Floods in Dar es Salaam

 International Federation  
of Red Cross and Red Crescent Societies

<b>DREF n°: MDRTZ024 / PTZ040</b>	<b>Glide n°: FL-2019-000048-TZA</b>
<b>Date of issue:</b> 27 May 2019 <b>Operation start date:</b> 24 May 2019	<b>Expected timeframe:</b> 3 months <b>Expected end date:</b> 24 August 2019
<b>IFRC Focal point responsible for this operation:</b> Lisa Zitman, DM Delegate, East Africa CCST is responsible for project management and reporting of this operation	<b>National Society focal point responsible for this operation:</b> Mr. Renatus Mkaruka, Director Disaster Management.
<b>Category allocated to the of the disaster or crisis:</b> <b>Yellow</b>	
<b>DREF allocated:</b> CHF 125,828	
<b>Total number of people affected:</b> Approximately 7,800 people (1,560 households)	<b>Number of people to be assisted:</b> 7,800 people (1,560 households) <ul style="list-style-type: none"> <li><b>Direct recipients:</b> 2,500 people (500 households<sup>1</sup>)</li> <li><b>Indirect recipients:</b> Approximately 5,300 people (1,060 households).</li> </ul>
<b>Host National Society presence (n° of volunteers, staff, branches):</b> 50 volunteers in Dar es Salaam branch have been deployed, among which trained BDRT staff, an additional 300 volunteers are available to be deployed. There are 17 trained NDRT members based in Dar es Salaam, of which 10 on standby; 5 staff at HQ ready for immediate deployment (DM & Health).	
<b>Red Cross Red / Crescent Movement partners actively involved in the operation:</b> Spanish Red Cross, Belgian Red Cross-Flanders, IFRC and ICRC.	
<b>Other partner organizations actively involved in the operation:</b> Government of Tanzania, DarMAERT, UN agencies, National and International Non-Governmental Organisations.	

## A. Situation analysis

### Description of the disaster

Heavy rains were reported in Dar es Salaam, starting on 8 May 2019 to-date. According to the Tanzania Meteorological Agency (TMA), these rains are a result of the Inter-Tropical Convergence Belt and led to continuous rainfall and resulting flooding which peaked on 13 May 2019. According to IGAD Climate Prediction Application Centre (ICPAC), much of southern and eastern Tanzania recorded wetter than normal rainfall condition with a few places in southern and eastern Tanzania recording [severely to extremely wet rainfall conditions](#) between 1<sup>st</sup> and 10<sup>th</sup> May 2019. On 23<sup>rd</sup> May 2019, the TMA issued a weather information update stating that rains will continue with significant impact; floods, fishing activities to be interfered, transport network impaired, socio-economic/livelihood will be damaged and increased risk of waterborne and vector borne disease outbreak.



*Submerged houses in Kinondoni Municipality ©TRCS*

<sup>1</sup> Five (5) people per household



TRCS volunteers conducting the initial rapid assessment ©TRCS

The floods caused a significant impact to the people in Dar es salaam leading to damage of properties and livelihoods and putting the affected population at risk of diseases. The initial rapid assessment conducted by TRCS from May 20 to May 23<sup>rd</sup>, indicated that the heavy rains have caused serious flooding in Kinondoni, Temeke and Ilala municipalities of Dar es Salaam. The rains which fell upstream affected eight (8) out of twenty-seven (27) wards of Kinondoni municipality, eleven (11) out of twenty-four (24) Wards of Temeke municipality and eight (8) out of twenty-five (25) Wards of Ilala municipality. The initial rapid assessment conducted by TRCS volunteers reported the following impact:

**Table 1: Summary of floods impact in three affected municipalities of Dar es Salaam**

Kinondoni Municipality	Ilala Municipality	Temeke Municipality
<ul style="list-style-type: none"> <li>- 749 households affected</li> <li>- 2 health facilities flooded</li> <li>- 3 schools damaged</li> </ul>	<ul style="list-style-type: none"> <li>- 713 households affected</li> <li>- 2 deaths reported (1 male and 1 child)</li> </ul>	<ul style="list-style-type: none"> <li>- 54 households affected</li> <li>- 1 health facility flooded</li> <li>- 3 schools damaged</li> </ul>

The flooding has caused displacement of people, who are hosted by friends as well as in temporary public buildings, mainly schools, mosques and churches. A total of 1215 HH have been displaced (from the 1560 HH affected). There is a widespread destruction of physical infrastructure, particularly roads and bridges, some of which have been completely damaged/broken, interfering with communication between neighbouring places within and outside the municipality. The flooding has caused significant damage to houses and has swept away personal household items and belongings as well as other properties including poultry.



Picture 1: Dar es Salaam Regional Commissioner visited affected families in Kinondoni Municipality ©TRCS



Picture 2: School impacted by floods in Kinondoni municipality ©TRCS

In view of the above, Tanzania Red Cross Society (TRCS) is seeking CHF 125,828 from the IFRC Disaster Relief Emergency Fund (DREF) to meet the immediate needs of the flood affected population in the three affected districts of Dar es Salaam (Kinondoni, Temeke and Ilala municipalities). The operation will focus on the distribution of household items (HHIs) as well as provision of WASH and Health needs, targeting a total of 500 households (2,500 people) affected by the ongoing floods in Dar es Salaam.

The DREF operation will also enable the NS to conduct a detailed assessment in order to inform the operation. This assessment will inform any changes to the operational strategy.

## Summary of the current response

### Overview of Host National Society

The current TRCS response and early actions include the following:

- A total of 50 volunteers have been deployed to support the flood response in Dar es Salaam.
- An initial rapid assessment has been conducted in Dar es Salaam to assess the impact of the floods;
- TRCS has been participating in internal and external coordination meetings in Dar es Salaam, with local government, the Dar es Salaam Multi-Agency Emergency Response Team (DARMERT) and other relevant stakeholders.
- TRCS conducted a full stock overview of all the available stock in the central warehouse as well as in the branches;
- TRCS continues to monitor weather forecasts and to share updates with all regional branches;

### Overview of Red Cross Red Crescent Movement in country

TRCS is in constant contact with its in-country Movement partners (Spanish Red Cross, Belgium Red Cross, ICRC) as well as with the Operations Unit of the Eastern Africa Country Cluster Support Team (EA CCST). The following table provides an overview of Movement Partners programs in country:

**Table 2: Overview of RCRC Movement presence in Tanzania**

RCRC Movement Partner	Activities
IFRC	Provides technical support to the TRCS through the EA CCST based in Nairobi, Kenya and facilitates the launch of DREF and Appeal operations.
Belgian Red Cross Flanders	<ul style="list-style-type: none"> <li>- Disaster Preparedness (Pre-positioning of stock for emergency response, warehouse, capacity building of response team).</li> <li>- First Aid</li> <li>- CASH preparedness</li> <li>- WASH</li> </ul>
Spanish Red Cross	WASH
ICRC	<ul style="list-style-type: none"> <li>- RFL services in the refugee camps in Kigoma region</li> <li>- Communication and Dissemination activities with media, TPF/TPDF and</li> <li>- ONS Partnership and development support</li> </ul>

TRCS is currently finalizing procurement of stock for prepositioning, with support from Belgian Red Cross Society (BRCS). This stock will be available for quick response to current situation and will be replenished through this DREF operation.

IFRC EA CCST and Africa Region offices are providing technical support and are monitoring the situation, as well as carrying out overall coordination of the Movement response;

### Overview of non-RCRC actors in country

TRCS branch coordinator in Dar es Salaam is in continuous contact with the Regional Administrative Commissioner (RAS) and the District Administrative Commissioners to make sure that they are informed of the Government plans and participate in responding to affected communities in a coordinated manner. The operation is closely coordinated with *Dar es Salaam Multi-Agency Emergency Response Team (DARMAERT)*. No other actors are yet responding to the floods, DARMAERT has started rapid assessment of the situation. Results of assessments will be shared between DARMAERT and TRCS

## Needs analysis, targeting, scenario planning and risk assessment

### Needs analysis

The floods in Dar es Salaam have caused displacement, injuries, the death of two children, destruction of water & sanitation facilities as well as livelihood assets and increased prevalence and risks of vector transmitted, and water borne diseases. As a direct effect of the ongoing floods, a total number of 21 confirmed Cholera cases were reported by 20th May, with an additional 7 new cases reported between 20th and 22nd of May. One person has died from Cholera on May 22nd. As of 22nd May 2019, a total of 23 new confirmed Cholera cases were reported from Dar es Salaam

region, Ilala (7) and Temeke (5) municipalities<sup>2</sup>. In addition, Tanzania is experiencing one of its highest Dengue fever outbreaks in recent times. As of May 23<sup>rd</sup>, the cumulative number of confirmed Dengue cases in Tanzania is 2,804 and 2 deaths with a (CFR 0.01%), with the majority of cases in Dar es Salaam. Indeed, the heavy rains and floods have increased mosquito breeding sites, increasing Dengue transmission.

## Targeting

This DREF operation will provide assistance to the 500 most vulnerable households (2,500 people) who require urgent humanitarian assistance following the floods in Dar es Salaam. The targeted households will be supported with HH items, WASH and Health interventions. Further needs assessments will be conducted and might lead to this operation being adjusted based on new findings and depending on if/how the rains will continue over the coming weeks.

Persons in need have been identified through an initial rapid assessment conducted by the TRCS branch in Dar es Salaam, using the following selection criteria:

- Elderly people
- People with disabilities
- Chronically ill people
- Child headed households
- Orphans and vulnerable children
- Female-headed households
- Pregnant women

The most vulnerable people have been selected amongst people who have had to leave their homes due to the floods and are residing with host families. Health and hygiene promotion campaigns will include the overall displaced households sheltered in the host communities

## Operation Risk Assessment

The operation is heavy on procurement. Logistics support will be provided through the IFRC Logistic unit in Nairobi, including technical support missions to Tanzania. All procurement files are shared with IFRC Nairobi to review and validate before orders are placed.

To mitigate against security risks, adequate measures have been put in place. This includes, but is not limited to, staff tracking (e.g. via phone or SMS), pre-deployment security/safety briefs, situation monitoring, regular or ad hoc security/safety updates, (field) communication systems and protocols, contingency plans, and the completion of the respective IFRC e-learning courses (i.e. Personal Security, Security Management, Volunteer Security).

TRCS continues to assess and monitor the situation on the ground and will update the operational strategy according to the needs.

## Scenario planning

The below three possible scenarios have been developed for this operation:

Best case scenario	Most likely scenario	Worst case scenario
The rains quickly reduce intensity; <i>no</i> additional people are affected and no secondary effects are suffered e.g. increase in cholera and dengue cases in the current affected areas or other parts of the country.	The rains continue but no more than 50mm in 24 hours in any part of the current affected areas.	The rains continue heavily through May/June, with episodes of more than 50mm in 24 hours in any part of the current affected areas or other parts of the country, resulting in massive displacement of people and destruction of infrastructure and assets.
TRCS Action		
Response will be limited to the proposed DREF operation as captured in this EPoA.	Limited to the current DREF operation, with continued alert and on standby. Engaging with communities for early	Revision of the current DREF operation through an Operations update to widen the scope of intervention, with possible change of strategy, increased timeframe and

<sup>2</sup> Situation Update Cholera #18 23<sup>rd</sup> May 2019, Ministry of Health Tanzania  
MDRTZ024 – Tanzania Floods in Dar es Salaam- DREF EPoA

	warning, preparedness and disaster risk reduction measures.	possibly a request for a second allocation or proceed to a large-scale operation through an application for an Emergency Appeal.
--	---	--

The current DREF operation seeks to respond to the best-case scenario. Any changes to the current plan of action will be informed by field assessments and how situation evolves.

## B. Operational strategy

### Overall Operational objective:

The overall objective of this DREF operation is **to meet the immediate Shelter, WASH and Health related needs of 500 households (2,500 people)** affected by the impact of heavy rain and ensuing floods Kinondoni, Temeke and Ilala municipalities of Dar es Salaam.

### Proposed strategy

Since 8 May heavy rainfall occurred in various parts of the country resulting into floods starting from 13 May, with the most affected area being Dar es Salaam.

The operation will focus on the following activities:

**1. Provision of Shelter related household items (HHIs):** TRCS is focusing on the provision of immediate relief items to the 500 most affected households as a result of the floods. The relief items will include the below:

- Procurement and distribution of 1,000 blankets (2 per household)
- Procurement and distribution of 500 kitchen sets (1 per household)
- Procurement and distribution of 1,000 sleeping mats (2 per household)

A market assessment and cash feasibility study are planned for, to assess the possibility of cash distributions. The operational strategy might be adjusted based on the outcome of this assessment.

**2. Water, Sanitation, and Hygiene:** TRCS will ensure that the targeted 500 households have access to storage facilities and water treatment tablets. In addition, hygiene promotion activities will be conducted and ORP kits deployed to manage cases of Watery Diarrhoea. The activities will include:

- Procurement and distribution of 1,000 water buckets with lids (2 per household)
- Procurement and distribution of 500 collapsible jerry cans (1 per household)
- Procurement and distribution of 2,000 soap bars (4 per household)
- Procurement and distribution of 18,750 water purification tablets (30 tabs per household)
- Hygiene promotion activities (5 mobile cinema sessions and house to house visits, targeting 7,800 people)
- Procurement of 10 Oral Rehydration Point (ORP) kits
- Train 25 staff and volunteers on Operation and Management of ORP
- Deploy the 10 ORP kits to the affected areas
- Procurement of hoes, spades, wheelbarrows and rakes to drain stagnant water during an environmental cleaning exercise

**3. Health and Care:** The TRCS will ensure that affected households have good health practices with a view to reducing the occurrences of water and vector borne diseases such as Malaria, Dengue and diarrhoeal diseases. Health promotion activities will focus mainly on provision of information and prevention of Cholera and Dengue fever. Activities will include:

- Procurement of 1,000 mosquito nets (2 per household)
- Procurement and distribution of 2,000 IEC materials
- Procurement of 500 dignity kits for women and girls of childbearing age
- Procurement of 60 First Aid kits for TRCS response teams
- Organize First Aid training for volunteers
- Conduct health promotion activities, including door to door visits, community campaigns and mobile cinema sessions on Health and Hygiene promotion.

This DREF operation will support the replenishment of stock which can be distributed directly from TRCS warehouses as well as procurement of budgeted items not available in the current stock.

TRCS visibility is maintained through procurement of all items under HHIs, WASH, Health, visibility materials and protective clothing from TRCS stock for the 50 volunteers involved in this operation. Continued assessments and monitoring are also integrated in the operation to ensure that the operation is in line with the evolving situation on the ground.

A lesson learnt workshop will be conducted to review the implementation and a report will be produced for learning and improving future operations.

TRCS responded to floods in Dar es Salaam in 2018. The current operation will build on lessons learnt from last operation, mostly on strengthening community feedback systems and ensure timeliness of response through the availability of prepositioned stock, which were not available in 2018.

An external DREF review is equally planned as part of this operation, with the aim of evaluating recent operations of TRCS using the Preparedness for Emergency Response (PER) post operational assessment as a framework to capture the main learnings and recommendations. The alignment with the PER is expected to ease integration of the findings within TRCS emergency response mechanism, as well as understand the existing capacity of the National Society to manage similar situations (e.g. in the case of recurrent emergencies) in the future.

### **Operational Support Services**

**Human resources:** An initial number of 50 volunteers will be deployed to support the response. All volunteers will be insured and equipped with protective gears. The volunteers will be supervised by the Regional branch coordinator from Dar es Salaam and HQ, under the coordination of the TRCS Director of Disaster Management.

**Logistics and Procurement:** Logistics responsibilities will include sourcing the most urgent and relevant relief items, delivered and distributed equitably to those in need, in a timely, transparent and cost-efficient manner. For the initial response, available prepositioned TRCS stocks will be utilized and replenished through the DREF. Technical support will be provided through the IFRC Regional Logistic Unit in Nairobi.

**Procurement:** Local procurement will be carried out in accordance with the IFRC standard procurement procedures.

**Warehousing:** Warehousing plays a significant role in this operation. The national society will use their national warehouse to store items in advance of distribution activities.

**Communication and Visibility:** To support volunteers in their mission as well as the visibility of Red Cross actions on the ground, TRCS support with protection and visibility items for 50 volunteers including Red Cross bibs, raincoats and gumboots from their existing stock. TRCS will use its own megaphones to evacuate at risk members of the community. Some 2,000 IEC materials will equally be produced to promote hygiene and health awareness.

**Planning, Monitoring, Evaluation and reporting (PMER):** IFRC Eastern Africa CCST will provide TRCS with necessary PMER support, especially with regards to monitoring and reporting of this DREF operation. Regular field visits by TRCS teams will ensure daily/weekly supervision of activities, in the first few weeks of the operation. Continuous needs and situation assessments will be carried out during the DREF implementation to inform decision-making.

Field staff will provide weekly updates/reports about the ongoing operation to the Disaster Response Manager based at the HQ. TRCS will be responsible for providing an operational and financial report (2 months after the end of the operation). This way, IFRC Eastern Africa Cluster can consolidate and ensure publishing within 3 months from the end of operation.

At the end of the operation, a lessons learnt workshop will be organized by TRCS with IFRC and other stakeholders of this operation, to reflect on implementation. This workshop will allow for informed planning in future operations planned and implemented by TRCS, but also will allow the NS to reflect on its disaster readiness status, given that it is prone to flooding.

**Community Engagement and Accountability (CEA):** CEA will be mainstreamed throughout the intervention to guarantee maximum and meaningful participation of the affected communities. A feedback and complaint desk will be put in place for recipients of distributed items to provide direct feedback on the distribution exercise. For the purpose of clarity and for a good flow of information, clear roles and responsibilities will be agreed with representatives, community leaders and committees. The beneficiary selection process will be clearly communicated to all affected. Mobile cinema sessions on hygiene and health promotion will also be instrumental in collecting feedback and respond to community concerns.

**Protection, Gender and Inclusion (PGI):** Acknowledging that women, girls, men and boys with diverse ages, disabilities and backgrounds have very different needs, risk and coping strategies, the operation will pay particular

attention to protection and inclusion of vulnerable groups base and on gender and diversity analysis. Gender roles will be considered when setting up distribution time and dates as well as in health promotion activities.

### C. Detailed Operational Plan



#### Shelter

People targeted: 2,500 people (500 Households)

Male: 1,225

Female: 1,275

Requirements (CHF): 39,458

**Needs analysis:** Through this DREF operation, TRCS will provide HHIs to the 500 most affected HH in Dar es Salaam, to ensure that families minimum needs are met.

**Population to be assisted:** The TRCS will initially support 500 households (2,500 people) with the procurement and distribution of household items.

**Programme standards/benchmarks:** The activities planned in this area of focus will seek to meet the Sphere standards.

P&B Output Code	Shelter Outcome 1: Communities in disaster and crisis affected areas restore and strengthen their safety, well-being and short-term recovery through emergency shelter and settlement solutions	# people/households provided with HHI's (Target: 2,500 people or 500 households)															
	Shelter Output 1.1: Short-term shelter and settlement assistance is provided to affected households	- # of shelter related HH items procured and distributed (Target: 1,000 blankets; 500 kitchen sets, 1,000 mattresses)															
	Activities planned Week	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16
AP005	Procurement and distribution of 1,000 blankets (2 per household)																
AP005	Procurement and distribution of 500 Kitchen kits																
AP005	Procurement and distribution of 1000 Mattresses																
AP005	Post distribution monitoring																



#### Health

People targeted: 7,800 (1560 Households)

Male: 3,822

Female: 3,978

Requirements (CHF): 39,235

**Needs analysis:** The floods have caused outbreaks of water borne and vector borne diseases. Floods also pose a risk of injuries, which would need urgent attention. There is a need to provide health information and promotion to the communities to reduce the risk of further spread of diseases, especially cholera and dengue.

**Population to be assisted:** The TRCS will directly support 500 families with the provision of mosquito nets. First aid (FA) services will be provided as needed. Some 500 women and girls will also be supported with dignity kits. TRCS will indirectly provide support to an additional 5,300 people through health promotion activities.

**Programme standards/benchmarks:** The Sphere standards will guide the implementation of activities under this section and where/if necessary, WHO standards will be adhered to.

P&B Output Code	Health Outcome 1: The immediate risks to the health of affected populations are reduced	# of people/households reached with community-based disease prevention and health promotion programming (Target: 7,800 people or 1560 households)															
	Health Output 1.1: The health situation and immediate risks are assessed using agreed guidelines	<ul style="list-style-type: none"> <li>- # of mosquito nets distributed (Target: 1,000)</li> <li>- Minimum percentage of target population properly using distributed mosquito nets (Target: 80%)</li> <li>- Number of women and girls reached with dignity kits (Target: 500)</li> <li>- Percentage of injured people reached with First aid services (Target: at least 50%)</li> <li>- # of IE materials printed (target: 2,000)</li> </ul>															
	Activities planned Week	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16
AP011	Procurement of 1,000 mosquito nets (2 per household)																
AP019	Procurement and distribution of IEC material (a total number of 2,000 fliers will be printed)																
AP011	Procurement of 500 dignity kits for women and girls																
AP019	Procurement of 60 FA kits for provision of FA services where needed																
AP011	Health promotion targeting 7,800 people																



### Water, sanitation and hygiene

People targeted: 7,800 (1,560 Households)

Male: 3,822

Female: 3,978 Requirements (CHF): 26,511

**Needs analysis:** The floods have caused disruption of water and sanitation infrastructure and services. TRCS will provide water treatment chemicals and hygiene promotion activities to curb any possible water, sanitation and hygiene related diseases and conditions.

**Population to be assisted:** The NS will provide direct support to 2,500 people (500 hhs) and reach out indirectly to an additional 5,300 people (1,060 hhs) through hygiene promotion.

**Programme standards/benchmarks:** The Sphere standards will be used to guide the activities under WASH

P&B Output Code	WASH Outcome1: Immediate reduction in risk of waterborne and water related diseases in targeted communities	# households/people provided with safe water services that meet agreed standards according to specific operational and programmatic context (Target: 1560 households or 7,800 people)															
		- Minimum percentage of water related HH items recipients practicing proper handling of water and storage container (Target: 80%) - # of post-distribution monitoring of water treatment and storage equipment conducted (Target: 2)															
	Activities planned Week	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16
AP026	Procurement and distribution of 1,000 buckets (2 per household)																
AP026	Procurement of 500 collapsible jerry cans (1 per household)																
AP026	Procurement of 2,000 bars of soap (4 per household)																
AP026	Procurement of 18,750 water purification tablets (38 tabs per household)																
P&B Output Code	WASH Output 1.4: Hygiene promotion activities which meet Sphere standards in terms of the identification and use of hygiene items provided to target population	# of households/people reached by hygiene promotion activities (Target: 7,800 people or 1,560 households) - # of hygiene awareness campaigns conducted (Target: 5)															



AP055	Continuous needs assessment carried out to inform programmatic changes relative to population requirements. Market assessment and feasibility study will be carried out in week 1	■			■					■							
AP055	Conduct a lessons learnt workshop										■						
AP055	Conduct a DREF review										■	■					

## D. Budget

The overall allocation required for implementation of this emergency plan of action is CHF 125,828 as detailed in attached budget.


# DREF OPERATION

MDRTZ024 - Floods in Dar es Salaam

24/05/2019

## Budget by Resource

Budget Group	Budget
Clothing & Textiles	32,500
Water, Sanitation & Hygiene	17,563
Medical & First Aid	10,840
Utensils & Tools	11,331
<b>Relief items, Construction, Supplies</b>	<b>72,233</b>
Storage	50
Distribution & Monitoring	3,000
Transport & Vehicles Costs	120
<b>Logistics, Transport &amp; Storage</b>	<b>3,170</b>
Volunteers	15,075
<b>Personnel</b>	<b>15,075</b>
Workshops & Training	12,000
<b>Workshops &amp; Training</b>	<b>12,000</b>
Travel	6,750
Information & Public Relations	5,000
Office Costs	1,000
Communications	2,700
Financial Charges	220
<b>General Expenditure</b>	<b>15,670</b>
DIRECT COSTS	118,148
INDIRECT COSTS	7,680
<b>TOTAL BUDGET</b>	<b>125,828</b>

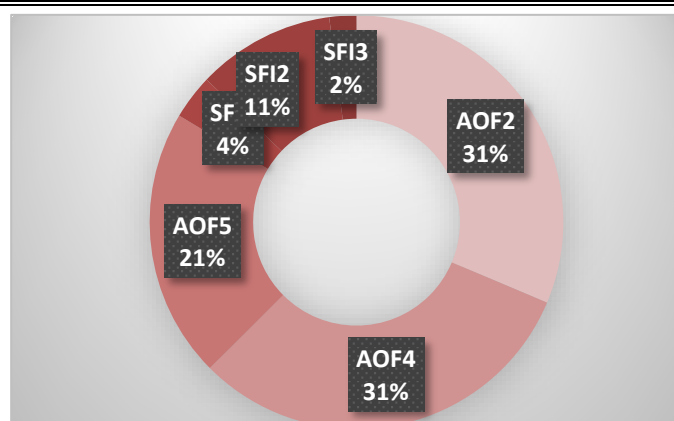

## Budget by Area of Intervention

AOF2 Shelter	39,458
AOF4 Health	39,235
AOF5 Water, Sanitation and Hygiene	26,511
SF11 Strengthen National Societies	4,382
SF12 Effective International Disaster Management	13,579
SF13 Influence others as leading strategic partners	2,663
<b>TOTAL</b>	<b>125,828</b>

## Contact information

### Reference documents



Click here for:

- Previous Appeals and updates
- Emergency Plan of Action (EPoA)

**For further information, specifically related to this operation please contact:**

#### For Tanzania Red Cross (TRCS):

- Julius Kejo, Secretary General TRCS, email: Kejo Julius [kejojulius@trcs.or.tz](mailto:kejojulius@trcs.or.tz)
- Renatus Mkaruka, head of DM TRCS, phone: +255713412791, email: [rmkaruka@trcs.or.tz](mailto:rmkaruka@trcs.or.tz);

#### IFRC Country Cluster Office, Nairobi:

- Andreas Sandin, Ag Head of Cluster, IFRC EACCST; phone: +254732508060; email: [andreas.sandin@ifrc.org](mailto:andreas.sandin@ifrc.org)
- Lisa Zitman, DM Delegate, Tel: +254733203004, email: [lisa.zitman@ifrc.org](mailto:lisa.zitman@ifrc.org);

#### IFRC office for Africa Region:

- Adesh Tripathee, Head of Disaster Crisis Prevention, Response and Recovery, Nairobi, Kenya; phone +254731067489; email: [adesh.tripathee@ifrc.org](mailto:adesh.tripathee@ifrc.org);
- Alina Atemnkeng, DREF Delegate – Africa, phone +254731067277; email: [alina.atemnkeng@ifrc.org](mailto:alina.atemnkeng@ifrc.org);

#### In IFRC Geneva:

- Karla Morizzo, DREF Senior Officer, DCPRR Unit Geneva; email: [karla.morizzo@ifrc.org](mailto:karla.morizzo@ifrc.org);
- Nicolas Boyrie, Ops Coordinator, Senior Officer, DCPRR Unit Geneva; email: [nicolas.boyrie@ifrc.org](mailto:nicolas.boyrie@ifrc.org);

#### For IFRC Resource Mobilization and Pledges support:

- IFRC Africa Regional Office for resource Mobilization and Pledge: Franciscah Cherotich Kilel, Senior Officer Partnership and Resource Development, Nairobi, email: [franciscah.kilel@ifrc.org](mailto:franciscah.kilel@ifrc.org);

#### For In-Kind donations and Mobilization table support:

- IFRC Africa Regional Office for Logistics Unit: Rishi Ramrakha, Head of Africa Regional Logistics Unit, email: [rishi.ramrakha@ifrc.org](mailto:rishi.ramrakha@ifrc.org); phone: +254 733 888 022

#### For Performance and Accountability support (planning, monitoring, evaluation and reporting enquiries)

- **IFRC Africa Regional Office:** Fiona Gatere Regional PMER Coordinator, phone: +254 780 771 139; e-mail: [fiona.gatere@ifrc.org](mailto:fiona.gatere@ifrc.org)

## How we work

All IFRC assistance seeks to adhere to the **Code of Conduct** for the International Red Cross and Red Crescent Movement and Non-Governmental Organizations (NGO's) in Disaster Relief and the **Humanitarian Charter and Minimum Standards in Humanitarian Response (Sphere)** in delivering assistance to the most vulnerable. The IFRC's vision is to inspire, encourage, facilitate and promote at all times all forms of humanitarian activities by National Societies, with a view to preventing and alleviating human suffering, and thereby contributing to the maintenance and promotion of human dignity and peace in the world.

The IFRC's work is guided by Strategy 2020 which puts forward three strategic aims:



**Save lives,**  
protect livelihoods,  
and strengthen recovery  
from disaster and crises.



Enable **healthy**  
and **safe** living.



Promote **social inclusion**  
and a culture of  
**non-violence** and **peace**.



International Federation of Red Cross and Red Crescent Societies  
Fédération internationale des Sociétés de la Croix-Rouge et du Croissant-Rouge  
Federación Internacional de Sociedades de la Cruz Roja y de la Media Luna Roja  
الاتحاد الدولي لجمعيات الصليب الأحمر والهلال الأحمر



## Tanzania, Floods

### DREF

24 May 2019 ● FL-2019-000048-TZA



The maps used do not imply the expression of any opinion on the part of the International Federation of the Red Cross And Red Crescent Societies or National Societies concerning the legal status of a territory or of its authorities. Map data sources: GADM, Natural Earth, IFRC.

