

## Emergency Plan of Action (EPoA) Tunisia: Flash Floods

|                                                                                                                                                                                                                                                                                                                                                                                                                                                       |                                                                                                     |
|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------|
| <b>DREF n° MDRTN009</b>                                                                                                                                                                                                                                                                                                                                                                                                                               | <b>Glide n°:</b> <a href="#">FF-2020-000204-TUN</a>                                                 |
| <b>Date of Issue:</b> 06 October 2020                                                                                                                                                                                                                                                                                                                                                                                                                 | <b>Expected timeframe:</b> 4 months<br><b>Expected end date:</b> 28 February 2021                   |
| <b>Category allocated to the disaster or crisis:</b> <b>Yellow</b>                                                                                                                                                                                                                                                                                                                                                                                    |                                                                                                     |
| <b>DREF allocated:</b> CHF 490,443                                                                                                                                                                                                                                                                                                                                                                                                                    |                                                                                                     |
| <b>Total number of people affected:</b> 40,000 people                                                                                                                                                                                                                                                                                                                                                                                                 | <b>Number of people to be assisted:</b> 10,000 people<br>(2,000 households)                         |
| <b>Provinces affected:</b> Tunis, Sousse, Monastir, Kairouan, Sfax, Mehdiya and Sidi Bouzid, Kef                                                                                                                                                                                                                                                                                                                                                      | <b>Provinces/Regions targeted:</b> Tunis, Sousse, Monastir, Kairouan, Sfax, Mehdiya and Sidi Bouzid |
| <b>Host National Society:</b> Tunisian Red Crescent, 700 volunteers mobilized in 7 branches.                                                                                                                                                                                                                                                                                                                                                          |                                                                                                     |
| <b>Red Cross Red Crescent Movement partners actively involved in the operation:</b> The National Society works closely with International Federation of Red Cross and Red Crescent Societies (IFRC) in this operation. The President of the Tunisian Red Crescent (TRCS) has personally been engaged with the National Health and Disaster Responsible and Emergency and NDRT in this DREF operation from planning, to coordination, and supervision. |                                                                                                     |
| <b>Other partner organizations actively involved in the operation:</b> Tunisian authorities activated the National Disaster Management Team and dispatched police forces, civil defence, army and rescue teams to some regions in response to the crisis.                                                                                                                                                                                             |                                                                                                     |

### A. Situation analysis

#### Description of the disaster

Heavy rainfall began around 12 September when Monastir, a capital of the Monastir Governorate in the center of the country, and many other towns around recorded 47.8 mm of rain in 24 hours, and Sidi Bouzid and many other towns of this governorate 58 mm. During the same period, Mahdia and all belonging localities recorded more than 40 mm of rain in 24 hours during 3 separate days. Kairouan recorded 89 mm of rain. Kef governorate registered similar amounts of rain especially in Sers locality. During that period almost an average of a monthly rain was registered.


Flooding and related fatalities were reported in the governorates of Monastir, Sousse, Mahdia, Sfax and Tunis, according to the country's Civil Protection Agency. Floods struck several districts of the capital, Tunis. Some areas were under 1 meter of water, leaving roads impassable and buildings damaged. Orthopedic hospital in the governorate of Manouba was flooded; water reaching archives and hospitalization rooms. National Institute of Meteorology (Institut national de la météorologie) of Tunisia issued warnings for further heavy rainfall on 13 and 14th of September. Consequently, floodwater surged through many different districts damaging infrastructure, houses, properties, and livelihoods of the community members.

During this period, media reports said at least 6 people have died in floods after days of torrential rainfall in Tunisia, hundreds were rescued and thousands of homes damaged.

More than 40,000 people have been affected by the floods. Some of them fled their homes seeking shelter in neighboring high-ground houses and communities, while other chose to stay in their damaged houses moving to rooftops rather than

risking crossing flooded areas to reach evacuation points. Water supply through pipelines is limited, and the water available in some areas is contaminated. Electricity has been cut off in certain districts to avoid risk to people and electrical damage.

The below photos show the flashfloods damages.

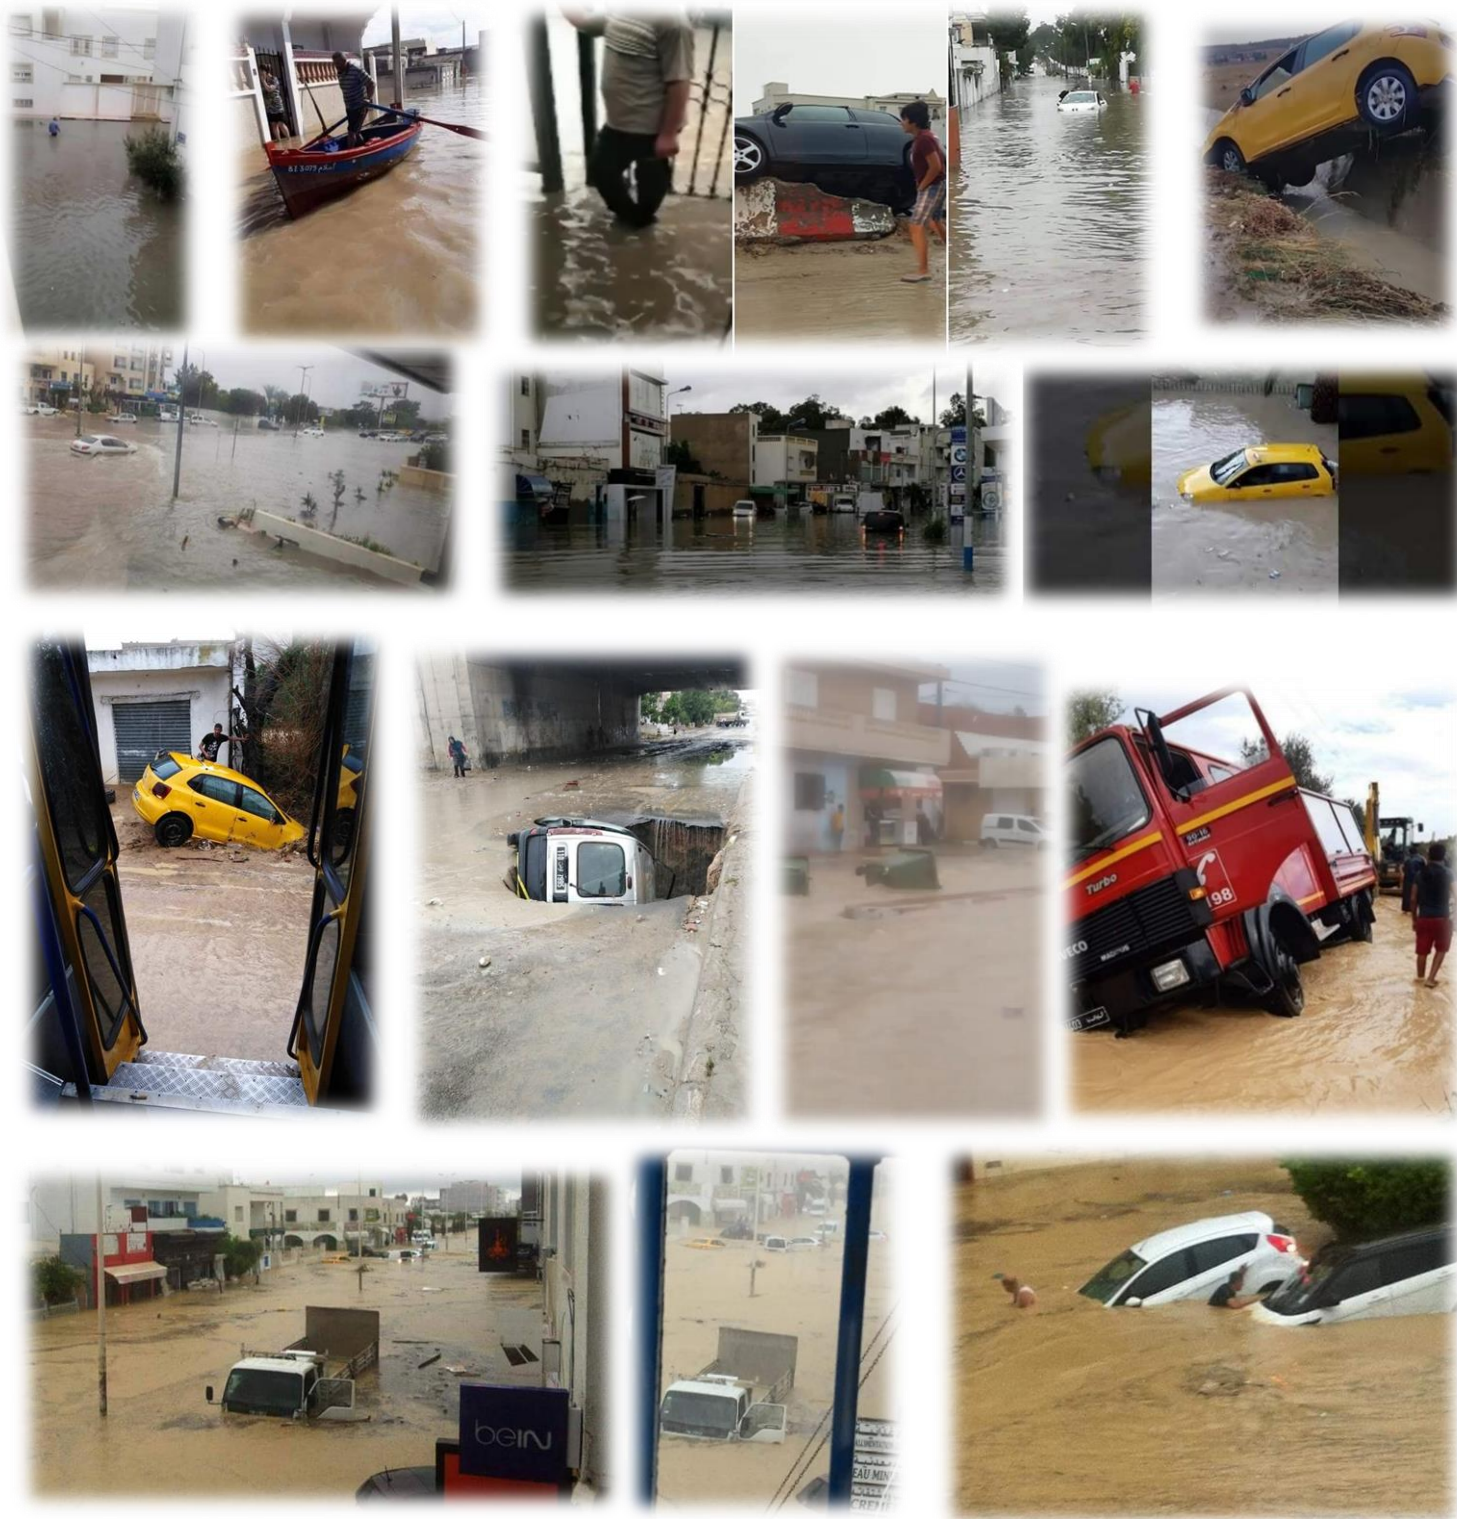

## Summary of the current response

### Overview of Host National Society Response Action

The Tunisian Red Crescent Society (TRCS) branches staff and volunteers are currently conducting initial rapid needs assessment supported by National Disaster Response Team members (NDRT), together with the Local Disaster Response Team (LDRT). Altogether, seven branches are coordinating the overall response, meetings, and interviews with affected communities and authorities to get more information on the situation and identify the eminent needs.

TRCS volunteers are providing psychosocial support to the traumatised people as they witnessed the sudden inundation of water into their houses and surrounding land.

TRCS is actively engaging in meetings with all relevant stakeholders at national and regional levels level to discuss the response plan and deliver a coordinated operation. TRCS continues to attend regular Government led coordination meetings as appropriate and applicable.

Flooding overwhelmed the local response capacity. TRCS in coordination with the local authorities and several organisations have deployed its volunteers to help clean the flooded area of debris, mud, and to drain the flood waters.



*TRCS volunteers mobilized to help clean the flooded areas*

The below photos show the TRCS response to the floods.



### Overview of Red Cross Red Crescent Movement Actions in country

The IFRC provides technical and financial support to TRCS through its Northern Africa Country Cluster Support Team (CCST) and the Middle East and North Africa (MENA) Regional Office based in Lebanon. IFRC is working closely with TRCS to assess the situation as well as to identify priority needs and capacity gaps which need to be enhanced.

IFRC MENA Regional Office will continue to provide technical inputs in planning and implementation and undertake monitoring and evaluation of the operation. IFRC, through a DREF operation, will support TRCS in their immediate emergency response to the needs of the flood-affected people.

## Overview of other actors in country

Local authorities dispatched police forces, army and rescue teams to some regions. Municipalities assisted the affected people by providing shelters in public places and providing some basic needs. Civil defense is helping people to extract water from their houses.

Other local organizations, in coordination with TRCS are collecting in-kind donations to be distributed to the affected people.

The below photos show the flashfloods damages.





## **Needs analysis, targeting, and risk assessment**

### **Needs analysis:**

TRCS actually relies on data collected from the initial rapid assessment conducted by TRCS branches, NDRT, LDRT, and local committee members.

#### **Detailed needs assessment:**

For the moment, only rapid assessments have been conducted. As such, it is important to support NS participation at the joint needs assessment with municipalities. Based on information gathered through the initial needs' assessment, the identified needs are related to food, household items (HHIs), shelter, safe drinking water, health, sanitation and hygiene.

In order to ensure that the community is engaged at the activities design level as per their perspectives, priorities, and needs, and to fulfil their mandate, TRCS will be providing support to the most vulnerable where specific needs are identified in line with the findings of their assessments. This DREF is launched based on preliminary information collected by TRCS branches and may be revised in the coming weeks once detailed assessments are completed and results are shared.

#### **Shelter and household items:**

Due to the floods, many homes were damaged, and household items and assets were washed away. The initial needs assessment by TRCS is to provide affected households with emergency shelter options as rains are forecasted to continue in the coming days, but also to enable them to protect their remaining possessions.

Due to many belongings being lost or damaged beyond repairs, there is also need for mattresses, blankets, clothes, food stocks, hygiene materials, schoolbooks, etc. All affected houses will need clean up and sanitation in order to be habitable again. Many houses need prompt repair especially damaged roofs and inside electric network. The provision of shelter items and household items will ensure the affected households get protection from diseases, specifically respiratory illnesses, water transmitted diseases and ensure they can maintain privacy and dignity.

#### **Health and care:**

While the Health Minister has been coordinating the provision of emergency health services to the affected population in the seven-targeted governorates through existing health facilities, health and hygiene promotion through individual household visits or community campaigns due to the COVID-19 restrictions are vital for the prevention of waterborne diseases and diarrhea.

The health and hygiene promotion activities will also improve and promote health-seeking behaviors, while vector control activities will prevent diseases outbreaks, such as dysentery and insects and little rodents transmitted diseases.

### **Water, Hygiene and Sanitation (WASH):**

Due to flooding, access to drinking water is a major issue. The safe water supply through pipelines have been contaminated. Affected families are also at health risks due to flooded pit latrines, water wells and contaminated surrounding areas.

Assistance on water and sanitation is therefore essential. With stagnant waters lying all over and inadequate waste disposal. TRCS will consider implementing vector control actions such as clean-ups campaigns and spraying, to be done with the supervision and support of Municipalities and civil defense for drainages

The proposed activities in this operation are designed to complement the ongoing response activities to cover the existing gaps in emergency shelter/ HHs, health education and environmental sanitation in the most-affected areas of the seven-targeted states.

### **Targeting:**

This DREF operation will target 2,000 affected families (10,000 people) in 7 governorates (Tunis, Sousse, Monastir, Kairouan, Sfax, Mehdiya and Sidi Bouzid), as per the coordination agreement with the local authorities and other internal actors.

Persons in need will be identified through the assessments being conducted by the TRCS with the support of branches and authorities. Targeting will aim to identify the most vulnerable among:

- Women;
- Children;
- Elderly people;
- Peasants.

Affected people living in villages will be prioritised for response, as they are most vulnerable.

### **Operation Risk Assessment:**

Weather forecasted for the coming days shows rainfall in most of the country and flood warnings have been issued. If heavy rainfall occurs again in the area, it may delay the distributions as roads may become impassable, more people will be affected, impact would be higher, and more health concerns will be aroused.

TRCS would closely monitor the situation through its network of local committees and volunteers across the country and revise the DREF when necessary.

During the lessons learnt exercise in the 2018 floods, local procurement has been identified as one of the biggest challenges to the timely implementation of the operation, the IFRC RO and the CCST are working closely with the National Society to facilitate the procurement process and provide the necessary support to the NS.

The current DREF operation and its operational strategy considers the risks related to the current COVID-19 pandemic and is aligned with the IFRC global emergency appeal that supports National Societies to deliver assistance and support to communities affected or at risk of being affected by the COVID-19 (novel coronavirus) outbreak.

As auxiliaries to public authorities, Red Cross and Red and Crescent National Societies have a strong role to play in supporting domestic operations focused on preparedness, containment, and mitigation against the pandemic. National Society responses to COVID-19 are supported through the global appeal, which will facilitate supporting them to maintain critical service provision, while adapting to COVID-19. Business continuity plans for IFRC at all levels have been developed and are continuously being adapted as the situation changes. Focus is given to supporting National Societies to maintain critical service provision through ongoing operations, while adapting to COVID-19. This includes ensuring the health and safety of staff and volunteers and developing plans specifically for emergency health service provision where relevant. As such, the National Society actions dedicated to COVID-19 and those conducted through ongoing operations will be mutually beneficial and built upon common synergies.

TRCS will continue emphasizing the communities to take precaution and preventive measures. TRCS will use the country guideline for preparedness and response to COVID 19 to communicate risks during elections. TRCS will use Risk Communication and Community Engagement approach to disseminate COVID-19 messages to the communities. Local medias, influential people and social mobilization structures will be used and resources trained under COVID-19 response will be activated for the same. All staff and volunteers engaged in elections response will be oriented on COVID 19 preventive measures and provided with PPE for their safety

This DREF operation is aligned with and will contribute to the current [global strategy](#) and [Regional Emergency Plan of Action for COVID-19](#) developed by the IFRC MENA Regional Office, in coordination with global and regional partners. IFRC continues to assess how emergency operations in response to disasters and crisis should adapt to this crisis and provide necessary guidance to its membership on the same. The NS will keep monitoring the situation closely, focusing on the health risks, and revise accordingly if needed taking into consideration the evolving COVID-19 situation and the operational risks that might develop, including operational challenges related to access to the affected population, availability of relief items and procurement issues, and movement of NS volunteers and staff as well as international staff. For more information please consult the Covid-19 operation page on the IFRC Go platform.

To note that new cases are increasingly registered in the country and the National Society is monitoring the situation should it affect the operation implementation.

## B. Operational strategy

### Overall Operational objective:

This DREF operation aims to deliver emergency assistance and humanitarian relief to 2,000 flood-affected households in seven governorates for 4 months. In addition to providing food baskets and HHs, the National Society will carry out psychosocial support and environmental sanitation campaigns. The proposed strategy is formulated based on the initial and short-term needs assessment of the affected people.

The following initial activities will be implemented:

#### 1- **Emergency Shelter/ Household Items: (Target: 10,000 people or 2,000 HH)**

The DREF operation will ensure the provision of the Emergency shelter as well as the distribution of household items for 2,000 HHs/10,000 people who are residing with host families or in temporary shelters in public spaces provided by the authorities. Items will include mattresses and blankets per household in the seven governorates.

#### 2- **Food Security: (Target: 10,000 people or 2,000 HHs)**

Food baskets containing essential food ingredients in Tunisian culture will be procured and distributed to 2000 HHs. Items will involve 6 Kg of Spaghetti, 4 kg tomato paste, 2 kg rice, 5 kg couscous, 2 kg of sugar, 0.25 kg salt, 0.25 kg coffee, 0.25 kg tea, and 3 litres oil.

#### 3- **Health and care: (Target: 10,000 people or 2,000 HHs)**

TRCS volunteers provided psychosocial first aid (PFA) as part of their response and will continue to do so for the affected and people. Another 100 volunteers will be trained on Mental Health and Psychosocial Support (MHPSS) . TRCS Community Based Health and First Aid (CBHFA) teams will carry on health awareness sessions on the various potential health risks, such as water borne diseases due to polluted water (diarrhoea), acute respiratory infections (including COVID-19) . Additionally, TRCS will deploy mobile clinics to the shelters and the locations lacking health care in support of the health authorities.

#### 4- **Water, Hygiene and Sanitation: (Target: 10,000 people or 2,000 HHs)**

Hygiene kits will require procurement and distribution for 2,000 HHs. The kit will include: 5 soap bars, 5 toothbrushes, 5 toothpaste, 5 shampoos, surgical masks and one alcohol gel item.

TRCS will also organise clean-up/environmental sanitation campaigns for a clean and safe environment for the flood-affected people at several stages throughout the operation.

Most vulnerable families who lost access to decent latrines will be supported to dig a septic tank and to install a Turkish style latrine. Also, training will be offered to these families to do a proper maintenance of these latrines.

### **Community Engagement and Accountability (CEA):**

Community Engagement and accountability (CEA) function is at the core of the response and should integrate CEA minimum actions that help put communities at the centre of the response, by ensuring communication and participation throughout the program cycle.

To inform its interventions and begin the selection process, the TRCS has initiated the rapid needs assessment so that the intervention modality is driven by community perspectives as well as observed needs.

While implementing the DREF operation, TRCS will continue to assess the situation to facilitate an appropriate response strategy. Depending on the needs, the strategy may need to be reviewed to ensure the National Society is properly resourced and supported to provide life-saving operational activities.

A beneficiary satisfaction survey will be conducted to collect the views of the population on support provided. This will also help to gauge impact of the overall operation in the affected community and inform planning of future responses. Satisfaction surveys will also be used for gathering feedback and complaints and act upon them accordingly to make corrective actions.

TRCS will ensure continuation of activities and plan for an exit strategy during the implementation of the DREF operation. A lesson learnt workshop will be conducted to review the implementation and a report will be produced for future learning.

The IFRC regional CEA unit and in collaboration with IFRC country office will be providing needed technical support throughout this program and beyond which will include training to staff and volunteers such as (Feedback mechanism, Risk Communication skills, Rapid assessment), CEA policy reviews, and in setting-up/scaling-up feedback mechanism through diversity of channels. The IFRC will also provide technical support and guidance in conducting the after action lessons learnt workshop and utilizing its results to inform future projects. The IFRC will keep on supporting TRCS with risk communication technical support related to COVID-19 messaging throughout this DREF.

### **Protection Gender and Inclusion (PGI):**

PGI will be mainstreamed throughout the intervention to ensure communities dignity, access, participation and safety.

Acknowledging that women, girls, men and boys with diverse ages, disabilities and backgrounds have very different needs, risk and coping strategies, the operation will pay particular attention to protection and inclusion of vulnerable groups and on gender and diversity analysis.

TRCS volunteers are taking shifts on a 24-hour a day in several branches, monitoring for protection issues and gender-based violence.

### **Operational Support Services**

#### **• Human Resources**

Given that TRCS deploys its volunteers per sector, 700 volunteers will be mobilized for the implementation of this emergency operation in the seven target governorates. If more support is required, volunteer mobilisation will be requested from each local community.

The above-mentioned volunteers will be provided with additional training, insurance coverage, as well as visibility items, facemasks and hand sanitizer for protection in view of the COVID-19 pandemic.

Three TRCS staff will be hired for this operation: a team leader, a Legal Officer and a Logistics Assistant. Meanwhile other TRCS staff will provide all necessary support to the operation.

#### **• Logistics and supply chain**

TRCS has one main warehouse with a big storage capacity. There are several storage spaces in the different local branches where stocks will be mobilized from warehouse to storage spaces before distribution.

However, TRCS own warehouses were seriously inundated and damaged by the flooding; the need for repairs in order to face the DREF operation is heavily recognized and should be addressed. TRCS is requesting the covering of repair costs of three warehouses in Kairouan, Sidi Bouzid and Megrine).

The HHIs needed for the operation will be carried out using TRCS local procurement channels. No international procurement will be conducted. IFRC Regional logistics support will be provided throughout the operation phase to support this process.

#### **• Communications**

Constant contact with the TRCS volunteers and branches as well as effective communication between all levels of the operation will be maintained throughout. Periodic meetings will be held to provide updates and information on progress.

Publications will be shared both locally and internationally on different platforms including Facebook and Twitter. Information will be continuously shared with the IFRC Cluster office for further dissemination with partners and donors, including articles and photos.

#### **• Security**

Security risks vary considerably between different regions across Tunisia. There is a latent militant threat in Tunisia with government targets and tourist areas targeted in the past. There are no other significant security concerns in the affected region other than those associated with incidental threats due to the flooding. Covid-19 remains a threat, however.

TRCS will work closely and coordinate with the local authorities, and other partners to ensure access to the intervention areas by the TRCS volunteers and staff. The TRCS will mobilize 700 volunteers and ensure adequate insurance as per the IFRC Global Insurance policy.

#### **• Planning, monitoring, evaluation, & reporting (PMER)**

IFRC CCST will provide TRCS with the necessary PMER support, especially concerning monitoring and reporting of this DREF operation.

Regular monitoring of activities and disaster situation generally will be carried out by TRCS and IFRC, which will monitor implementation of the DREF operation and support coordination. TRCS and IFRC will dedicate PMER capacity to the operation to maintain timely and standard reporting against the set objectives of the response operation.

A lessons learnt workshop will also be held at the end of the operation to ensure that feedback from volunteers is obtained and to identify strengths or weaknesses to address them and inform future planning.

#### **• Community Engagement and Accountability**

Community engagement and accountability activities will be carried out including community meetings to share information and collect feedback, along with setting up of feedback desks during distributions and sharing information on entitlements.

#### **• Administration and Finance**

TRCS administration and finance unit will be closely involved to support the financial management of the operation. IFRC Regional office will provide support to ensure quality and adherence of standards and procedures.

## C. Detailed Operational Plan



### Shelter

People targeted: 10,000

Male: 5,000

Female: 5,000

Requirements (CHF): 149,100

**Needs analysis:** Many houses were partially or fully damaged. Affected people are taking shelter with relatives and friends after they have lost most of their assets. These people have lost their household effects including mattresses and blankets.

**Population to be assisted:** 10,000 people (2,000 households) in the seven governorates: Tunis, Sousse, Monastir, Kairouan, Sfax, Mehdi and Sidi Bouzid.

**Programme standards/benchmarks:** The activities under this sector will seek to meet the SPHERE standards.

| P&B<br>Output<br>Code | Shelter Outcome 1: Communities in disaster and crisis affected areas restore and strengthen their safety, well-being and longer-term recovery through shelter and settlement solutions | # of families having received shelter NFIs. (Target: TBD) |   |   |   |   |   |   |   |   |    |    |    |    |    |    |    |
|-----------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------|---|---|---|---|---|---|---|---|----|----|----|----|----|----|----|
|                       | Shelter Output 1.1: Short, medium and long-term shelter and settlement assistance is provided to affected households                                                                   | # of NFI sets procured and distributed (Target: 2,000)    |   |   |   |   |   |   |   |   |    |    |    |    |    |    |    |
|                       | Activities planned<br>Week                                                                                                                                                             | 1                                                         | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 |
| AP005                 | Identification of caseloads and verification of beneficiaries in different target groups – inclusion factors integrate gender, diversity and disability in the response                | X                                                         | X | X | X | X | X | X | X | X | X  | X  | X  |    |    |    |    |
| AP005                 | Identification of the appropriate modality of support for each caseload                                                                                                                | X                                                         | X | X | X | X | X | X | X | X | X  | X  | X  |    |    |    |    |
| AP005                 | Identification of community participation modalities in program design and implementation                                                                                              | X                                                         | X | X | X | X | X | X | X | X | X  | X  | X  |    |    |    |    |
| AP005                 | Coordination with government and other stakeholders                                                                                                                                    | X                                                         | X | X | X | X | X | X | X | X | X  | X  | X  |    |    |    |    |
| AP005                 | Analysis of the local market to identify availability/access to shelter and household items                                                                                            | X                                                         |   | X | X |   |   |   |   |   |    |    |    |    |    |    |    |
| AP005                 | Distribution of the household items to the affected population                                                                                                                         | X                                                         | X | X | X | X | X | X | X | X | X  | X  | X  |    |    |    |    |
| AP005                 | Evaluation of the shelter support provided                                                                                                                                             |                                                           |   |   | X |   |   |   | X |   |    |    | X  |    |    |    |    |



## Livelihoods and basic needs

**People targeted: 10,000**

Male: 5,000

Female: 5,000

**Requirements (CHF) 25,560**

**Needs analysis:** The project targets vulnerable households directly affected by the floods through damage to their homes and food stocks. Initial assessment is currently carried out on the basic needs. One food basket will be distributed as a one-month food rotation.

**Population to be assisted:** 10,000 people (2,000 households) in the seven governorates: Tunis, Sousse, Monastir, Kairouan, Sfax, Mehdi and Sidi Bouzid.

**Programme standards/benchmarks:** Sphere standards on the definition of food assistance based on energy coverage of 2,100 kcal/person/day

| P&B<br>Output<br>Code | Livelihoods and basic needs Output 1.2: Basic needs assistance for livelihoods security including food is provided to the most affected communities | # of people provided with basic needs assistance including food.<br>(Target: TBD) |   |   |   |   |   |   |   |   |    |    |    |    |    |    |    |
|-----------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------|---|---|---|---|---|---|---|---|----|----|----|----|----|----|----|
|                       |                                                                                                                                                     | 1                                                                                 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 |
| AP008                 | Procurement and packaging food parcels for 2000 HHs                                                                                                 |                                                                                   |   | X | X | X | X | X | X | X |    |    |    |    |    |    |    |
| AP008                 | Defining beneficiary selection                                                                                                                      |                                                                                   |   | X |   | X |   | X |   |   |    |    |    |    |    |    |    |
| AP008                 | Basic food distributions                                                                                                                            |                                                                                   |   |   |   |   |   |   |   | X | X  | X  | X  |    |    |    |    |



## Health

**People targeted: 10,000**

Male: 5,000

Female: 5,000

**Requirements (CHF) 12,780**

**Needs analysis:** The affected households from the floods have been traumatised from the crisis and are in need for psychosocial support. TRCS CBHFA teams will carry on health awareness sessions on the various potential health risks, such as water born disease due to polluted water (diarrhoea), allergies related to the drying floods and acute respiratory infections, include covid -19. Additionally, TRCS will deploy mobile clinics to the shelters and the location lacking health care in support of the health authorities during the DREF operation.

**Population to be assisted:** 10,000 people or 2,000 households in the 7 governorates.

**Programme standards/benchmarks:** The activities implemented under this section will seek to meet Sphere standards.

| P&B Output Code | Health Output 1.2: Target population is provided with rapid medical management of injuries and diseases         |   |   |   |   |   |   | # of people provided with clinical health care services during emergencies (Target: TBD) |   |   |    |    |    |    |    |    |    |
|-----------------|-----------------------------------------------------------------------------------------------------------------|---|---|---|---|---|---|------------------------------------------------------------------------------------------|---|---|----|----|----|----|----|----|----|
|                 | Activities planned Week                                                                                         | 1 | 2 | 3 | 4 | 5 | 6 | 7                                                                                        | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 |
| AP022           | Deployment of mobile clinics in shelters and communities                                                        |   | X | X | X | X | X | X                                                                                        | X | X | X  | X  | X  |    |    |    |    |
| P&B Output Code | Health Output 1.3: Community-based disease prevention and health promotion is provided to the target population |   |   |   |   |   |   | # of people reached by community-based health activities. (Target: TBD)                  |   |   |    |    |    |    |    |    |    |
|                 | Activities planned Week                                                                                         | 1 | 2 | 3 | 4 | 5 | 6 | 7                                                                                        | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 |
| AP021           | Training of 100 volunteers on CBHFA                                                                             |   |   |   | X | X |   |                                                                                          |   |   |    |    |    |    |    |    |    |
| AP021           | Deploy CBHFA volunteers in the affected communities and in the shelters                                         |   |   | X | X | X | X | X                                                                                        | X | X | X  | X  | X  |    |    |    |    |
| P&B Output Code | Health Output 1.5: Psychosocial support provided to the target population                                       |   |   |   |   |   |   | # of people reached by psychosocial support. (Target: TBD)                               |   |   |    |    |    |    |    |    |    |
|                 | Activities planned Week                                                                                         | 1 | 2 | 3 | 4 | 5 | 6 | 7                                                                                        | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 |
| AP023           | Training of 100 volunteers on MHPSS                                                                             |   |   |   |   | X |   |                                                                                          |   |   |    |    |    |    |    |    |    |
| AP023           | Psychosocial support is provided by volunteers throughout the response and operation                            | X | X | X | X | X | X | X                                                                                        | X | X | X  | X  | X  |    |    |    |    |
| P&B Output Code | Health Output 2.3: Community -based disease prevention and health promotion measures provided.                  |   |   |   |   |   |   | # of people reached with health promotion messaging. (Target: TBD)                       |   |   |    |    |    |    |    |    |    |
|                 | Activities planned Week                                                                                         | 1 | 2 | 3 | 4 | 5 | 6 | 7                                                                                        | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 |
| AP011           | Monitor the health situation in shelters and communities and alert the health authorities for outbreaks         | X | X | X | X | X | X | X                                                                                        | X | X | X  | X  | X  |    |    |    |    |



## Water, sanitation and hygiene

**People targeted: 10,000**

Male: 5,000

Female: 5,000

**Requirements (CHF) 214,172**

**Needs analysis:** The heavy rains have affected an estimated 40,000 peoples in Tunisia. The consequences have also impacted the water and sanitation facilities of the population (households and communities)

|                       |                                                                                                                                                                 |                                                                                                                                                          |   |   |   |   |   |                                                                                                                         |   |   |   |    |    |    |    |    |    |    |
|-----------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------|---|---|---|---|---|-------------------------------------------------------------------------------------------------------------------------|---|---|---|----|----|----|----|----|----|----|
| P&B<br>Output<br>Code | WASH Outcome1: Immediate reduction in risk of waterborne and water related diseases in targeted communities                                                     |                                                                                                                                                          |   |   |   |   |   | # of people reached by NS with services to reduce relevant health risk factors. (Target: TBD)                           |   |   |   |    |    |    |    |    |    |    |
|                       | WASH Output 1.1: Continuous assessment of water, sanitation, and hygiene situation is carried out in targeted communities                                       |                                                                                                                                                          |   |   |   |   |   | # of assessments conducted based on standard IFRC and / or WHO assessment guidelines. (Target: TBD)                     |   |   |   |    |    |    |    |    |    |    |
|                       | Activities planned<br>Week                                                                                                                                      |                                                                                                                                                          | 1 | 2 | 3 | 4 | 5 | 6                                                                                                                       | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 |
| AP026                 | Conduct initial assessment of the water, sanitation and hygiene situation in targeted communities                                                               | X                                                                                                                                                        | X | X |   |   |   |                                                                                                                         |   |   |   |    |    |    |    |    |    |    |
| AP026                 | Continuously monitor the water, sanitation and hygiene situation in targeted communities                                                                        |                                                                                                                                                          |   | X | X | X | X | X                                                                                                                       | X | X | X | X  | X  |    |    |    |    |    |
| P&B<br>Output<br>Code | WASH Output 1.4: Hygiene promotion activities which meet Sphere standards in terms of the identification and use of hygiene items provided to target population |                                                                                                                                                          |   |   |   |   |   | # households reached with key messages to promote personal and community hygiene. (Target: TBD)                         |   |   |   |    |    |    |    |    |    |    |
|                       | Activities planned<br>Week                                                                                                                                      |                                                                                                                                                          | 1 | 2 | 3 | 4 | 5 | 6                                                                                                                       | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 |
|                       | AP029                                                                                                                                                           | Conduct needs assessment: define hygiene issues and assess capacity to address the problem.                                                              | X | X | X | X |   |                                                                                                                         | X | X | X | X  |    | X  |    |    |    |    |
| AP029                 | Assess progress and evaluate results.                                                                                                                           |                                                                                                                                                          |   |   | X |   |   |                                                                                                                         | X |   |   |    | X  |    |    |    |    |    |
| P&B<br>Output<br>Code | WASH Output 1.5: Hygiene-related goods (NFIs) which meet Sphere standards and training on how to use those goods is provided to the target population           |                                                                                                                                                          |   |   |   |   |   | # households reached with awareness raising activities on improved treatment and safe use of wastewater . (Target: TBD) |   |   |   |    |    |    |    |    |    |    |
|                       | Activities planned<br>Week                                                                                                                                      |                                                                                                                                                          | 1 | 2 | 3 | 4 | 5 | 6                                                                                                                       | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 |
|                       | AP030                                                                                                                                                           | Determine the needs for hygiene kits, including soap, water storage for each community based on health risks and user preference in targeted communities | X | X |   |   |   |                                                                                                                         |   |   |   |    |    |    |    |    |    |    |
| AP030                 | Distribute 2000 hygiene kits, sufficient for 2 months to 10,000 people.                                                                                         |                                                                                                                                                          |   |   |   | X | X | X                                                                                                                       | X | X | X | X  | X  |    |    |    |    |    |
| AP030                 | Determine whether additional distributions are required and whether changes should be made.                                                                     |                                                                                                                                                          |   |   |   |   |   |                                                                                                                         | X |   |   |    | X  |    |    |    |    |    |
| AP030                 | Training of 100 volunteers on hygiene promotion                                                                                                                 |                                                                                                                                                          |   |   |   | X |   |                                                                                                                         |   |   |   |    |    |    |    |    |    |    |
| P&B<br>Output<br>Code | WASH Outcome 2: Sustainable reduction in risk of waterborne and water related diseases in targeted communities in the recovery phase                            |                                                                                                                                                          |   |   |   |   |   | Please include an indicator from the Key Data Sheet with a target TBD                                                   |   |   |   |    |    |    |    |    |    |    |
|                       | WASH Output 2.1: Continuous monitoring and evaluation of water, sanitation, and hygiene situation is carried out in targeted communities                        |                                                                                                                                                          |   |   |   |   |   | Please include an indicator from the Key Data Sheet with a target TBD                                                   |   |   |   |    |    |    |    |    |    |    |

|                       | Activities planned<br>Week                                                                                                           | 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 |
|-----------------------|--------------------------------------------------------------------------------------------------------------------------------------|---|---|---|---|---|---|---|---|---|----|----|----|----|----|----|----|
| AP026                 | Continuously monitor the water, sanitation and hygiene situation in targeted communities                                             | X | X | X | X | X | X | X | X | X | X  | X  | X  |    |    |    |    |
| P&B<br>Output<br>Code | <b>WASH Output 2.3: Improved access to and use of adequate sanitation by the target population. is provided to target population</b> |   |   |   |   |   |   |   |   |   |    |    |    |    |    |    |    |
|                       | Activities planned<br>Week                                                                                                           | 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 |
| AP028                 | Carry out environmental sanitation campaigns: drainage, vector control, and solid waste in targeted communities.                     | X |   |   |   | X |   |   |   | X |    |    |    |    |    |    |    |



### Protection, Gender and Inclusion

People targeted: 2,500

Requirements (CHF) Cost Included with other trainings

**Needs analysis:** Around 500 families fled their homes to seek shelter in the neighborhood or with their relatives.

**Population to be assisted:** 2,500 people or 500 households in the most affected areas.

**Programme standards/benchmarks:** The activities implemented under this section will seek to meet Sphere and WHO

|                       |                                                                                                                                                                                                                                                                                 |                                                                              |   |   |   |   |   |   |   |   |    |    |    |    |    |    |    |
|-----------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------|---|---|---|---|---|---|---|---|----|----|----|----|----|----|----|
| P&B<br>Output<br>Code | <b>Inclusion and Protection Outcome 1: Communities identify the needs of the most vulnerable and particularly disadvantaged and marginalised groups, as a result of inequality, discrimination and other non-respect of their human rights and address their distinct needs</b> | Please include an indicator from the Key Data Sheet with a target <b>TBD</b> |   |   |   |   |   |   |   |   |    |    |    |    |    |    |    |
|                       | <b>Inclusion and Protection Output 1.2: Emergency response operations prevent and respond to sexual- and gender-based violence and all forms of violence against children.</b>                                                                                                  | Please include an indicator from the Key Data Sheet with a target <b>TBD</b> |   |   |   |   |   |   |   |   |    |    |    |    |    |    |    |
|                       | Activities planned<br>Week                                                                                                                                                                                                                                                      | 1                                                                            | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 |
| AP034                 | Use Minimum Standard Commitments as a guide to support sectorial teams to include measures to mitigate the risk of SGBV                                                                                                                                                         | X                                                                            | X | X | X | X | X | X | X | X | X  | X  | X  |    |    |    |    |
| AP034                 | Include messages on preventing and responding to SGBV in all community outreach activities                                                                                                                                                                                      | X                                                                            | X | X | X | X | X | X | X | X | X  | X  | X  |    |    |    |    |

**Requirements (CHF) 88,832**

|                       |                                                                                                                                                                                                                                                                                  |                                                                                 |   |   |   |   |   |   |   |   |    |    |    |    |    |    |    |
|-----------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------|---|---|---|---|---|---|---|---|----|----|----|----|----|----|----|
| P&B<br>Output<br>Code | <b>S1.1: National Society capacity building and organizational development objectives are facilitated to ensure that National Societies have the necessary legal, ethical and financial foundations, systems and structures, competences and capacities to plan and perform.</b> | Please include an indicator from the Key Data Sheet with a target<br><b>TBD</b> |   |   |   |   |   |   |   |   |    |    |    |    |    |    |    |
|                       | <b>Output S1.1.4: National Societies have effective and motivated volunteers who are protected</b>                                                                                                                                                                               | Please include an indicator from the Key Data Sheet with a target<br><b>TBD</b> |   |   |   |   |   |   |   |   |    |    |    |    |    |    |    |
|                       | Activities planned<br>Week                                                                                                                                                                                                                                                       | 1                                                                               | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 |
| AP040                 | Ensure that volunteers are insured                                                                                                                                                                                                                                               |                                                                                 |   | X | X | X | X | X | X | X | X  | X  | X  |    |    |    |    |
| AP040                 | Provide complete briefings on volunteers' roles and the risks they face                                                                                                                                                                                                          | X                                                                               | X | X | X | X | X | X | X | X | X  | X  | X  |    |    |    |    |
| AP040                 | Ensure volunteers are aware of their rights and responsibilities                                                                                                                                                                                                                 | X                                                                               | X | X | X | X | X | X | X | X | X  | X  | X  |    |    |    |    |
| AP040                 | Ensure volunteers' safety and wellbeing                                                                                                                                                                                                                                          | X                                                                               | X | X | X | X | X | X | X | X | X  | X  | X  |    |    |    |    |
| AP040                 | Ensure volunteers are properly trained                                                                                                                                                                                                                                           | X                                                                               | X | X | X | X | X | X | X | X | X  | X  | X  |    |    |    |    |
| AP040                 | Ensure volunteers' engagement in decision-making processes of respective projects they implement                                                                                                                                                                                 | X                                                                               | X | X | X | X | X | X | X | X | X  | X  | X  |    |    |    |    |
| P&B<br>Output         | <b>Outcome S2.1: Effective and coordinated international disaster response is ensured</b>                                                                                                                                                                                        | Please include an indicator from the Key Data Sheet with a target<br><b>TBD</b> |   |   |   |   |   |   |   |   |    |    |    |    |    |    |    |

| Code                  | Output S2.1.4: Effective response preparedness and NS surge capacity mechanism is maintained                                                                                                                                               | Please include an indicator from the Key Data Sheet with a target<br>TBD |   |   |   |   |   |   |   |   |    |    |    |    |    |    |    |
|-----------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------|---|---|---|---|---|---|---|---|----|----|----|----|----|----|----|
|                       | Activities planned<br>Week                                                                                                                                                                                                                 | 1                                                                        | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 |
| AP050                 | Common running services for operational centers                                                                                                                                                                                            | X                                                                        | X | X | X | X | X | X | X | X | X  | X  | X  |    |    |    |    |
| P&B<br>Output<br>Code | Outcome S3.1: The IFRC secretariat, together with National Societies uses their unique position to influence decisions at local, national and international levels that affect the most vulnerable.                                        | Please include an indicator from the Key Data Sheet with a target<br>TBD |   |   |   |   |   |   |   |   |    |    |    |    |    |    |    |
|                       | Output S3.1.1: IFRC and NS are visible, trusted and effective advocates on humanitarian issues                                                                                                                                             | Please include an indicator from the Key Data Sheet with a target<br>TBD |   |   |   |   |   |   |   |   |    |    |    |    |    |    |    |
|                       | Activities planned<br>Week                                                                                                                                                                                                                 | 1                                                                        | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 |
| AP053                 | Communication work                                                                                                                                                                                                                         | X                                                                        | X | X | X | X | X | X | X | X | X  | X  | X  |    |    |    |    |
| P&B<br>Output<br>Code | Output S3.1.2: IFRC produces high-quality research and evaluation that informs advocacy, resource mobilization and programming.                                                                                                            | Please include an indicator from the Key Data Sheet with a target<br>TBD |   |   |   |   |   |   |   |   |    |    |    |    |    |    |    |
|                       | Activities planned<br>Week                                                                                                                                                                                                                 | 1                                                                        | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 |
| AP055                 | Final DREF review and lessons learned workshop                                                                                                                                                                                             |                                                                          |   |   |   |   |   |   |   |   |    |    |    |    |    | X  | X  |
| P&B<br>Output<br>Code | Outcome S3.2.4: The IFRC enhances its effectiveness, credibility and accountability                                                                                                                                                        | Please include an indicator from the Key Data Sheet with a target<br>TBD |   |   |   |   |   |   |   |   |    |    |    |    |    |    |    |
|                       | Output S3.2.4: Financial resources are safeguarded; quality financial and administrative support is provided contributing to efficient operations and ensuring effective use of assets; timely quality financial reporting to stakeholders | Please include an indicator from the Key Data Sheet with a target<br>TBD |   |   |   |   |   |   |   |   |    |    |    |    |    |    |    |
|                       | Activities planned<br>Week                                                                                                                                                                                                                 | 1                                                                        | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 |
| AP064                 | Finance work                                                                                                                                                                                                                               | X                                                                        | X | X | X | X | X | X | X | X | X  | X  | X  |    |    |    |    |
| AP065                 | Administration work                                                                                                                                                                                                                        | X                                                                        | X | X | X | X | X | X | X | X | X  | X  | X  |    |    |    |    |

## Budget

The overall amount required for this operation is CHF 490,443 as detailed below.

DREF OPERATION

APPEAL CODE - TUNISIA - FLASH FLOODS


04/10/2020

Budget by Resource

| Budget Group                         | Budget  |
|--------------------------------------|---------|
| Clothing & Textiles                  | 140.000 |
| Food                                 | 24.000  |
| Water, Sanitation & Hygiene          | 201.100 |
| Relief items, Construction, Supplies | 365.100 |
| Storage                              | 9.000   |
| Transport & Vehicles Costs           | 10.500  |
| Logistics, Transport & Storage       | 19.500  |
| National Society Staff               | 16.200  |
| Volunteers                           | 39.500  |
| Personnel                            | 55.700  |
| Workshops & Training                 | 7.610   |
| Workshops & Training                 | 7.610   |
| Travel                               | 3.000   |
| Office Costs                         | 7.500   |
| Communications                       | 2.100   |
| General Expenditure                  | 12.600  |
| DIRECT COSTS                         | 460.510 |
| INDIRECT COSTS                       | 29.933  |
| TOTAL BUDGET                         | 490.443 |

Budget by Area of Intervention

|       |                                                |         |
|-------|------------------------------------------------|---------|
| AOF1  | Disaster Risk Reduction                        |         |
| AOF2  | Shelter                                        | 149.100 |
| AOF3  | Livelihoods and Basic Needs                    | 25.560  |
| AOF4  | Health                                         | 12.780  |
| AOF5  | Water, Sanitation and Hygiene                  | 214.172 |
| AOF6  | Protection, Gender and Inclusion               |         |
| AOF7  | Migration                                      |         |
| SFI1  | Strengthen National Societies                  | 54.528  |
| SFI2  | Effective International Disaster Management    | 21.087  |
| SFI3  | Influence others as leading strategic partners | 8.424   |
| SFI4  | Ensure a strong IFRC                           | 4.793   |
| TOTAL |                                                | 490.443 |

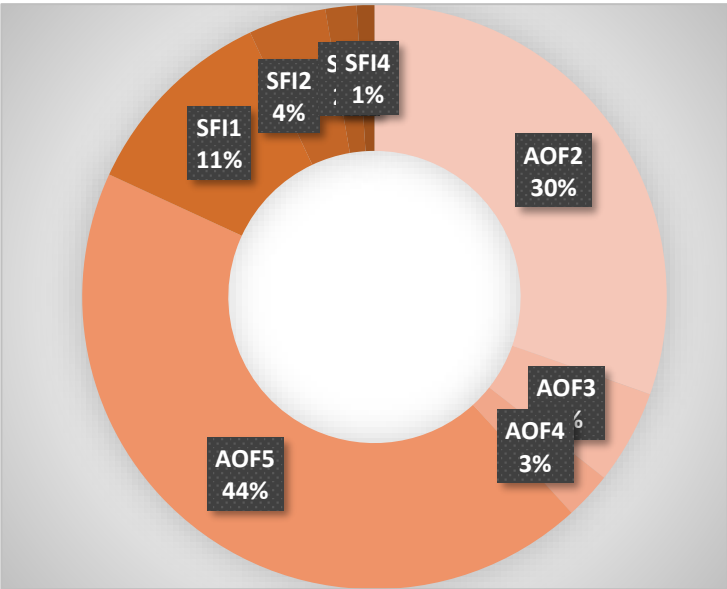




**+C IFRC**

22 September 2020  
MDRTN009  
FF-2020-000204-TUN



## Tunisia - Flash Floods Disaster Relief Emergency Funds

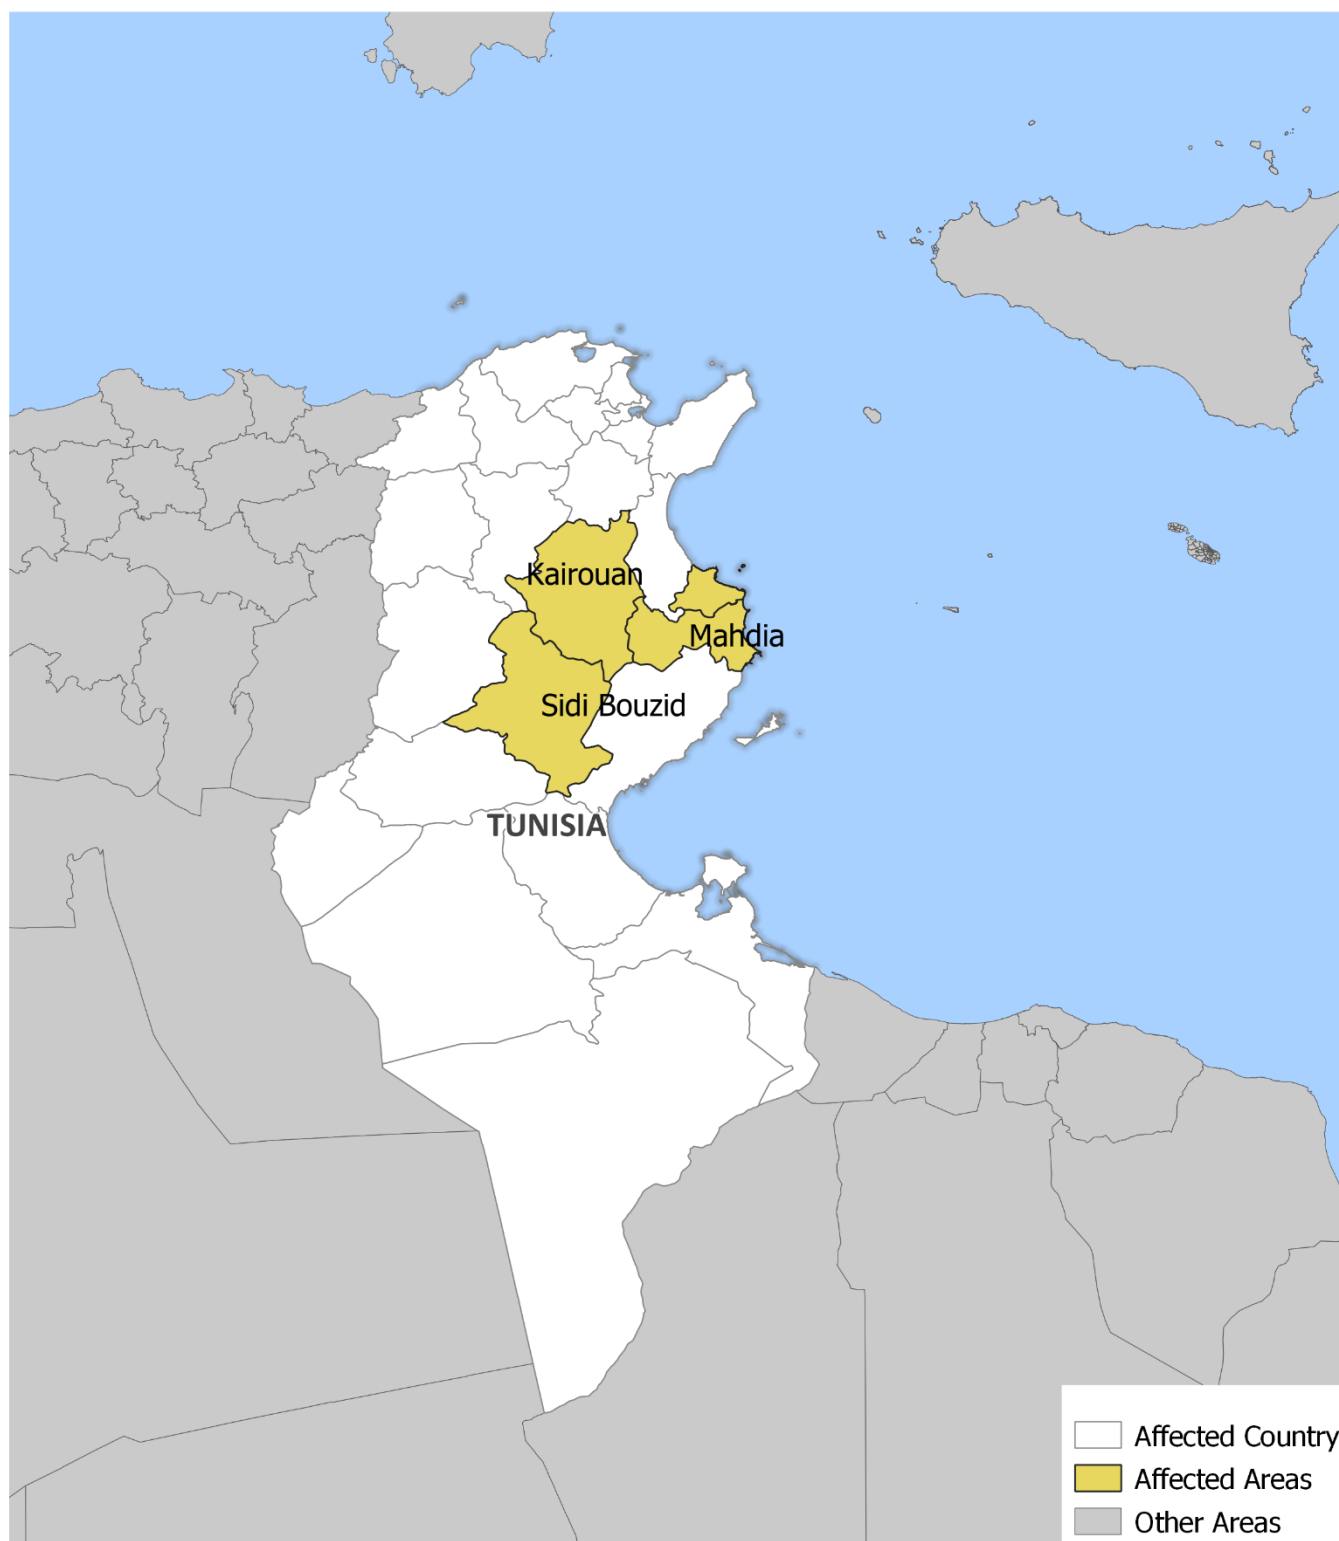

The maps used do not imply the expression of any opinion on the part of the International Federation of Red Cross and Red Crescent Societies or National Societies concerning the legal status of a territory or of its authorities.

0 0.0005 0.001 0.0015 0.002



## Contact information

For further information, specifically related to this operation please contact:

### In the Tunisian Red Crescent Society

- President NS ; Dr. Abdellatif Chabbou, [contact@croissant-rouge.tn](mailto:contact@croissant-rouge.tn) +216 71325572
- Operational coordinator: Dr Mounir Jeliti [jelitimounir2@yahoo.fr](mailto:jelitimounir2@yahoo.fr) Fax: +216253052
- National Health and disaster responsible: Mr Ridha Ameur [ridha-ameur@hotmail.com](mailto:ridha-ameur@hotmail.com) +21698319968

### In the IFRC

- **IFRC North Africa office:** Dr. Iliana Mourad, Head of Country Cluster; phone: +216 58 51 08 07; email: [iliana.mourad@ifrc.org](mailto:iliana.mourad@ifrc.org)
- **IFRC Regional Office:** Dr. Hosam Faysal, Head of Disaster and Crisis (Prevention, Response and Recovery) – MENA; phone +961 71 802 916; email: [hosam.faysal@ifrc.org](mailto:hosam.faysal@ifrc.org)

### For IFRC Resource Mobilization and Pledges support:

- **IFRC Regional Office:** Anca Zaharia, MENA Regional Head of Partnership and Resource Development, phone: +961 813 11 918; email: [anca.zaharia@ifrc.org](mailto:anca.zaharia@ifrc.org)

### For In-Kind donations and Mobilization table support:

- **IFRC Regional Office:** Dharmin Thacker, Acting Head of Logistics, Procurement and Supply Chain Management, phone: +961 5 428 505, email: [dharmin.thacker@ifrc.org](mailto:dharmin.thacker@ifrc.org)

### For Performance and Accountability support (planning, monitoring, evaluation and reporting enquiries)

**IFRC MENA Regional Office, Beirut:** Nadine Haddad, Regional PMER Manager, phone: +961 71 802 775; email: [nadine.haddad@ifrc.org](mailto:nadine.haddad@ifrc.org)

## How we work

All IFRC assistance seeks to adhere to the Code of Conduct for the International Red Cross and Red Crescent Movement and Non-Governmental Organizations (NGOs) in Disaster Relief and the Humanitarian Charter and Minimum Standards in Humanitarian Response (Sphere) in delivering assistance to the most vulnerable. The IFRC's vision is to inspire, encourage, facilitate and promote at all times all forms of humanitarian activities by National Societies, with a view to preventing and alleviating human suffering, and thereby contributing to the maintenance and promotion of human dignity and peace in the world.

[www.ifrc.org](http://www.ifrc.org)

Saving lives, changing minds.



The IFRC's work is guided by Strategy 2020 which puts forward three strategic aims:

1. Save lives, protect livelihoods, and strengthen recovery from disaster and crises.
2. Enable healthy and safe living.
3. Promote social inclusion and a culture of non-violence and peace
